

TECHNICAL PROPOSAL, April 2025



PROPOSAL FOR WEB DEVELOPER CONSULTANT

BIDDER'S IDENTITY

Name: MK Business Analysis (MK BA)

Areas of intervention: Software Engineering – Website Development, Redesign/Improvement and Maintenance – IT Strategy Development – Digital Marketing - Hardware and Infrastructure – Information Systems Audits – Data Analytics – Information Security – FinTech – Monitoring and Evaluation

Headquarters: Yassa – Douala Cameroon

Website: <https://mk-business-analysis.com>

Contact Person: Joel KUATE

Phone Number: +237 670 60 42 15

Email addresses: info@mk-business-analysis.com/joel.kuate@mk-groupe.com

CONTENTS

<u>II.</u>	<u>ABOUT MK BA.....</u>	<u>6</u>
II.1	COMPANY DESCRIPTION.....	6
II.2	SERVICES OFFERED.....	6
II.3	INDUSTRIES SERVED	7
II.4	SOLUTIONS LANDSCAPE	7
II.5	MK Gov : OUR E-GOVERNANCE SOFTWARE SUITE.....	8
II.6	RELEVANT EXPERTISE	13
II.6.1	EXPERIENCE IN DESIGNING, DEVELOPING AND DEPLOYING DIGITAL PLATFORMS	13
II.6.2	SCREENSHOTS OF FEW SOLUTIONS	18
II.6.3	CERTIFICATE OF GOOD PERFORMANCE/PAST CONTRACTS.....	29
II.7	QUALITY CONTROL SYSTEM.....	31
II.7.1	THREE-TIER QUALITY ASSURANCE FRAMEWORK	31
II.7.2	QUALITY TOOLS AND METHODOLOGIES	31
II.8	WHY CHOOSE MK BA?	32
II.9	ADMINISTRATIVE DOCUMENTS	37
<u>III.</u>	<u>GENERAL PROJECT FRAMEWORK.....</u>	<u>39</u>
III.1	EXECUTIVE SUMMARY.....	39
III.2	BACKGROUND	39
III.3	PROJECT OBJECTIVES.....	40
III.3.1	GLOBAL OBJECTIVE	40
III.3.2	SPECIFIC OBJECTIVES.....	40
III.4	DELIVERABLES AND EXPECTED RESULTS	41
III.5	LOCATION	44
III.5.1	OPERATIONAL SETUP	44
III.5.2	TIME ZONE ADVANTAGE	44
III.5.3	REMOTE COLLABORATION FRAMEWORK.....	44
III.5.4	QUALITY ASSURANCE PROCESS.....	44
III.5.5	CONTINGENCY PLANNING	44
<u>IV.</u>	<u>IMPLEMENTATION METHODOLOGY</u>	<u>45</u>
IV.1	PHASE 1: INCEPTION AND DISCOVERY	46
IV.2	PHASE 2: DESIGN	49
IV.3	PHASE 3: DEVELOPMENT.....	54
IV.4	PHASE 4: DEPLOYMENT AND LAUNCH.....	58
IV.5	PHASE 5: CLOSURE.....	62
<u>V.</u>	<u>PROJECT TEAM AND SCHEDULE.....</u>	<u>65</u>
V.1	PROJECT TEAM.....	65
V.2	PROJECT ORGANIZATION CHART	68
V.3	PROJECT SCHEDULE.....	69

V.3.1	RESOURCE ALLOCATION MATRIX	70
V.3.1	KEY MILESTONES	71
<u>VI.</u>	<u>EXPERTS CVS</u>	<u>72</u>
VI.1	CV OF THE PROJECT MANAGER	72
VI.2	CV OF THE UX ENGINEER	83
VI.3	CV OF THE ANALYST	86
VI.4	CV OF THE FULL STACK DEVELOPER N°1	93
VI.5	CV OF THE FULL STACK DEVELOPER N°2	98
VI.6	CV OF THE TEST ENGINEER	105
<u>VII.</u>	<u>ANNEXES</u>	<u>108</u>

I. TENDER SUBMISSION LETTER

To :

The Procurement Unit of NetHope

Subject : Submission of Proposal for Web Developer Consultant

We, the undersigned, are pleased to submit our complete proposal for the Web Developer Consultant position as detailed in your Request for Proposal dated March 24, 2025. Having carefully reviewed your requirements, we are confident in our ability to enhance NetHope's online presence through comprehensive website improvements that align with your strategic communication goals.

MK BA brings 7 years of expertise in digital transformation and web development, with particular experience serving international organizations and nonprofits across multiple countries. Our team has successfully delivered more than 15 web platforms for clients including UNDP, UNICEF, and several financial institutions, implementing solutions that combine technical excellence with strategic communication objectives.

For this engagement, we have assembled a specialized team of seven professionals with extensive experience in WordPress development, UI/UX design, and nonprofit digital communications. Our team includes certified professionals in project management, information security, and web development, ensuring a comprehensive approach to your website enhancement needs.

Our recent comparable projects that demonstrate our qualifications include:

- **MK WBC (2025):** Redesign the website of the MK WBC client
- **OAG (2025):** Redesign the website of the OAG client
- **GEDYS (2025):** Development the website of the GEDYS
- **UNDP Madagascar (2024):** Development of an Environment Management Information System with interactive mapping and data visualization
- **UNDP Guinea (2023-2024):** Development of the web platform for coordination of development partners of the Republic of Guinea
- **Bange Bank Cameroon (2023-2024):** Development of the corporate website with responsive design and modern user experience as a subcontractor of the Best Group (TBG)
- **UNICEF Cameroon (as subcontractor of MK WBC):** Development of an "m-Hhealth" initiative aiming to strengthen compliance and retention in care of pregnant/breast-feeding women and adolescents living with HIV (ongoing project)
- **UNICEF Cameroon (2023-2024):** Development of an m-Health initiative with both web and mobile interfaces

Our proposal features a comprehensive migration strategy from your current Oxygen theme to a modern, performance-optimized WordPress theme, with particular attention to maintaining your visual identity while enhancing user experience. We have structured our approach around five phases: Inception and Discovery, Design, Development, Deployment and Launch, and Closure. Each phase incorporates stakeholder involvement, quality assurance, and knowledge transfer to ensure sustainable results.

In line with your request, we have included a recommendation for improving your organization's website: implementing a modular content architecture using Advanced Custom Fields (ACF) with the Astra Pro theme. This approach would enable your communications team to easily update dynamic content while maintaining design consistency, establishing a component-based page building system that remains flexible while ensuring content governance across your global network.

We are excited about the opportunity to collaborate with NetHope on this important project. Our team is available to provide any additional information or clarification you may require regarding our proposal.

Thank you for your consideration. We look forward to the possibility of working together.

Sincerely,

Joel KUATE

Technical Director, MK BA

April 04, 2025



II. ABOUT MK BA

II.1 Company description

MK Business Analysis is an Engineering and Consulting Services Company operating in Africa and offering a wide range of services in its different areas of expertise. Since 8 years now, we have been providing government, international organizations and private companies quality and world class services to improve their efficiency and enhance their growth.


II.2 Services offered

In the field of information technology and finances, we offer the following services.


- | | |
|---|---|
| <p>1 E-GOVERNANCE & DIGITAL TRANSFORMATION</p> <ul style="list-style-type: none"> • Development of regional, national and local IT strategies • E-Government software solutions • Support for private business strategic planning | <p>2 ERP & INTEGRATION</p> <ul style="list-style-type: none"> • Accounting, HR, Inventory Management – Odoo • CRM and Collaboration – Bitrix24 • Document Management System – Maarch, Alfresco • Sage (Accounting, Payroll, Sales, X3...) |
| <p>3 SOFTWARE, WEB & MOBILE DEVELOPMENT</p> <ul style="list-style-type: none"> • Feasibility studies • Specifications elicitation • Design, coding, testing, deployment, support for web and mobile applications | <p>4 INFORMATION SECURITY</p> <ul style="list-style-type: none"> • Data Privacy and Protection • Encryption and certificates • Information systems audits • Advanced Threat and Vulnerability Management • Managed Security Services • Disaster recovery and business continuity |
| <p>5 DATA MANAGEMENT</p> <ul style="list-style-type: none"> • Data governance and data quality management • Data integration (ETL), analytics and visualization • Data storage • Data migration and backup • Big data and Business intelligence • Reference and master data management | <p>6 NETWORK & SYSTEM ENGINEERING</p> <ul style="list-style-type: none"> • Network design, deployment, upgrades, troubleshooting and management • Hardware infrastructures deployment • Cloud computing – AWS and Azure • CI/CD Continuous Integration / Continuous Delivery |
| <p>7 IT OURSOURCING</p> <ul style="list-style-type: none"> • Dedicated remote and onsite development teams • Staff augmentation • Remote and on-premise network and hardware infrastructure management • Intuitive user interfaces • Data storage and backup | <p>8 IT SUPPORT</p> <ul style="list-style-type: none"> • Software and hardware maintenance • Managed IT services • Helpdesk • Capacity building |
| <p>9 FINANCIAL SERVICES</p> <ul style="list-style-type: none"> • Digital payment • Assets management • Budget management • Inclusive finance • Green finance • Intermediation | <p>10 BUSINESS FORECASTING</p> <ul style="list-style-type: none"> • Market analysis • Industry and sector-specific forecasting • Ratings |

II.3 Industries served

We serve multiple industries.


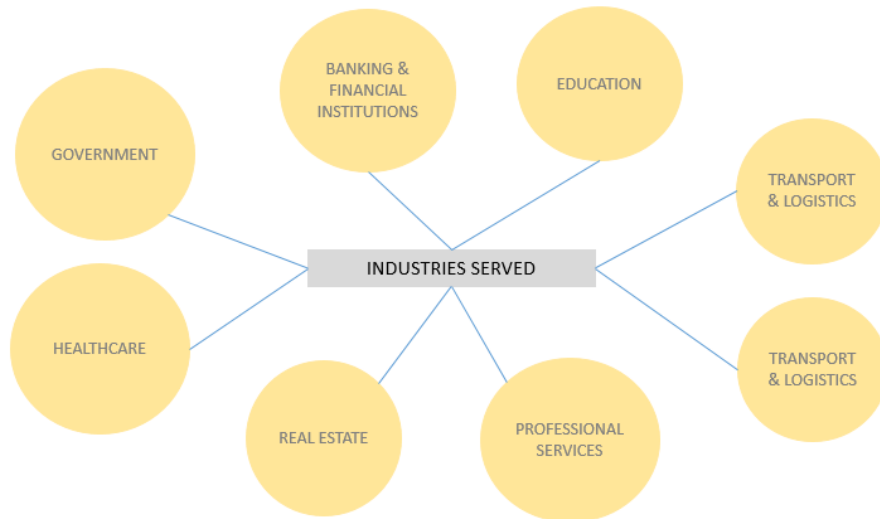




II.4 Solutions landscape


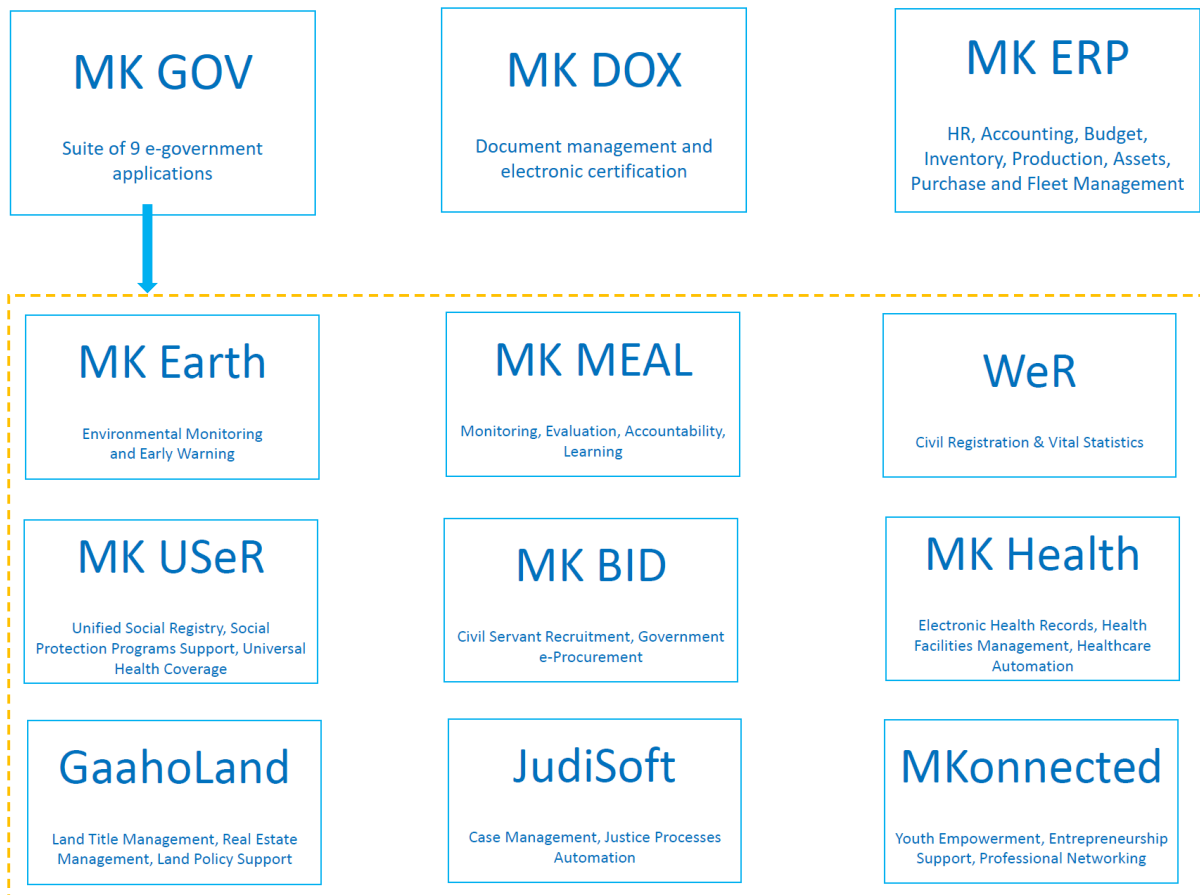




II.5 MK Gov : our E-Governance software suite


MK BA offers a suite of 10 e-Governance solutions known as MK Gov, for the use of governments and international organizations, to support public service efficiency and policy enforcement.

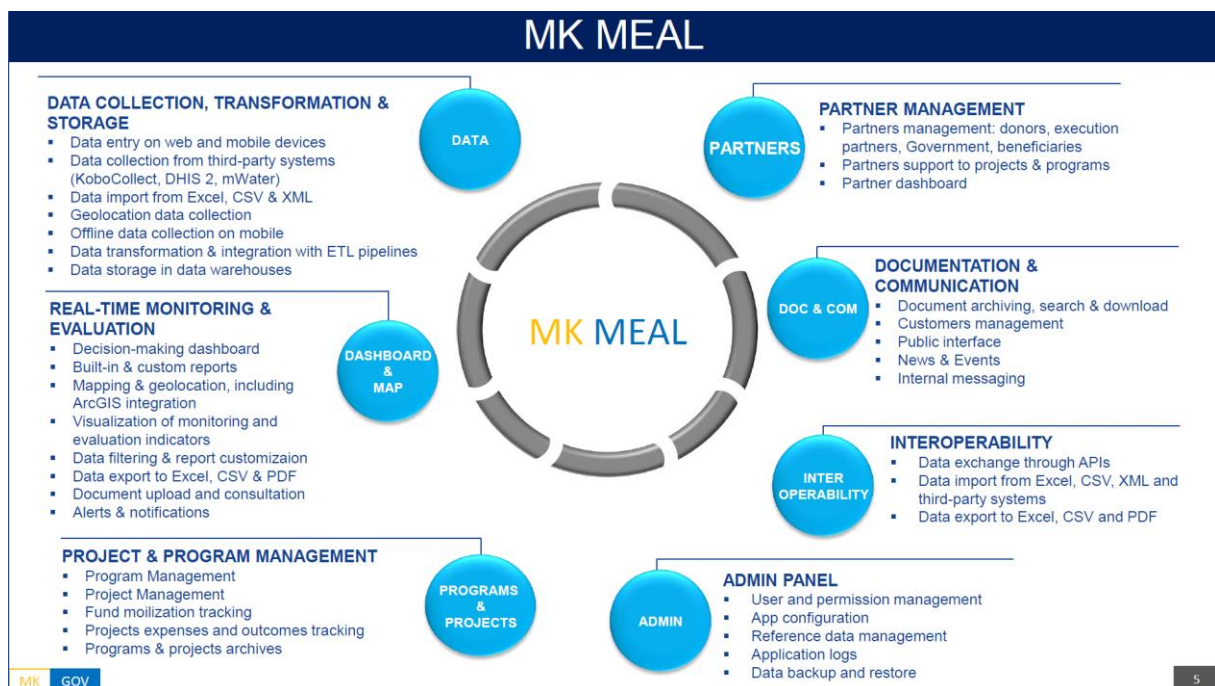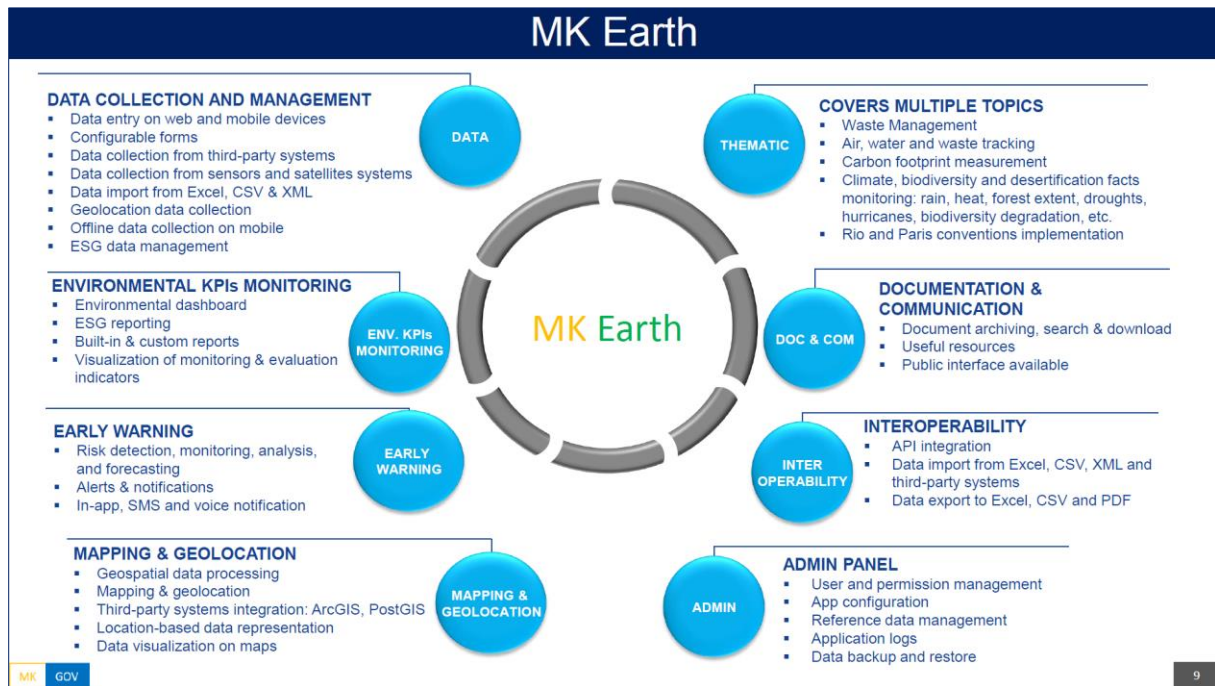

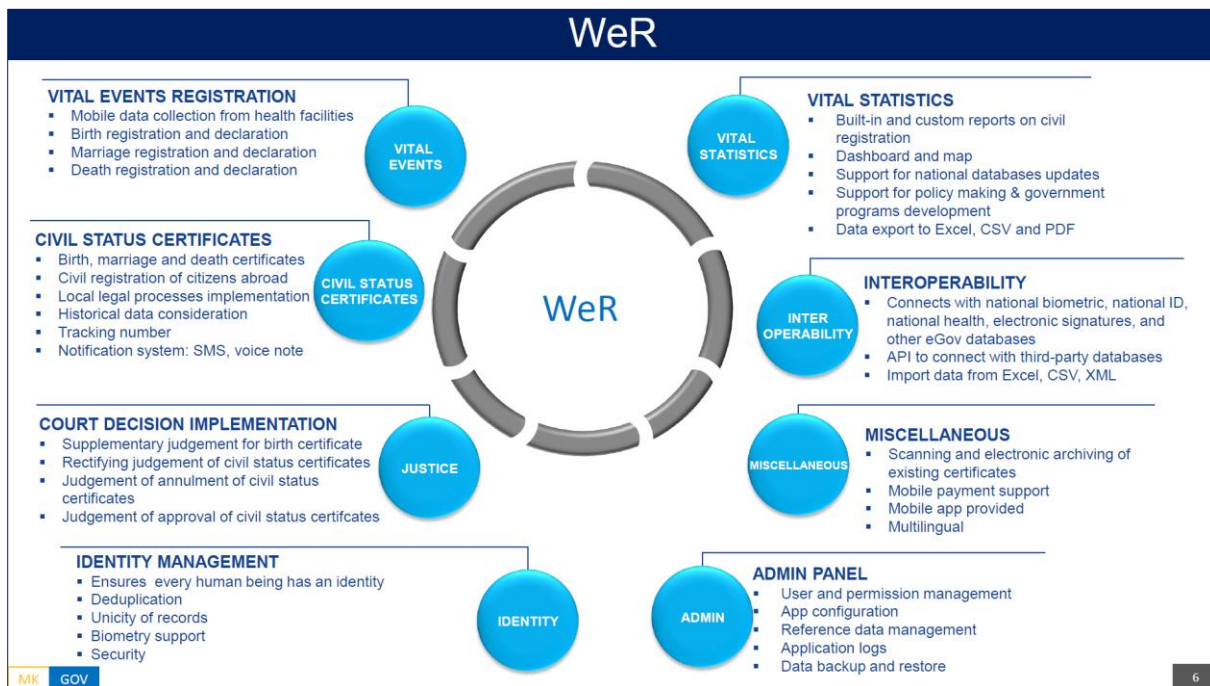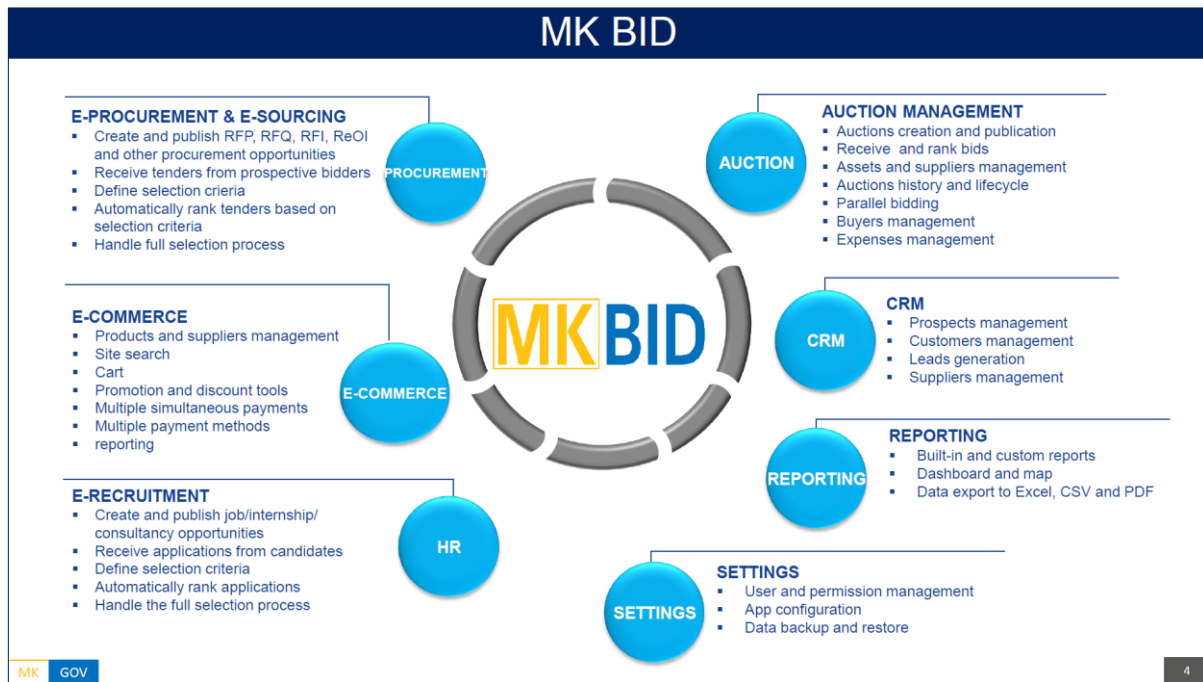


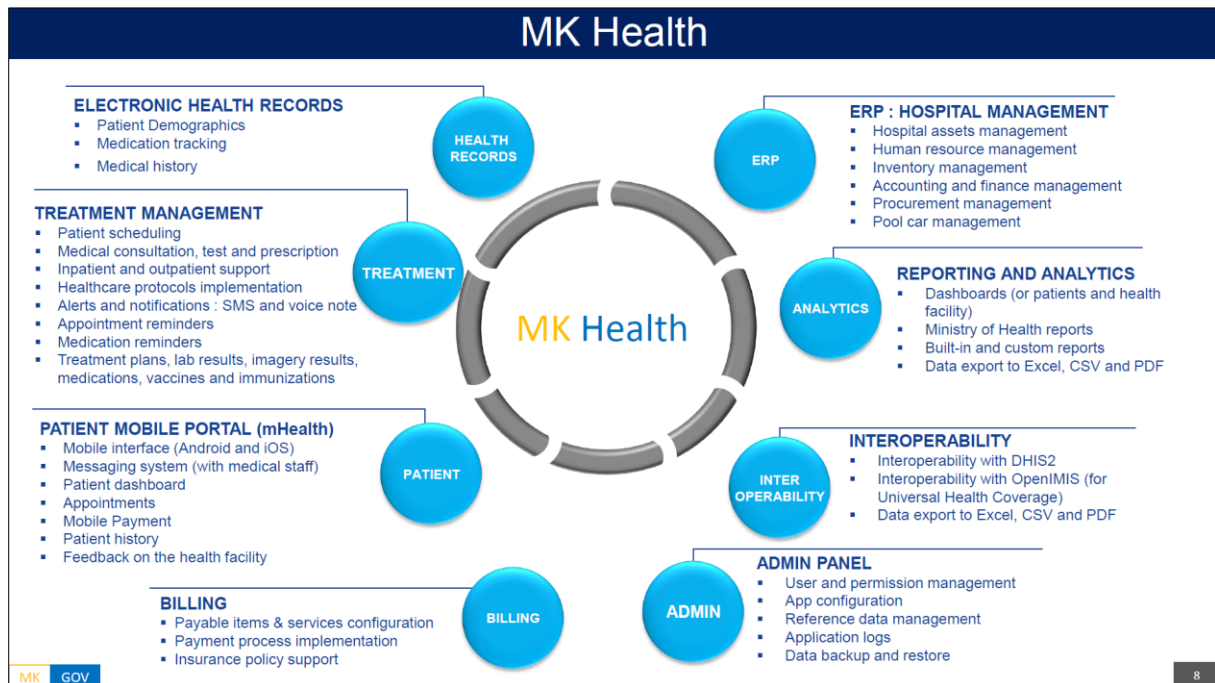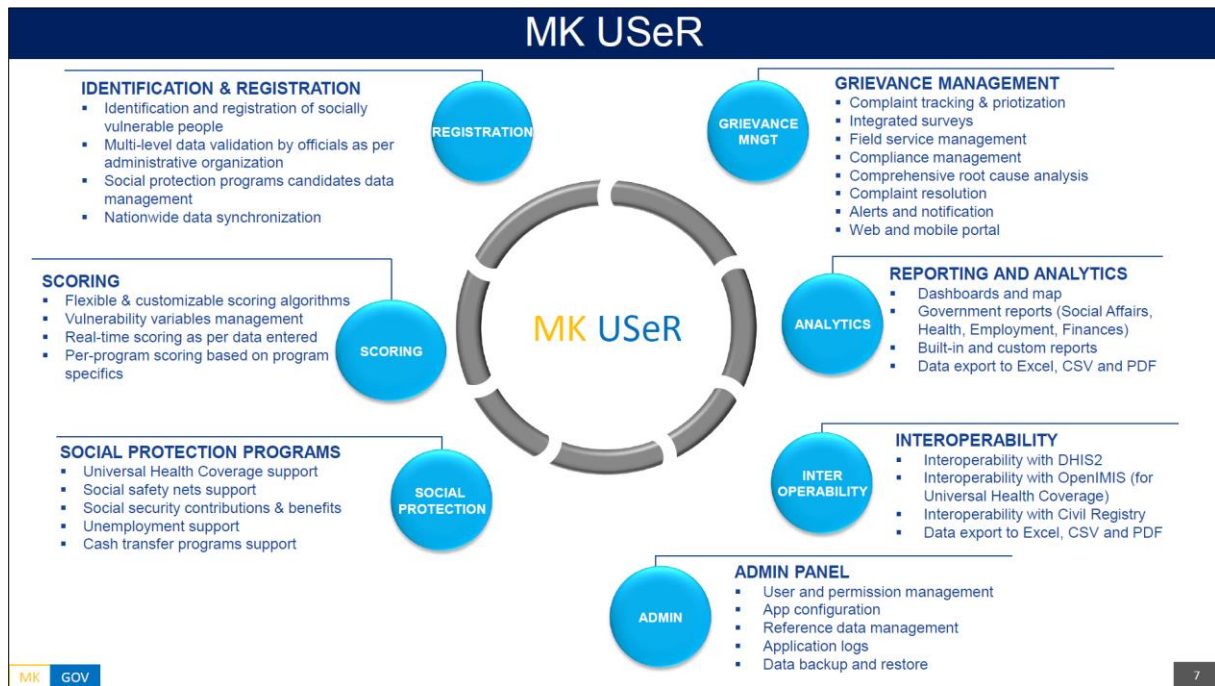

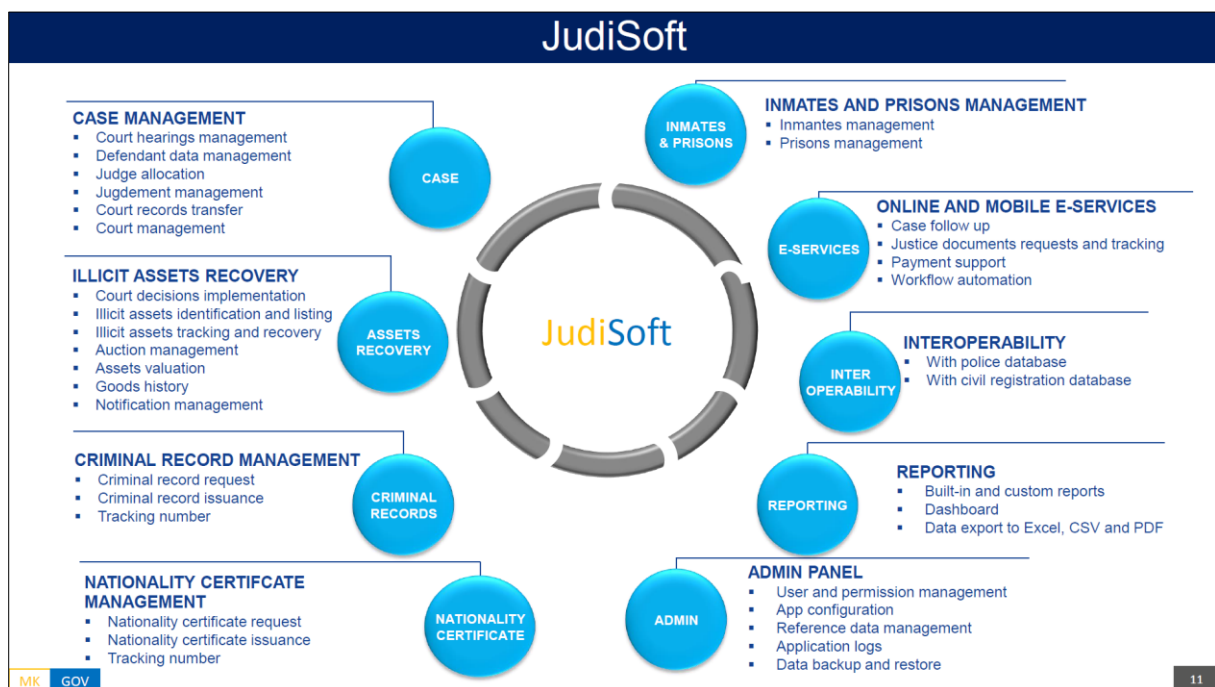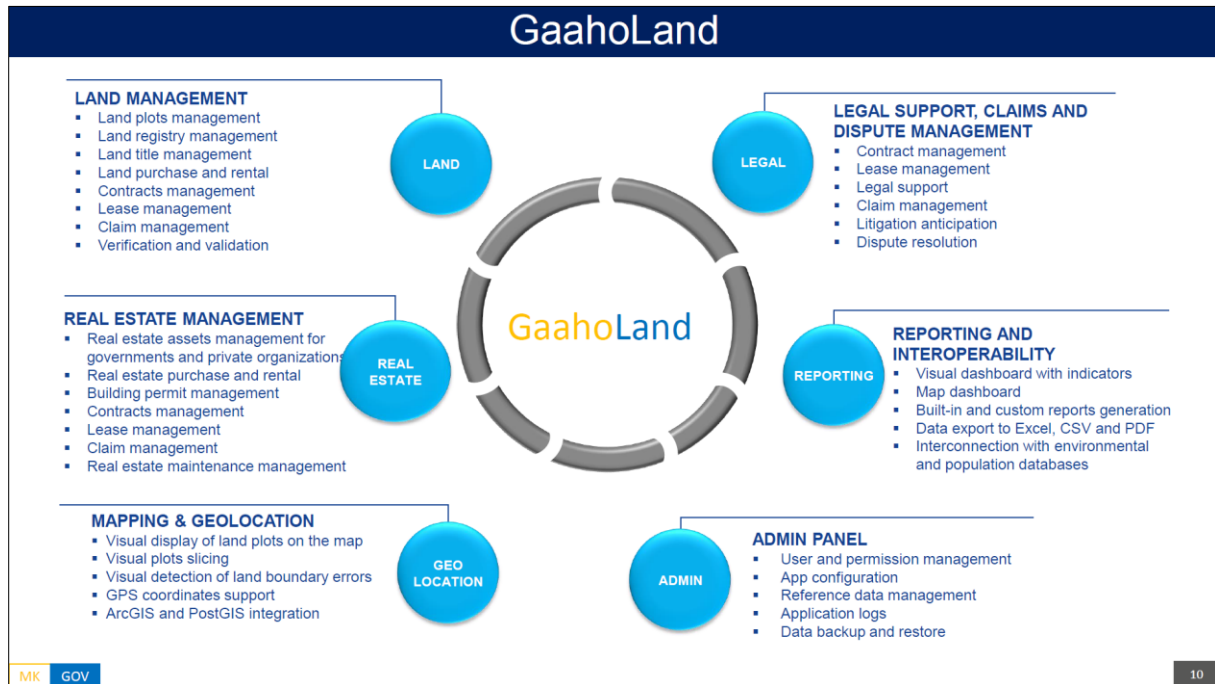

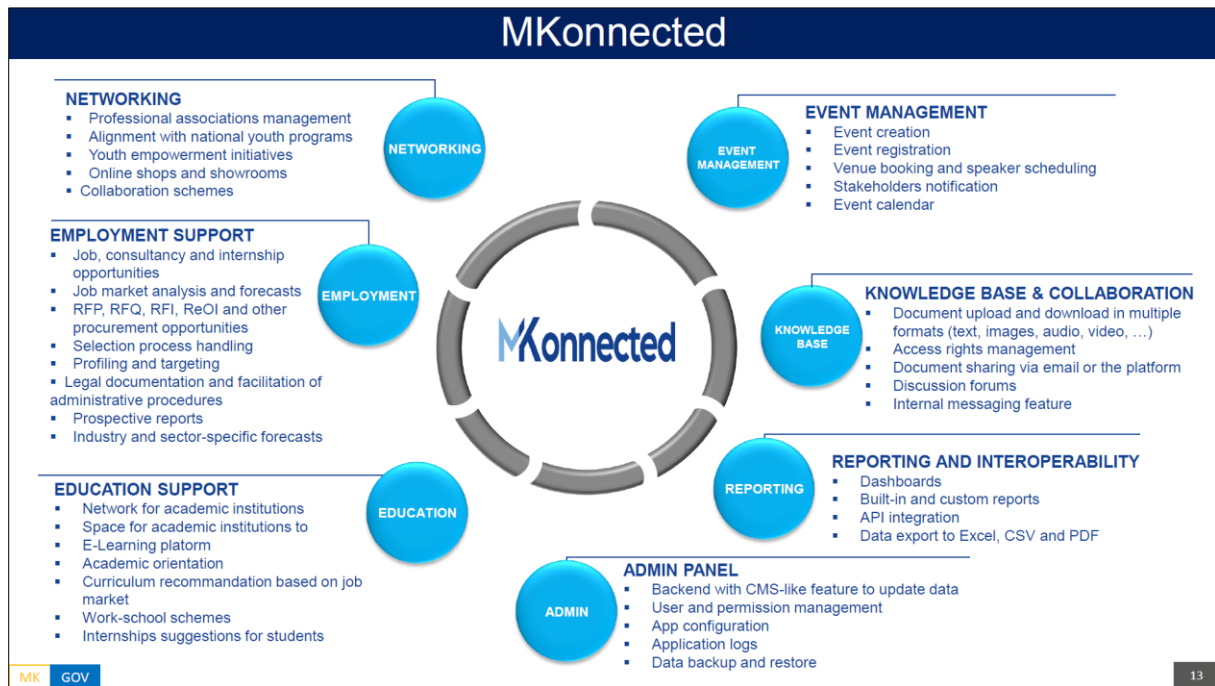

MK Gov has features of great and modern software as listed below.

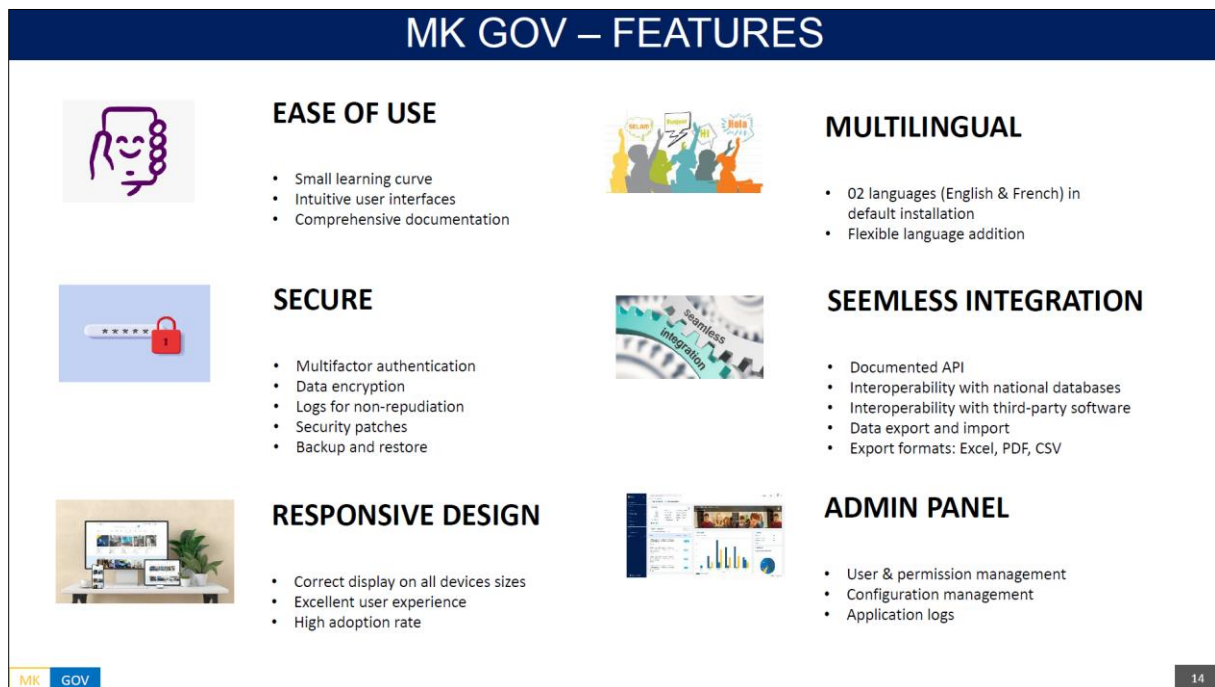

MK Gov Deployment models and licensing are described hereafter.

OUR SOLUTION MK GOV – DEPLOYMENT & LICENSING

Deployment models & Licensing



CLOUD DEPLOYMENT

- Software as a Service (SaaS) model
- No installation
- No management
- Automatic scale
- Yearly license



ON-PREMISE DEPLOYMENT

- Done on your physical or remote infrastructure
- Full control on the solution
- Lifetime license

OUR PROJECT MANAGEMENT APPROACH

- Requirements gathering
- Solution customization if applicable
- Deployment on customer infrastructure or cloud account creation
- Provide documentation
- Train end users and technical staff
- Minimum 03 months free support
- Provide for updates
- Get feedback from customer

LICENSING

- Lifetime license
 - Applicable to on-premise deployment
 - Source code transfer with documentation
 - Software ownership transferred to the customer
- Yearly license
 - Applicable to cloud deployment
 - Source code remains the property of MK
 - License to be renewed yearly

MK

GOV

15

II.6 Relevant expertise

II.6.1 Experience in designing, developing and deploying digital platforms

As a software development company, we have been providing web and mobile applications to many clients in numerous projects, including UNICEF Cameroon, UNICEF Mali, UNICEF Central African Republic, UNDP Madagascar, UNDP Guinea, French Development Agency (AFD) Cameroon. The firm also possess a web-based environmental monitoring and management platform called MK Earth which has been deployed in multiple projects involving UN agencies, and that MK BA intends to use in this mission in order to deliver the requested platform more quickly. Few projects led by the company are listed below.

Project title	Development of an Environment Management Information System
Customer information	UNDP Madagascar
	Contact : Fanomezantsoa Andrianaivoarivon fanomezantsoa.andrianaivoarivon@undp.org
Period	Jan – May 2024
Budget	91,367 USD
Description	Web platform to real time visualize environmental indicators as data is collected and updated, to document activities performed in favor of the respect by the state of Madagascar of its international commitments regarding Rio conventions on biodiversity, climate change and desertification.

The platform also monitors environmental facts and events and informs relevant stakeholders for appropriate decision making.

In this project we customized our environment monitoring solution MK Earth.

Link to the map in the public interface: <https://e-voary.mg/sige/carte>

Link to the administrative interface : <https://e-voary.mg/sige/admin/login>

Project title	HIMO 3 MINKA – Reinforced Monitoring & Evaluation and Conflict-Sensitive Analysis in the Far-North Region of Cameroon
Customer information	Agence Française de Développement – French Development Agency (MK BA was a subcontractor of Oversee Advising Group – OAG)
	Contact : Hubal PFUMTCHUM hp@myoag.org +237 699 58 84 89
Period	Nov 2020 – Jan 2022
Budget	15,360,000 XAF
Description	Online dashboard including an interactive map, for the visualization of reinforced monitoring-evaluation indicators and conflict-sensitive analysis for projects supported by AFD in the Far-North region in Cameroon

Project title	Development of Civil Registration and Vital Statistics System for Mali
Customer information	UNICEF Mali
	Contact : Alassane MAIGA alamaiga@unicef.org
Period	Since July 2025
Budget	83,017 USD
Description	Web and mobile platform to record civil status events (birth, marriage, deaths), to edit certificates related to civil registration, to calculate and visualize statistics related to civil registration.

Project title	Web platform for the coordination of development partners of the Republic of Guinea
Customer information	UNDP Guinea
	Contact : Mouna El JAOUHARI eljaouhari@un.org
Period	Sep 2023 – Mar 2024
Budget	11,212.50 USD
Description	Web platform to follow up the projects carried on by development partners (technical and financial) of the Republic of Guinea. Link: https://ptf.gov.gn

Project title	Development of the Central Registry for Freezing, Seizure and Confiscation of Illicit Assets
Customer information	UNDP Madagascar Contact: Herizo Randriamampianina herizo.randriamampianina@undp.org
Period	Since November 2024
Budget	175,392,000 MGA

Description	Web platform to record goods illegally acquired, and follow up justice decisions issues to recover those goods and penalize authors
Project title	Design and implementation of the pilot Management Information System (MIS) for the Unified Social Register in Cameroon
Customer information	UNICEF Cameroon Contact : Jean Jacques NDONGBANG jndongbang@unicef.org +237 692 55 42 75
Period	Jul 2022 – Mar 2023
Budget	9,849,000 XAF
Description	Web platform to register, validate and data of socially vulnerable people in the country, in support to the universal healthcare coverage.
Project title	Development of an ERP platform to manage purchase, budget, assets and inventory for Bange Bank Cameroon
Customer information	Bange Bank Cameroon (MK BA was a subcontractor of The Best Group) Contact : Linda MOKO linda.moko@thebest-group.com
Period	Apr – Aug 2024
Budget	6,000,000 XAF
Description	The scope of this mission is as follows: - Requirement gathering from internal departments - Development, deployment and Go live of the ERP with the modules below: - o Fixed Asset Management - o Budget Management - o Purchasing Management - o Inventory Management - o Reporting - Training of user groups (Administrators, end users, etc.) on the various modules and features of the solution
Project title	Development of the Corporate website of Bange Bank Cameroon
Customer information	Bange Bank Cameroon (MK BA was a subcontractor of The Best Group) Contact : Linda MOKO linda.moko@thebest-group.com
Period	Sep 2023 – Apr 2024
Budget	6,000,000 XAF
Description	The scope of this mission is as follows: - Requirements gathering and analysis - UI/UX design and integration (over 63 pages) - CMS pages module (Home, Who we are, Find us, Connect, Become a customer, Products, Services, Finance your cash flow, Finance your investments, Make your investments, Agency, Need help, Media, News, Photo library, Video library, Legal information, Cookie policy, Data protection and confidentiality, General conditions of sale, Pricing conditions, etc.) - Team management module

- Blog management module
- Dashboard module
- Product/service management module
- Settings and configuration management
- Notification management
- Security management
- Etc.

The design of some of the over 63 pages can also be viewed using this link:
https://drive.google.com/drive/folders/1SH05cxWmqDXU4QirzmtQZddY5NPA2hce?usp=drive_link

Website link: <https://bangecmr.com>

Project title	"Third Party Monitoring" for 52 projects funded by UNICEF in Central African Republic
Customer information	UNICEF Central African Republic (MK BA was a subcontractor of Oversee Advising Group – OAG)
	Contact : Hubal PFUMTCHUM hp@myoag.org +237 699 58 84 89
Period	Oct 2020 – Mar 2021
Budget	8,500,000 XAF
Description	Online data visualization showing real-time updated monitoring and evaluation indicator for funded projects.

Project title	Gaaho Immobilier – Web and mobile platform for real estate management
Customer information	MK WBC
	Contact : Lionnel KAMGA lionnel.kamga@mk-wbc.com +237 690 755 586
Period	2018 – 2020
Budget	13,400,000 XAF
Description	Real estate management software (web and mobile) developed and sold by the company. Link: https://gaahoimmo.com/

Project title	MyExpertise
Customer information	Oversee Advising Group (MK BA was the subcontractor of MK WBC) Contact : Hubal PFUMTCHUM hp@myoag.org +237 699 58 84 89
Period	Oct 2020 – Mar 2021
Budget	9,100,000 XAF
Description	Project Management web platform to follow the execution of humanitarian missions Link : https://myoagexpert.org/



Project title	Redesign of MK WBC corporate website
Customer information	MK WBC
	Contact : Lionnel KAMGA lionnel.kamga@mk-wbc.com +237690755586
Period	Jan – Feb 2025
Budget	1,000,000 XAF
Description	Website showcasing the expertise of the company. Link: https://mk-wbc.com/

Project title	Development of GEDYS website
Customer information	MK WBC
	Contact : Lionnel KAMGA lionnel.kamga@mk-wbc.com +237690755586
Period	Feb – Mar 2025
Budget	1,000,000 XAF
Description	Website of the think-tank named GEDYS. To be hosted online during March 2025.

Project title	OAG website
Customer information	Oversee Advising Group
	Contact : Hubal PFUMTCHUM hp@myoag.org +237 699 58 84 89
Period	Jan – Feb 2025
Budget	1,500,000 XAF
Description	Website showcasing the expertise of the company. Link: https://myoag.org/

II.6.2 Screenshots of few solutions

UNDP Madagascar – Development of an Environment Management Information System

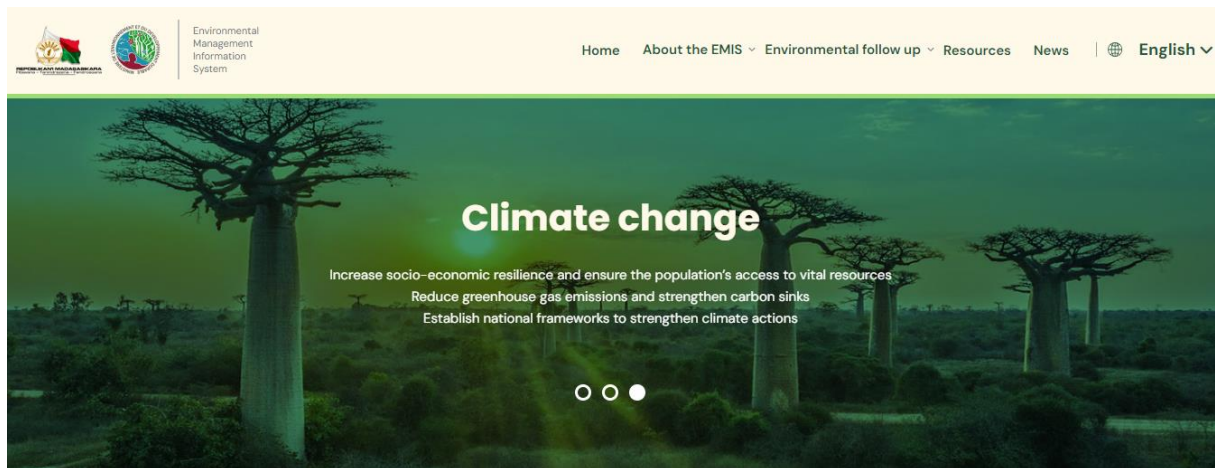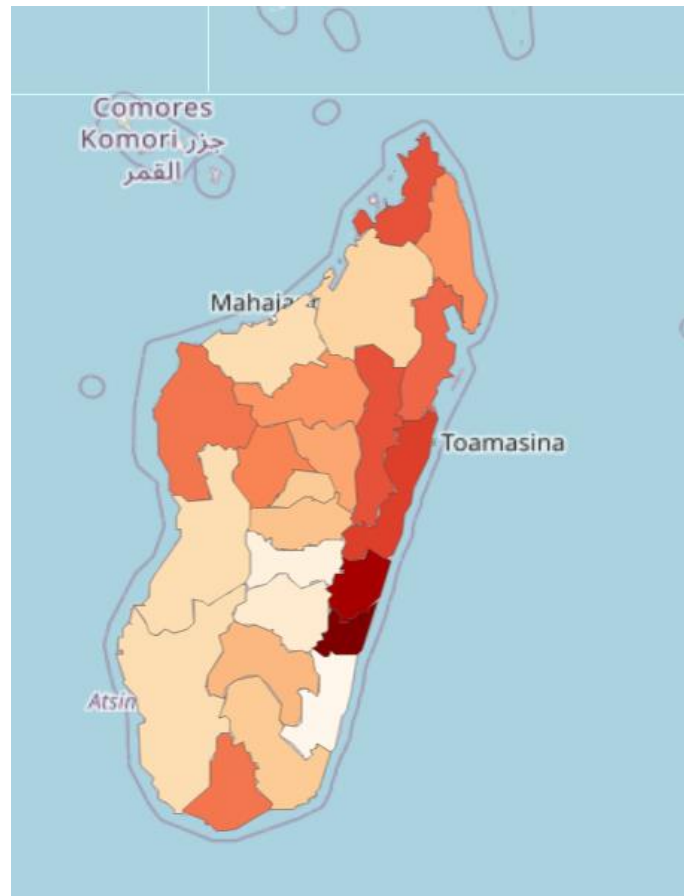


Indicators

CLIMATE CHANGE CONVENTION

BIODIVERSITY CONVENTION

CONVENTION ON DESERTIFICATION

Impacts of extreme phenomena and natural disasters on education (number of students deprived of lessons following disasters)

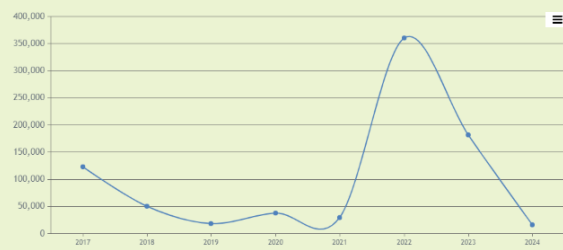


Impacts of extreme phenomena and natural disasters on education (number of students deprived of lessons following disasters)
Source :

Update date: 02-06-2024

Print data

Impacts des phénomènes extrêmes et des catastrophes naturelle sur la santé



Impacts des phénomènes extrêmes et des catastrophes naturelle sur la santé
Source : BNGRC, Ministère de la Santé

Update date: 19-06-2024

Print data



Environmental
Management
Information
System

Home About the EMIS Environmental follow up Resources News English

Funding



Biodiversity

Mobilize additional and innovative means in favor of the conservation of biodiversity.

Financing requirement : 211 000 \$ USD 16.11%
Funding obtained : 34 000 \$ USD



Climate change

Mobilize additional and innovative means to fight climate change.

Financing requirement : 225 000 \$ USD 6.67%
Funding obtained : 15 000 \$ USD



Desertification

Mobilize additional and innovative means to combat desertification.

Financing requirement : 509 000 \$ USD 14.11%
Funding obtained : 71 800 \$ USD



Environmental
Management
Information
System

Home About the EMIS Environmental follow up Resources News English

MADAGASCAR dynamic map

All regions



The total population in 2018


25 680 342

Population in 2018 by selected region

25 680 342


Total Population by region

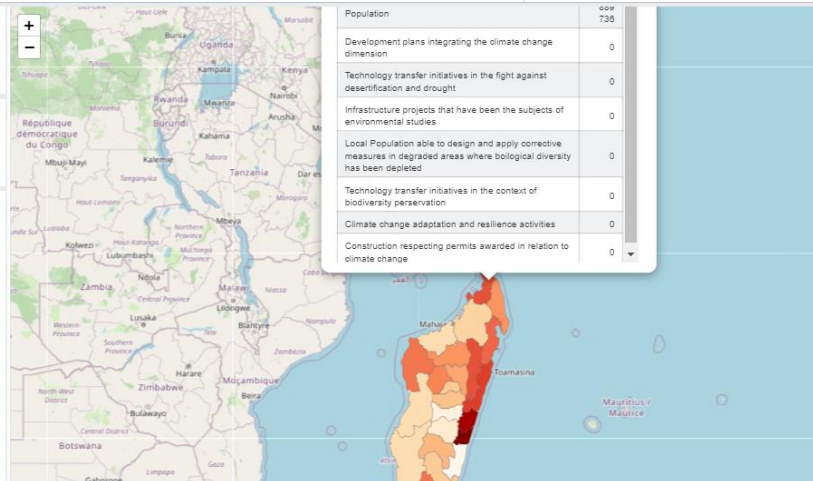

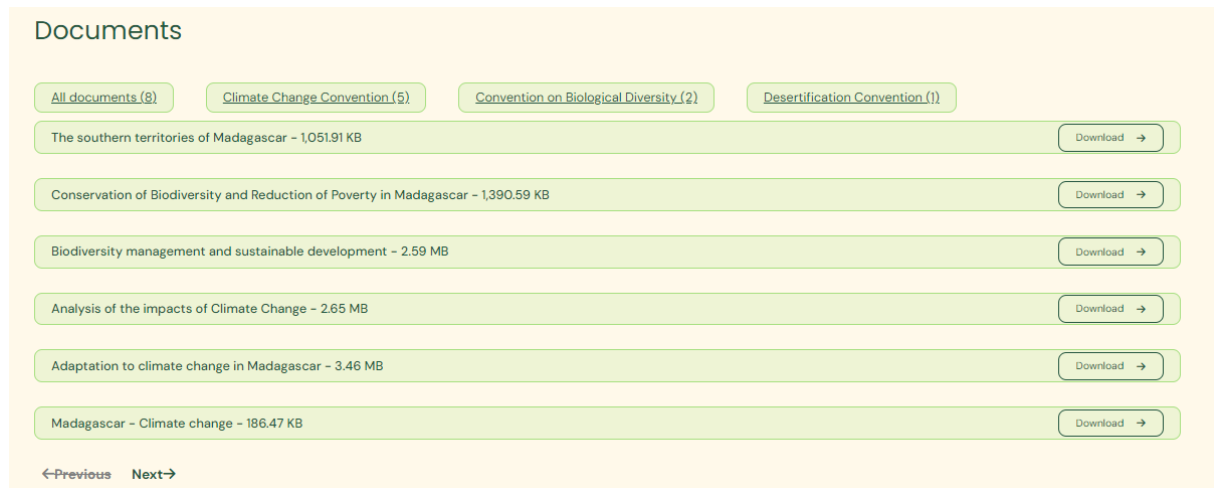


[Bange Bank Cameroon corporate website](#)


[Homepage](#)

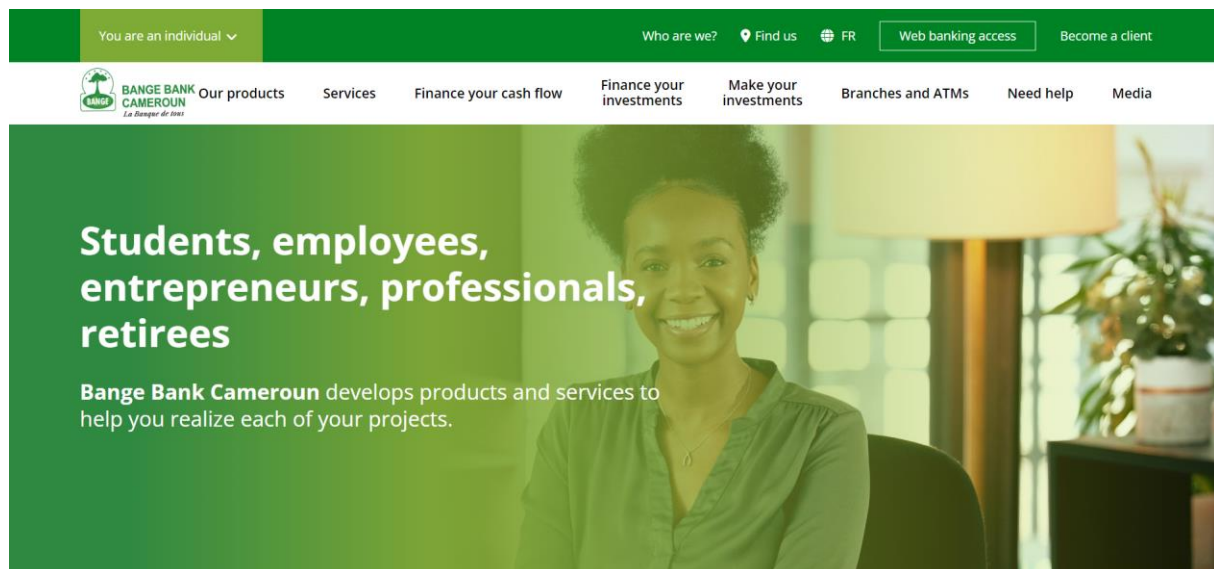

Nearest branches and ATMs

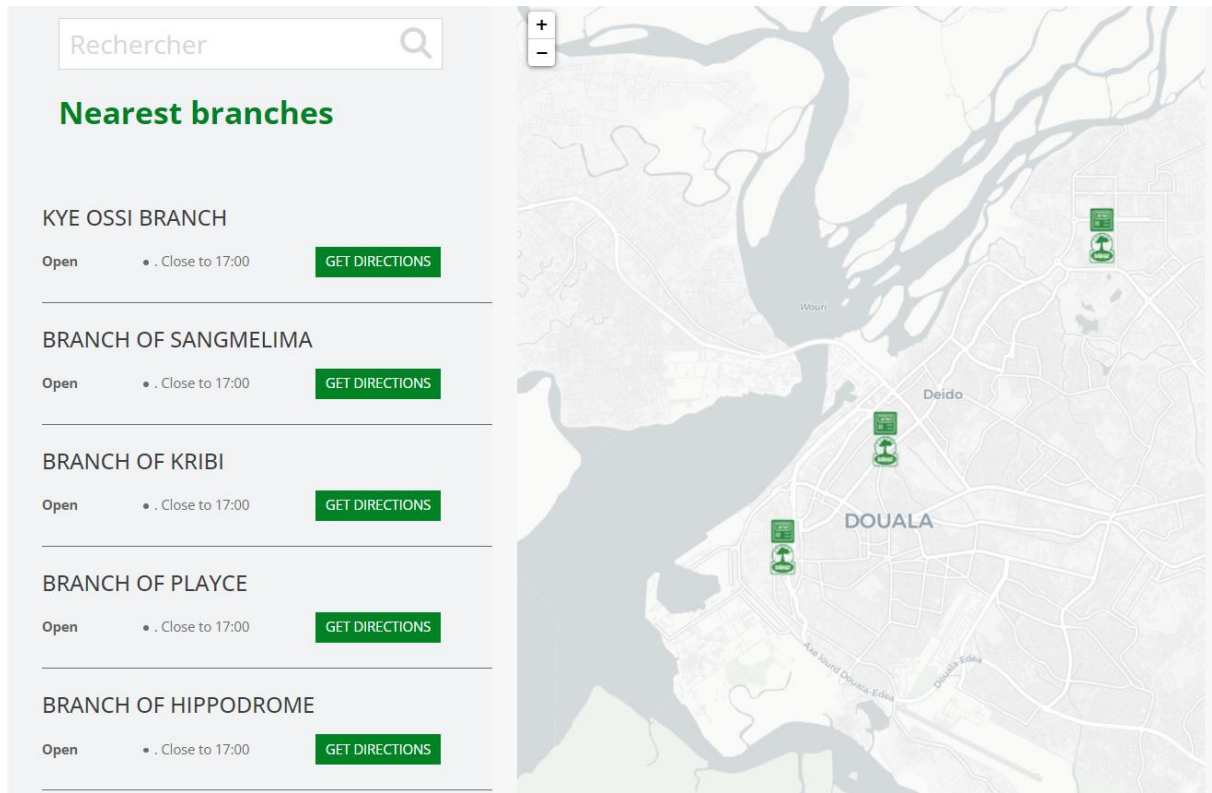

Products

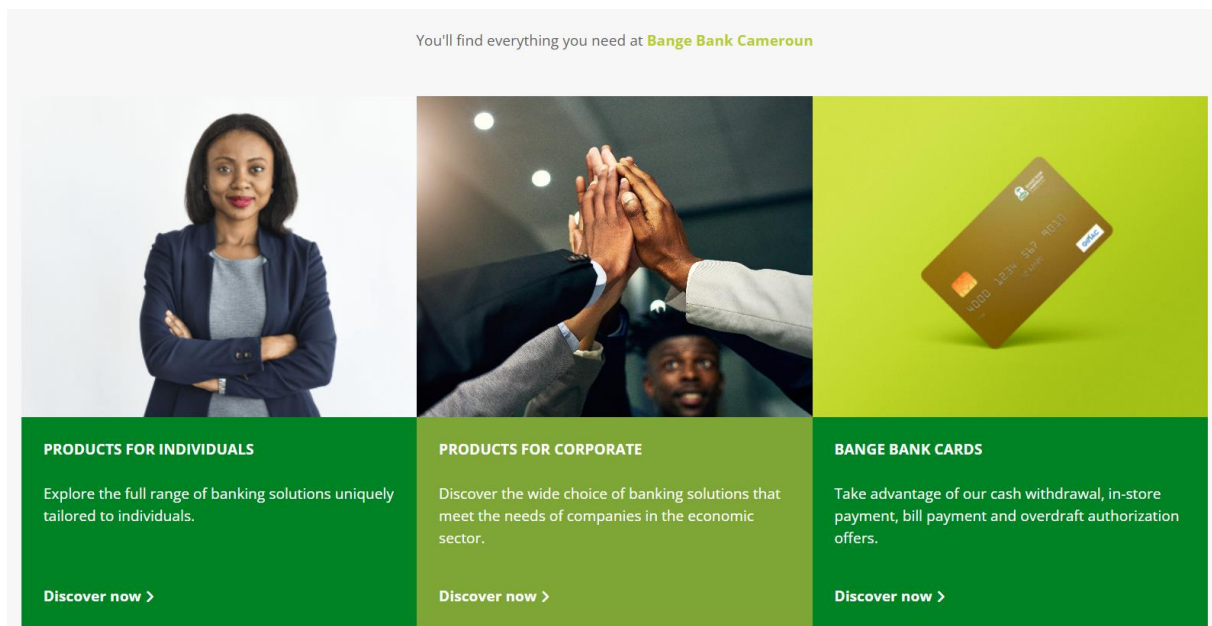

OPTIMAL CONTROL OF YOUR EXPENSES AND CASH FLOW

You can keep a constant eye on your accounts, access them online and manage financial operations remotely and securely, wherever you are.

[Learn more >](#)



EXCEPTIONAL BANKING EXPERIENCE AT BANGE BANK CAMEROUN

Take advantage of several free services included in all our bank accounts to meet your unique needs.

[Learn more >](#)



Services

What BANGE BANK CAMEROUN offers you when you subscribe to our banking services

DIVERSIFICATION POLICY

Bange Bank Cameroun offers you a multitude of services. Each of these services responds to specific needs that you encounter on a daily basis

ATTRACTIVE PRICING

Whether it's our online services or our international money transfer services, Bange Bank Cameroun has one of the most flexible rates on the market

SECURITY AND GUARANTEES

To ensure your peace of mind, our online services are regularly updated. Financial operations are meticulously controlled

Banking services available at Bange Bank Cameroun

MOBILE BANKING

With Bange Mobile, your finances are at your fingertips. Mobile application available on Play Store

[Learn more >](#)

WEB BANKING

Save time with our online banking services; accessible over the Internet via computer or cell phone

[Learn more >](#)

PAYMENTS AND TRANSFERS

We offer you the possibility of paying university fees, CNPS contributions and international transfers

[Learn more >](#)

Finance your cash flow

Are you looking for financing to expand your business?
Discover our wide range of financing solutions and find out which option best suits your specific needs

Finance your cash flow needs

Explore Bange Bank Cameroun's comprehensive range of short-term financing solutions :

[Discover now >](#)




Leasing


Preserve your cash flow while acquiring the assets you need to run your business.

[Discover now >](#)



UNICEF Central African Republic – “Third Party Monitoring” for 52 projects funded by UNICEF in Central African Republic

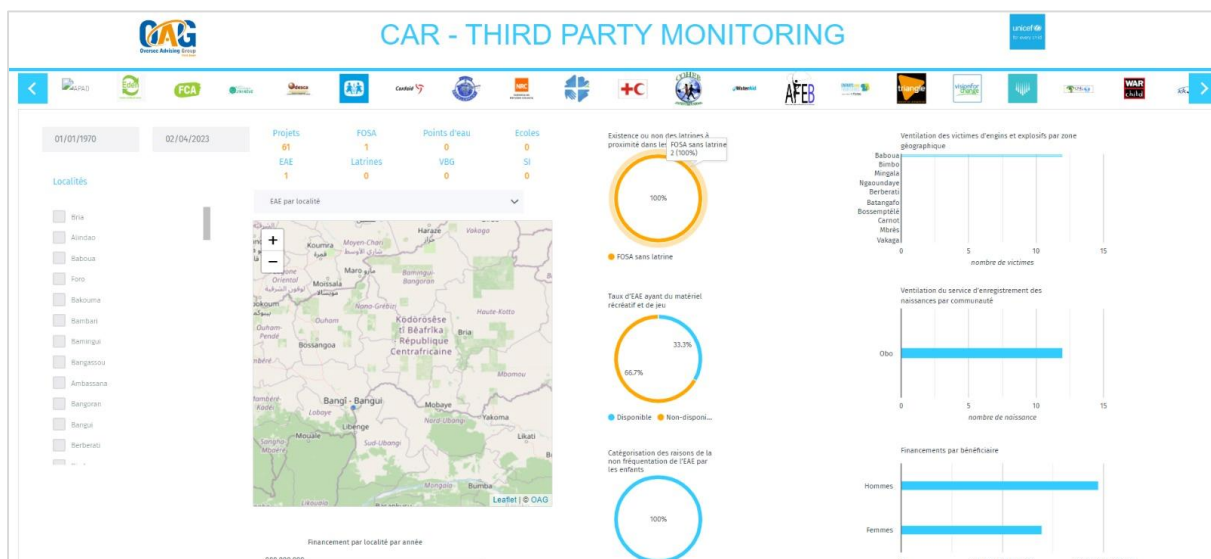

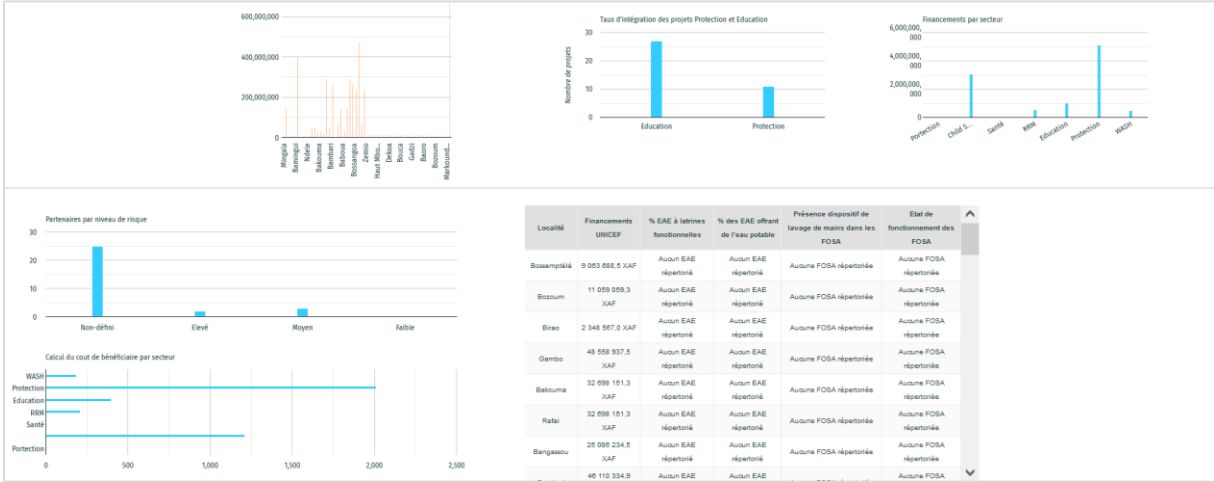

×

Que voulez-vous faire Elvis ?

Q

⌵

English

⌵

⌵

⌵

Dashbord / Mise à jour du projet: **Projet de réduction du taux de la morbi-mortalité ...**

Sauvegarder

Sauvegarder et modifier

Annuler

Projet de réduction du taux de la morbi-mortalité due à la malnutrition aigüe chez les enfants de moins de 5 ans à travers l'accès aux services de nutrition. d'eau. d'hygiène et

Input language

[EN]

Informations

Projet créé par : Elvis Presley

Date de création : Oct 20, 2022

Dernière mise à jour : Oct 20, 2022

NO de réf. du document de programme

REF21775697

Durée prévue

Date de remise du programme

Month

Day

Year

Date debut

01

02

03

Détail

Bénéficiaires

Secteurs & budgets

Localités

Activités

Suivi

Indicateurs

Pièces jointes

Indicateur	Valeur cible	Valeur référence	Valeur reportée	
Ajouter un indicateur				
- # d'enfants de 6 à 59 mois (filles et garçons) ciblés atteints de malnutrition aigüe sévère (MAS) admis dans les programmes nutritionnels thérapeutiques	0	0	0	0  
% d'enfants de 6 à 59 mois (filles et garçons) des UNTA/UNT guéris è≥75%	>/=75%	0%	0%	0%  
- % de décès <5% (filles et garçons)	<5%	0%	0%	0%  
% d'abandons 0% (filles et garçons)	0%	0%	0%	0%  

Que voulez-vous faire Elvis ?

English

Dashbord / Mise à jour du projet: Projet de réduction du taux de la morbi-mortalité ...

Sauvegarder Sauvegarder et modifier Annuler

Projet de réduction du taux de la morbi-mortalité due à la malnutrition aigüe chez les enfants de moins de 5 ans à travers l'accès aux services de nutrition, d'eau, d'hygiène et

Input language [EN]

Informations

Projet créé par : Elvis Presley

Date de création : Oct 20, 2022

Dernière mise à jour : Oct 20, 2022

NO de réf. du document de programme

REF21775697

Durée prévue

Date de remise du programme

Montl Day Year


Date debut

Détail Bénéficiaires Secteurs & budgets Localités Activités Suivi Indicateurs

Pièces jointes

Activité	Statut	Décaissement prévu	Commentaire
Ajouter une activité			
Formation de 13 agents de santé sur le PCIMA, SPC/ANJE et autres PFE (pratiques familiales essentielles) soit 1 staff/ UNTA pour 9 UNTA (1 infirmier et 1 point focal nutritionnel) et 4 stafs/UNT (1 médecin, infirmier, 1 PF nutritionnel et 1 hygiéniste	Planifiée		
Formation de 90 relais communautaires sur les thématiques de sensibilisation communautaire, le dépistage, le référencement et contre référencement des enfants mal nutris	Planifiée		
Approvisionnement de 10 FOSA (09 UNTA et 1 UNT) en intrants nutritionnels et médicaments pour la prise en charge de la MAS ainsi qu'en équipement et en	Planifiée		

French Development Agency (AFD) – Online dashboard including an interactive map, for the visualization of reinforced monitoring-evaluation indicators and conflict-sensitive analysis

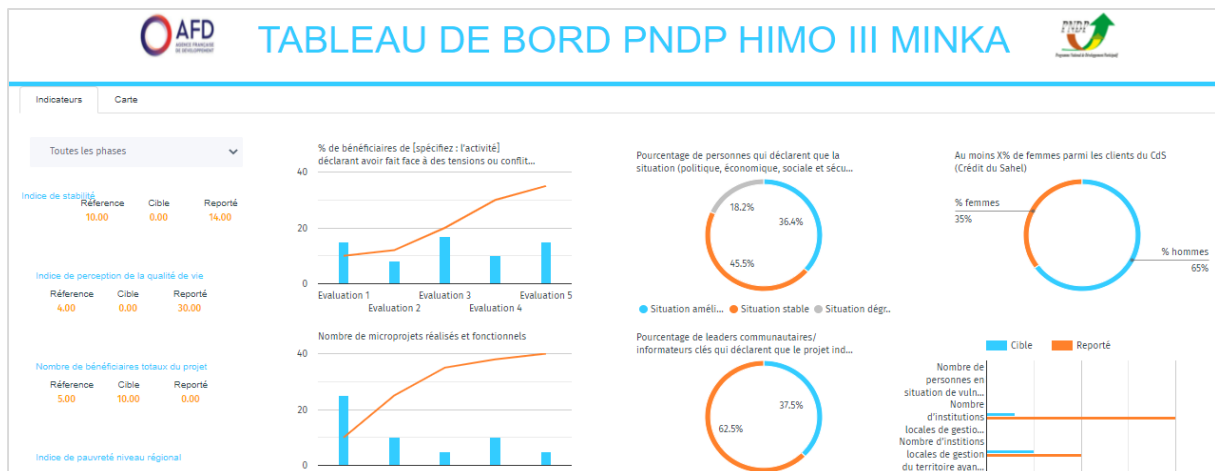




UNDP Guinea – Web platform for the coordination of development partners of the Republic of Guinea



Cartographie

Cartographie des projets soutenus par les partenaires techniques et financiers de la Guinée.

Les marqueurs représentent les préfectures, et des données agrégées des projets s'étant déroulés dans lesdites préfectures.

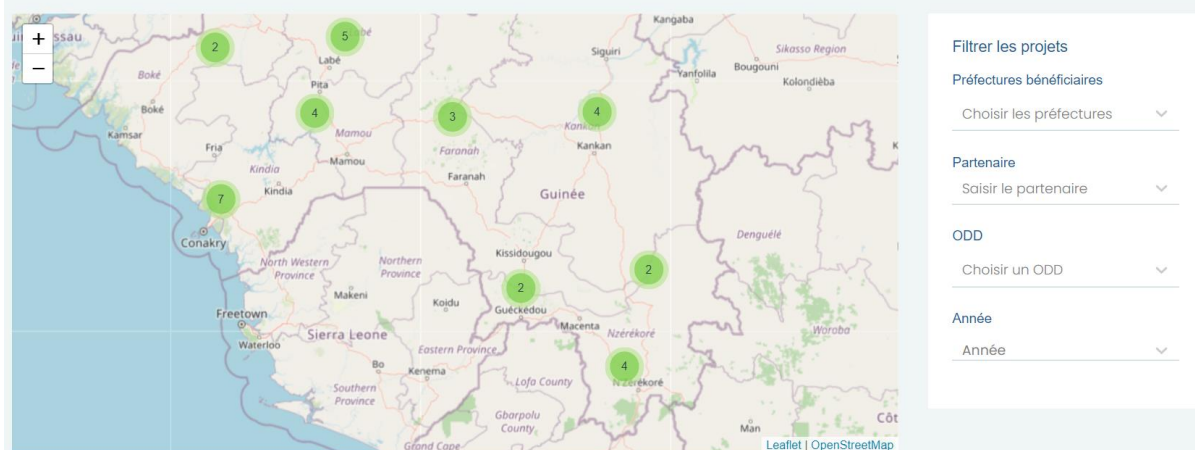

Vue tableau des projets (19)

 Excel Imprimer Imprimer

TITRE	PTF	DATES	FINAN. (USD)	PRÉFECTURES BÉNÉFICIAIRES
Tuberculose communautaire - vih prevention gin-c-plan 2021-2023/Sous récipiendaires pour la mise en œuvre de la subvention fonds mondial	Abu Dhabi Fund for Development	28/03/2024 à 31/03/2024	1 000 000	Beyla
Rural Poor Stimulus Facility 1 (RPSF 1)	FIDA	01/03/2021 à 22/06/2022	530 840	Kankan Gaoual Dabola Faranah Mali Tougué Lélouma
Project one	ALIMA	05/01/2015 à 31/03/2020	-	Boffa Conakry Coyah
CANVAC	Organisation Internationale pour les Migrations (OIM)	01/01/2022 à 31/12/2022	161 952.24	Conakry
Lecture durable et éducation à l'éco-citoyenneté dans la municipalité de Ratoma (projet coopération décentralisée)	Lay Volunteers International Association (LVIA)	01/01/2022 à 30/09/2022	55 919	Conakry

UNICEF Cameroon – Design and implementation of the pilot Management Information System (MIS) for the Unified Social Register in Cameroon

Resuc Apps Dashboard / Vue générale

Que voulez-vous faire ? Marius ?

Tableau de bord

- Nombre total de PSV** 37076
- Nombre total de ménages** 11699
- LISTES** 23

PSV 12136
Nombre total de PSV de la Commune

MÉNAGES 1793
Nombre total de PSV du ménage

LISTES 23
Nombre de Listes de ménages

Resuc Apps Dashboard / Ménages / Ajout d'un nouveau ménage

Que voulez-vous faire ? Marius ?

Tableau de bord ← Revoir la liste des ménages + Ajout d'un nouveau ménage

Créez un nouveau ménage
Renseignez les informations obligatoires et sauvegardez les changements

Identification du ménage

Habitat & Cadre de vie
Patrimoine
Sécurité alimentaire
Membres du ménage

La ressource n'a pas encore été sauvegardée

Identification du ménage
Entrez les informations d'identification du ménage

Région* Choisir une région
Département* Choisir un département
Commune* Choisir une commune

Quartier Entrez le quartier
Milieu de résidence Rural

Le ménage dispose-t-il d'un numéro de téléphone ?
Non

Le ménage dispose-t-il d'un numéro de téléphone ?
Entrez un numéro

Type d'inscription au registre Opérations de ciblage c...
Non

Le chef de ménage sait-il lire et écrire ?
Non

Les membres ont-ils reçu de l'argent ?
Non

Les membres ont-ils reçu des dons ?
Non

Le ménage est-il affilié à une mutuelle de...
Le ménage dispose-t-il d'une couverture...
Que faire-vous quand un membre est...

Données informatives
Ressource créée par : Marius Kazé
Date de création : 11/06/2023
Dernière mise à jour : 11/06/2023

Sauvegarder

Resuc Apps Dashboard / Scorings

Que voulez-vous faire ? Marius ?

Tableau de bord + Créer un scoring

Scoring de variable de vulnérabilité
Cliquez sur le bouton GÉNÉRER LES BÉNÉFICIAIRES pour appliquer le scoring

Vulnérabilité sociale	Variables	Scores	Observations
Risque d'insécurité alimentaire de façon autonome le besoin alimentaire	Habituellement, en moyenne, combien de repas (Nour) prend-il par jour ?	10 points	Cette variable est issue du questionnaire ménage
Score alimentaire	Nombre de jours (Jours) de consommation d'un produit alimentaire au cours des 7 derniers jours	0 Point	
	Principale source de nourriture au cours des 7 derniers jours	10 points	Cette variable est issue du questionnaire ménage
Risque d'insécurité alimentaire de façon autonome le besoin de se soigner	Quand un membre de votre ménage est malade, que faites-vous ?	04 points	Cette variable est issue du questionnaire ménage

VOIR LES LISTES DE BÉNÉFICIAIRES

Vulnérabilité(T) = x(poids ménage) + y(poids individus) où T est le score total de vulnérabilité. X et Y seront estimés par une ACM. Les poids des ménages et individus seront issus du scoring.

Vous devez sélectionner la commune sur laquelle vous souhaitez appliquer le scoring.

Application du scoring
Restreindre l'application du scoring géographiquement.

Date collecte
Du Au

Espace de collecte
Région Choisir les régions

GÉNÉRER LES BÉNÉFICIAIRES

II.6.3 Certificate of good performance/past contracts



ATTESTATION DE BONNE EXECUTION

Je soussigné, Monsieur **Andrianaivoarivony Fanomezantsoa**, Coordonnateur du projet CCCD-Rio au PNUD Madagascar atteste par la présente que le Groupement MK BA / MK WBC dans le cadre du projet de **Développement d'un Système d'Information de Gestion de l'Environnement (SIGE)** pour Madagascar, a livré un système d'information moderne et performant au profit du Ministère de l'Environnement et du Développement Durable de Madagascar. Le consultant avait à sa charge des actions suivantes :

- Le recueil des besoins auprès des parties prenantes au projet ;
- La conception, le développement, le test et le déploiement en ligne du système d'information ;
- La traduction du système d'information en 03 langues : Français, Malagasy et Anglais ;
- La formation technique du staff de la Direction de la Communication et des Systèmes d'Information du Ministère ;
- La formation des utilisateurs provenant des régions cibles du projet à l'utilisation du système d'information ;
- La sensibilisation des parties prenantes à propos du SIGE ;
- La mise à jour des indicateurs du Cadre de Développement des Statistiques Environnementales (CDSE) de Madagascar ;
- En collaboration avec l'Institut National de la Statistique, le développement d'un formulaire pour la collecte de données pour le CDSE, puis l'apurement et la validation de ces données ;
- L'organisation d'une dizaine d'ateliers dans plusieurs villes, y compris la cérémonie de lancement officiel du SIGE faisant intervenir des autorités.

La mission a été menée à bien avec sérieux et professionnalisme, dans le respect des délais, avec notre pleine satisfaction et appréciation.

La présente attestation est délivrée pour servir et valoir ce que de droit.

Fait à Antananarivo le 31 mai 2024

Fanomezantsoa Andrianaivoarivony

Andrianaivoarivony Fanomezantsoa
Coordonnateur Projet CCCD-Rio / PNUD



ATTESTATION DE BONNE EXECUTION

Je soussignée, Madame **Mouna El JAOUHARI**, Cheffe de Bureau de la Coordination Résidente du Système des Nations Unies en Guinée atteste par la présente que le Groupement MK BA / MK WBC, dans le cadre du projet de **CREATION DU SITE WEB POUR LA PLATEFORME DE CONCERTATION ET DE COORDINATION DES PTF EN GUINEE**, a livré un système d'information moderne et performant au profit du Ministère du Plan et de la Coopération Internationale (MPCI) de Guinée. Le consultant avait à sa charge des activités suivantes :

- Le recueil des besoins auprès des parties prenantes au projet ;
- La conception, le développement et le test de la plateforme ;
- Le déploiement en ligne de la plateforme sur l'infrastructure du MPCI ;
- La formation du staff du MPCI et des organes associés à l'utilisation et à l'administration de la plateforme.

La mission a été menée à bien avec sérieux et professionnalisme, dans le respect des délais, avec notre pleine satisfaction et appréciation.

La présente attestation est délivrée pour servir et valoir ce que de droit.

Fait à Conakry le 31 mai 2024



Mouna El JAOUHARI

II.7 Quality Control System

Our quality control system consists of three rigorous levels of verification designed to ensure all deliverables meet NetHope's expectations and maintain the highest standards of web development.

II.7.1 Three-tier quality assurance framework

▶ Level 1: Continuous stakeholder involvement

- Early and consistent involvement of NetHope stakeholders from day one
- Regular feedback sessions to validate progress against requirements
- Collaborative approach to ensure alignment with organizational goals
- Development iterations based on stakeholder feedback
- Transparent communication channels for immediate issue resolution

▶ Level 2: Technical quality verification

- Systematic code reviews by senior developers
- Automated testing for functionality across browsers and devices
- Performance testing to ensure optimal page load times
- Security audits to identify and remediate vulnerabilities
- Accessibility compliance verification (WCAG standards)
- Cross-browser and cross-device compatibility testing
- SEO technical validation

▶ Level 3: Expert validation

- Final review by MK BA's Quality Control Expert
- Comprehensive assessment against NetHope's requirements
- Independent verification of deliverables against industry standards
- Validation of documentation completeness
- Pre-launch technical audit to ensure production readiness

II.7.2 Quality tools and methodologies

- **Version control:** Git for code management and version tracking
- **Performance monitoring:** Google PageSpeed Insights, GTmetrix, WebPageTest
- **Automated testing:** Jest for unit testing, Cypress for end-to-end testing
- **Security scanning:** OWASP ZAP, SSL Labs for SSL/TLS verification
- **Accessibility testing:** WAVE, axe DevTools
- **SEO validation:** Screaming Frog SEO Spider, Google Search Console
- **Browser testing:** BrowserStack for cross-browser verification

This comprehensive quality control system ensures that the NetHope website will not only meet current requirements but will be built on a foundation of best practices that facilitate future maintenance and enhancement.

II.8 Why choose MK BA?

Company qualification alignment with NetHope requirements

MK BA brings extensive experience in web development, digital transformation, and technology consulting for international organizations and nonprofits. Our qualifications directly align with NetHope's selection criteria as follows:

NetHope selection criteria	MK BA qualifications	Evidence
Technical expertise	8 years experience in web development and digital solutions - Proven WordPress expertise with focus on performance optimization - Experience migrating from Oxygen theme to modern alternatives - Strong portfolio in HTML, CSS, JavaScript, PHP, and responsive design	- UNDP Madagascar EMIS (2024) - UNDP Guinea Web Platform (2023-2024) - Bange Bank Cameroon Website (2023-2024) - UNICEF m-Health Initiative (2023-2024)
Problem-solving capabilities	- Agile SCRUM methodology for adaptive problem resolution - Proven track record of identifying and resolving complex web issues - Experienced with performance optimization for sites with global reach - Expertise with web performance monitoring and diagnostics tools	- Implemented zero-downtime migration for Bange Bank - Resolved complex structural issues for UNICEF projects - Implemented end-to-end testing for system reliability
Design sensibility	- User-centered design approach with focus on accessibility - Expertise in creating cohesive visual identities for organizations - Responsive design implementation across all devices - UI/UX specialists with international organization experience	- WCAG 2.1 AA compliant designs for all recent projects - Award-winning design for Bange Bank website - UI/UX leadership for multiple international organizations - Expertise in Figma and Adobe XD for collaborative design
Collaboration skills	- Experience working with distributed global teams - Collaborative tools integration (Jira, Trello, GitHub) - Clear communication protocols for remote collaboration	- Successfully coordinated 10+ projects with international stakeholders - Implemented collaborative workflows for nonprofit clients - Strong testimonials from past clients on team integration

	o Demonstrated ability to align technical work with organizational goals	o Regular stakeholder workshops for alignment and feedback
Communication skills	- o Clear technical documentation for diverse audiences - o Expertise in translating complex concepts for non-technical stakeholders - o Regular reporting and transparent project status updates - o Multilingual team (English and French fluency)	- o Comprehensive documentation delivered for all past projects - o Client testimonials praising communication clarity - o Effective stakeholder management across organizational levels - o Customized training materials for different user groups
Proactivity	- o Anticipatory approach to identifying potential issues - o Regular security and performance audits beyond scope requirements - o Proactive recommendation of enhancements and optimizations - o Forward-looking technology recommendations	- o Identified and resolved potential security vulnerabilities for UNDP - o Recommended performance enhancements for UNICEF platform - o Implemented preventative maintenance protocols - o Development of future-ready roadmaps for clients
Time management	- o Proven track record of on-time delivery - o Structured sprint planning with clear milestones - o Efficient resource allocation across project phases - o Agile methodology for adapting to changing priorities	- o 100% on-time delivery for last 8 major projects - o Efficient sprint management with documented velocity - o Successful multi-project management - o Effective risk mitigation strategies for timeline management

Implementation team expertise and alignment

Our carefully selected team brings specialized expertise that directly addresses NetHope's requirements for this project:

Team member	Role	Key qualifications	Relevance to NetHope requirements
Joel KUATE MABOU	Project Manager	12 years experience - PMP Certified - ISO 27001 Certified - Led multiple website projects for international organizations	- Expert in managing nonprofit website projects - Security implementation expertise for website protection - Skilled at stakeholder management across organizational levels - Experience with WordPress theme migrations
Marlyse TEUNOU	UX Engineer	11 years experience - Expert in Figma and Adobe XD - Led UX for UNDP and UNICEF projects - Responsive design specialist	- Will create intuitive navigation structures - Experience designing for global, diverse audiences - Focus on accessibility and inclusive design - Expertise in nonprofit brand alignment
Claude Cyriac KOUM	Business Analyst	15 years experience - CISA Certified - ITIL v3 Certified - Led requirements gathering for major platforms	- Will ensure precise requirements mapping - Expert in security implementation for websites - Experience with Campaign Monitor integration - Skilled at performance optimization strategies
Marius KEMAYOU	Full Stack Developer	11 years experience - WordPress specialist (8+ years) - Expert in Laravel, React, PHP - UNDP platform developer	- Will lead WordPress theme migration - Experience with Oxygen theme alternatives - API integration expertise (Campaign Monitor) - Geo-location implementation specialist
Louis YOUNBI	Full Stack Developer	12 years experience - JavaScript/TypeScript expert - Performance optimization specialist	- Will implement front-end optimizations - Security implementation expert - Cross-browser compatibility specialist

		○ UNDP Guinea platform developer	○ Experience developing for global accessibility
Francis KAMGA	Test Engineer	○ 8 years experience ○ PageSpeed optimization specialist ○ Cross-platform testing expert ○ UNICEF testing lead	○ Will ensure site meets performance targets ○ Experience testing nonprofit websites ○ Security vulnerability assessment expertise ○ Specialist in cross-device compatibility testing
Franck FOWA	Backstopper	○ 8 years experience ○ M&E specialist ○ Nonprofit project management expertise ○ Documentation specialist	○ Will ensure efficient administrative coordination ○ Remote team coordination specialist ○ Quality control implementation ○ Nonprofit communication expertise

Value added to NetHope

Our approach brings specific added value that directly addresses NetHope's needs:

NetHope need	MK BA value added	Tangible benefits
Modern, responsive design	○ Mobile-first design philosophy ○ Implementation of Astra Pro theme with exceptional performance ○ Component-based architecture for consistency	○ 40-60% improvement in mobile experience ○ WCAG 2.1 AA compliance for accessibility ○ 90+ PageSpeed scores on all devices
Oxygen theme migration	○ Seamless transition with zero downtime ○ Content preservation strategy ○ SEO retention methodology	○ No content loss during migration ○ Preservation of SEO rankings ○ Modern theme with long-term support
Enhanced user experience	○ User journey mapping and optimization ○ Information architecture refinement ○ Intuitive navigation implementation	○ Reduced bounce rates (20-30% typical improvement) ○ Increased session duration ○ Improved content discoverability

Geo-location capabilities	- o Interactive mapping integration - o Location-based filtering system - o Performance-optimized implementation	- o Intuitive location discovery - o Minimal impact on page load times - o Accessibility-compliant interactive maps
Campaign monitor integration	- o Seamless API implementation - o Custom form builder integration - o Performance analytics dashboard	- o Simplified signup management - o Enhanced subscriber data collection - o Improved conversion tracking
Security implementation	- o Multi-layered security approach - o Regular vulnerability scanning - o Secure authentication implementation	- o Protection against common attack vectors - o Reduced security incident risk - o PII data protection compliance
Knowledge transfer	- o Comprehensive documentation approach - o Tailored training program - o Ongoing support transition plan	- o Self-sufficiency for NetHope team - o Reduced dependency on external support - o Clear maintenance procedures

II.9 Administrative documents

Company Registration (1st page)

DECLARATION DE CONSTITUTION DE PERSONNE MORALE

RENSEIGNEMENTS RELATIFS A LA PERSONNE MORALE

DENOMINATION: MK BUSINESS ANALYSIS en abrégé "MK BA" SARL

NOM COMMERCIAL-ENSEIGNE: "MK BA" SARL SIGLE: "MK BA" SARL

ADRESSE DU SIEGE: DOUALA BP 17.802

ADRESSE DE L'ETABLISSEMENT CREE: SOCIETE A RESPONSABILITE LIMITEE "SARL"

FORME JURIDIQUE: SOCIETE A RESPONSABILITE LIMITEE "SARL"

N° R. C. C. M. 19/00180718/2017

CAPITAL SOCIAL: 1.000.000 F. CFA DONT NUMERAIRE: 1.000.000 F. CFA DONT NATURE

ACTIVITE: ACTIVITES PRINCIPALES: le e-business et e-commerce, la représentation et distribution, le trading, le marketing traditionnel et digital, l'ingénierie financière, les expertises, l'informatique, la télécommunication, l'ingénierie et conseils, les services liés aux états, entreprises, organismes internationaux et particuliers, les prestations de services...

Date de début: _____ Nombre de salariés prévus: _____

RENSEIGNEMENTS RELATIFS A L'ACTIVITE AUX ETABLISSEMENTS

PRINCIPAL ETABLISSEMENT OU SUCCURSALE: _____

Adresse: _____

Origine: Création, Achat, Apport, Prise en location gérance, autre (préciser): _____

Autre: _____

Précédent exploitant: Noms: _____ Prénoms: _____

Adresse: _____ N° RCCM: _____

Loueur de fonds (nom/dénomination/adresse): _____

ETABLISSEMENT SECONDAIRE: (autre que celui créé) Non, Oui (préciser): _____

Adresse: _____

Activités: _____

ASSOCIES TENUS INDEFINIMENT ET PERSONNELEMENT (*)

(*) La totalité des renseignements relatifs à ces actionnaires doit IMPERATIVEMENT figurer sur le formulaire complémentaire M.o Bis annexé

NOM	PRENOM	DATE ET LIEU DE NAISSANCE	ADRESSE

RENSEIGNEMENTS RELATIFS AUX ASSOCIES (*) ()**

(**) Concerne les Gérants, Administrateurs ou actionnaires ayant le pouvoir d'engager la personne morale

(**) Les renseignements ne pouvant figurer ci-dessous doivent IMPERATIVEMENT être reportés sur le formulaire M.o Bis annexé

NOM	PRENOM	DATE ET LIEU DE NAISSANCE	ADRESSE

COMMISSAIRES AUX COMPTES

NOM	PRENOM	DATE ET LIEU DE NAISSANCE	ADRESSE

LE SOUSSIGNE: Maître NKOUH MAWAFO FONKOUA Marie-Louise _____

demande à ce que la présente constitue _____

DEMANDE D'IMMATRICULATION AU R.C.C.M

La conformité de la déclaration avec les pièces justificatives produites en application de l'Acte Uniforme sur le Droit Commercial général a été vérifiée par le greffier en chef soussigné qui a procédé à l'inscription

Le 19 MAY 2017 _____ Sous le NUMERO 19/00180718/2017

Administrateur des Greffes

FAIT A DOUALA
Le 17 Mai 2017
Signature _____

Tax Compliance Certificate

REPUBLIQUE DU CAMEROUN

Paix-Travail-Patrie

MINISTRE DES FINANCES

DIRECTION GENERALE DES IMPÔTS

CENTRE DIVISIONNAIRE DES IMPOTS DE DOUALA 4

CDI DOUALA 4

REPUBLIC OF CAMEROON

Peace-Work-Fatherland

MINISTRY OF FINANCE

DIRECTORATE GENERAL OF TAXATION

DIVISIONNAL TAXATION CENTER OF DOUALA 4

Référence ACF:

22704

DOUALA

15/02/2025**ATTESTATION DE CONFORMITE FISCALE**La société: **SOCIETE MK BUSINESS ANALYSIS SARL**Numéro Identifiant Unique (NIU): **M051712628472K**Sigle **SOCIETE MK BA SARL**Ville: **DOUALA**Commune **DOUALA 5**Lieu Dit **MAKEPE**

B.P:

Tél fixe:

Tél. Mobile:

FAX:

Adresse électronique(e.mail):

REGIME: **SIMPLIFIÉ**

n'est redevable d'aucun impot vis -a- vis de l'administration fiscale.

En foi de quoi la présente attestation lui est délivrée pour servir et valoir ce que de droit , et est valable pour une durée de (03) mois à compter de la date de création (**15/02/2025**).

NB: La présente attestation tient également lieu de justificatif de paiement de la patente EXERCICE 2025 ,de certificat d'imposition et de bordereau de situation fiscale.

LE RECEVEUR DES IMPOTS

LE CHEF DE CENTRE CDI 4



MBOM BAHÉL
Contrôleur Principal des Régies Financières
(Impôts)




EBWELE EBWELE DANIEL
Inspecteur Principal des Régies Financières
(Impôts)



Date Edition: 17/02/2025 à 18:03:30

III. GENERAL PROJECT FRAMEWORK

III.1 Executive Summary

MK BA is pleased to submit this proposal to support NetHope's Director of Communications and Head of Data and Digital Solutions in enhancing the organization's online presence. With 7 years of experience delivering digital solutions for international organizations and nonprofits, we offer a unique blend of technical expertise, nonprofit sector knowledge, and a proven track record of successful web development projects.

NetHope's requirements for website enhancement, including performance optimization, theme migration, and improved functionality, align perfectly with our core competencies. Our proposal addresses each aspect of the scope of work through a structured, user-centered approach that combines technical excellence with an understanding of nonprofit communication needs.

Our team of experts, led by a Project Manager with extensive experience in digital platform development for international organizations, brings together specialists in WordPress development, UX/UI design, and technical optimization. Having successfully implemented similar projects for organizations like UNDP, UNICEF, and international banks, we understand the unique challenges and opportunities in enhancing digital platforms for mission-driven organizations.

We propose an agile, phased approach that begins with a comprehensive website audit, followed by collaborative design, incremental development, and thorough testing. This methodology ensures continuous alignment with NetHope's goals while allowing for flexibility and adaptation throughout the project lifecycle.

Our solution will deliver:

- A fully optimized WordPress website with significantly improved speed and performance
- Seamless migration from the Oxygen theme to a more stable and flexible alternative
- Enhanced user experience through improved navigation and responsive design
- Strengthened security and technical foundation
- Comprehensive documentation and knowledge transfer to ensure sustainable maintenance

MK BA is committed to not just implementing technical improvements, but to being a true partner in advancing NetHope's mission through an effective, engaging digital presence.

III.2 Background

NetHope stands at the intersection of technology and nonprofit work, serving as a catalyst for collaboration between humanitarian organizations and technology innovators. Founded to bring the power of technological solutions to humanitarian challenges, NetHope has grown to become a consortium of nearly 60 global nonprofits, working across 190 countries.

In today's digital landscape, an organization's online presence is a critical component of its ability to communicate its mission, engage stakeholders, and facilitate collaboration. For NetHope, whose work involves connecting humanitarian organizations with technological resources, having a robust, accessible, and user-friendly website is particularly vital.

The current NetHope website faces several challenges that limit its effectiveness as a communication and engagement tool. Built on WordPress with the Oxygen theme module, which is approaching expiration, the site requires modernization to align with current web standards and user expectations. Issues with navigation, performance, and functionality are hindering the organization's ability to effectively showcase its work and

engage with its diverse audience of member organizations, technology partners, and the broader humanitarian community.

Additionally, as an organization that champions technological innovation in the nonprofit sector, NetHope's own digital presence must exemplify the standards it promotes. This includes not only visual appeal and functionality but also technical aspects such as site speed, security, and accessibility.

The web development consultancy project comes at a pivotal time as NetHope seeks to enhance its digital communication strategy and strengthen its online engagement with stakeholders. A refreshed, optimized website will support NetHope's mission by:

1. Improving access to critical resources and information for member organizations
2. Enhancing the organization's ability to communicate its impact and initiatives
3. Facilitating better engagement with partners, donors, and the broader community
4. Demonstrating technological best practices that align with the organization's advocacy

MK BA understands these challenges and opportunities, having worked extensively with international organizations facing similar digital transformation needs. Our approach to this project is informed by both technical expertise and a deep appreciation for NetHope's mission and the unique context in which it operates.

III.3 Project Objectives

III.3.1 Global objective

The primary objective of this consultancy is to enhance NetHope's online presence by developing a modern, high-performing, and user-friendly website that effectively communicates the organization's mission, facilitates stakeholder engagement, and serves as a robust digital platform for NetHope's communications strategy.

III.3.2 Specific objectives

Objective area	Description	Key performance indicators
Technical Performance	Systematically audit, optimize, and maintain the website's technical infrastructure to ensure optimal performance and security	• 40% improvement in page load time; 99.9% website uptime; Elimination of all identified security vulnerabilities; Successful SSL certificate renewals.
Theme Migration	Successfully migrate from the expiring Oxygen theme to a more sustainable, flexible theme while preserving functionality and improving design	• Zero data loss during migration; Successful transfer of all content and features; Implementation of an approved design that enhances user experience; Comprehensive documentation of the new theme implementation.
User Experience	Improve navigation, accessibility, and overall user experience across the website for all device types	• 30% decrease in bounce rate; 25% increase in average session duration; WCAG 2.1 AA compliance achievement; Successful implementation of improved information architecture.
Content Management	Enhance content management capabilities to enable efficient updates by NetHope staff	• Creation of intuitive WordPress content blocks; Implementation of streamlined publishing workflows; Development of user-friendly templates for common content types.
SEO & Visibility	Improve technical SEO elements to increase organic search visibility	• Implementation of optimized URL structure; Proper implementation of meta data; Improved page indexing; Enhanced site performance metrics in Google Search Console

Integration	Ensure seamless integration with third-party tools and platforms used by NetHope	• Successful integration with Campaign Monitor; - Functional connections with analytics platforms; - Implementation of data sharing capabilities between systems.
--------------------	--	---

III.4 Deliverables and expected results

Phase 1: Inception and Discovery		
Deliverable	Description	Expected results
Inception Report	Comprehensive document outlining the project approach, timeline, and methodology	• Clear roadmap for project execution • Established success metrics • Defined roles and responsibilities <i>Success Criteria: Approval by NetHope within 5 days of submission</i>
Website Performance Audit	Detailed analysis of current website performance, identifying issues and opportunities for improvement	• Comprehensive list of performance issues • Prioritized action items • Baseline metrics for future comparison <i>Success Criteria: Identification of all critical performance bottlenecks</i>
Technical Requirements Document	Detailed specification of technical requirements, including server environment, plugins, and integrations	• Clearly defined technical specifications • Documentation of required integrations • List of recommended technologies <i>Success Criteria: Comprehensive coverage of all technical aspects</i>
Phase 2: Design		
Deliverable	Description	Expected results
UI/UX Design Mockups	Visual designs for key website pages, showcasing the proposed new theme and layout	• Modern, engaging visual design • Improved information architecture • Mobile-responsive layouts <i>Success Criteria: Design approval by NetHope stakeholders</i>

PROPOSAL FOR WEB DEVELOPER CONSULTANT		
Wireframes	Structural layouts for homepage and key section pages	• Clear content hierarchy • Improved navigation flow • Optimized user journeys <i>Success Criteria: Improved user journey flows</i>
Theme Migration Plan	Detailed plan for transitioning from Oxygen theme to the new theme	• Step-by-step migration process • Risk mitigation strategies • Testing protocols <i>Success Criteria: Comprehensive migration pathway with minimal disruption</i>
Phase 3: Development		
Deliverable	Description	Expected results
Development Environment	Secure staging environment for development and testing	• Isolated testing environment • Functional copy of production site • Version control implementation <i>Success Criteria: Fully functional staging environment</i>
WordPress Theme Implementation	New theme implementation with all required functionality	• Responsive design across devices • Improved page load times • Enhanced visual appeal <i>Success Criteria: Successful theme application with all functionality preserved</i>
Custom WordPress Blocks	Development of custom content blocks for easy page building	• User-friendly content management • Consistent design elements • Flexible content options <i>Success Criteria: Content editors can easily create and update pages</i>
SEO Implementation	Technical SEO optimizations including URL structure, metadata, and image optimization	• Improved search engine visibility • Enhanced metadata structure • Optimized page indexing <i>Success Criteria: All pages pass SEO technical audits</i>

Phase 4: Testing and Deployment

Deliverable	Description	Expected results
Test Results Documentation	Comprehensive testing results including functionality, performance, and compatibility	• Verification of all requirements • Documentation of resolved issues • Performance benchmarks <i>Success Criteria: All critical tests passed</i>
Deployed Website	Live implementation of the new website	• Fully functional public website • Optimized performance • All integrations working <i>Success Criteria: Successful launch with minimal downtime</i>
User Training Materials	Documentation and training resources for NetHope staff	• Comprehensive user guides • Video tutorials • Best practice documents <i>Success Criteria: Staff can confidently manage website content</i>

Phase 5: Maintenance and Support

Deliverable	Description	Expected results
Monthly Performance Reports	Regular analysis of website performance metrics	• Ongoing performance tracking • Identification of optimization opportunities • Actionable recommendations <i>Success Criteria: Continuous performance improvement</i>
Technical Documentation	Comprehensive documentation of all technical aspects of the website	• Complete code documentation • System architecture diagrams • Maintenance procedures <i>Success Criteria: Future developers can easily understand and maintain the site</i>
Transition Portfolio	Documentation to facilitate smooth transition at the end of the contract	• Knowledge transfer plan • Outstanding issues log • Future recommendations <i>Success Criteria: Seamless handover process</i>

III.5 Location

Project execution approach

MK BA will execute this project remotely from our headquarters in Douala, Cameroon, leveraging our established remote collaboration infrastructure and methodologies. Our location strategy offers several advantages for this project while ensuring seamless service delivery to NetHope.

III.5.1 Operational setup

Our Douala office is equipped with:

- Enterprise-grade fiber internet connectivity with redundant backup lines
- Uninterrupted power supply infrastructure ensuring 24/7 operations
- Secure development environment with advanced cybersecurity protocols
- State-of-the-art collaboration tools and project management infrastructure

III.5.2 Time zone advantage

Operating from West-Central Africa (UTC+1) positions us advantageously between NetHope's global operations:

- Overlap with European working hours for real-time collaboration
- Early morning availability for North American stakeholders
- Ability to address urgent issues during US evening hours
- Flexibility in scheduling meetings across multiple time zones

III.5.3 Remote collaboration framework

Our team has refined a remote collaboration methodology through our work with international organizations such as UNDP, UNICEF, and others:

1. **Regular synchronization:** Scheduled video conferences with NetHope stakeholders at mutually convenient times
2. **Continuous communication:** Utilization of collaboration platforms (MS Teams, Slack, etc.) per NetHope's preference
3. **Progress transparency:** Real-time access to development environment and project management tools
4. **Documentation rigor:** Comprehensive documentation of all meetings, decisions, and development activities

III.5.4 Quality assurance process

Our location-independent quality assurance process includes:

- Automated testing protocols that run continuously throughout development
- Secure staging environment for stakeholder review and feedback
- Comprehensive cross-device and cross-browser testing
- Regular performance benchmarking against global standards

III.5.5 Contingency planning

To mitigate any location-specific risks, we maintain:

- Secondary internet providers with automatic failover
- Backup power generation systems
- Distributed team capability with staff in multiple locations if needed
- Alternate work arrangements for critical team members during infrastructure disruptions

MK BA's successful track record of delivering high-quality web development services to international clients from our Douala base demonstrates our ability to execute this project effectively. Our approach combines local expertise with global delivery standards, ensuring NetHope receives exceptional service regardless of physical distance.

IV. IMPLEMENTATION METHODOLOGY

As part of this project, MK BA will adopt an incremental and inclusive approach that actively engages all project stakeholders from the outset. Our methodology is designed to be user-centered and results-oriented, following the agile SCRUM framework which allows for close monitoring, greater stakeholder involvement, and flexibility in addressing evolving client needs throughout the project lifecycle.

The implementation of the SCRUM method will begin with defining clear user stories and organizing work into two-week sprints that will be reviewed collaboratively with NetHope. This incremental approach means that the final deliverable will be subdivided into smaller, manageable components that will be produced and tested progressively according to agreed priorities. Website features will be developed iteratively, with temporary deployments allowing NetHope stakeholders to monitor development progress and provide timely feedback.

[Our recommendation for NetHope website enhancement](#)

MK BA proposes a comprehensive approach to enhance NetHope's online presence through an agile, user-centered methodology. Based on our analysis of your current website and the expiration of the Oxygen theme/module, we recommend migrating to **Astra Pro** - a lightweight, highly customizable WordPress theme with excellent performance metrics and seamless integration with page builders. This theme offers exceptional speed optimization capabilities and robust WooCommerce support, addressing your requirements for improved performance and user experience.

Recommendation: We suggest implementing a modular content architecture using Advanced Custom Fields (ACF) with the Astra theme to enable your communications team to easily update dynamic content while maintaining design consistency. This approach would allow for component-based page building that remains flexible while ensuring content governance across your global network.

Our methodology consists of five distinct yet interconnected phases:



IV.1 Phase 1: Inception and Discovery

Objectives

The Inception and Discovery phase serves four critical objectives:

- **Align all stakeholders** on expectations, objectives, and scope of the mission
- **Establish a consensus** on the methodology and project plan
- **Review requirements** thoroughly with key stakeholders
- **Develop a comprehensive** project inception report

Description

This phase consists of four structured steps that create a solid foundation for the entire project.

Activity 1.1 : Project kickoff meeting

Immediately upon contract award, we will conduct a kickoff meeting with key NetHope stakeholders. This initial engagement will serve multiple crucial functions:

- > First, we will work to align all participants on the project's goals, scope, and expectations. Rather than treating this as a formality, we view the kickoff as a critical opportunity to establish a shared vision of success. We will facilitate structured discussions about what constitutes a successful website enhancement for NetHope, identifying priority areas and potential challenges.
- > Second, we will introduce the project teams from both NetHope and MK BA, establishing clear focal points for different aspects of the project. Our team will include the Project Manager, UX Designer, Full Stack Developers, and Test Engineer, each with defined responsibilities that will be clearly communicated. We will also identify the key decision-makers and subject matter experts from NetHope who will provide input throughout the process.
- > Third, we will establish the project's organizational structure, including communication channels, meeting cadence, and escalation protocols. Based on our experience with international organizations, we recognize the importance of establishing clear information flows from the outset. We will propose a

regular meeting schedule, reporting templates, and collaboration tools that align with NetHope's preferences.

- > Finally, we will exchange complementary documentation and establish the procedures and rules to be followed throughout the project. This includes determining review and approval processes, quality standards, and project governance mechanisms.

The kickoff meeting will be documented in detail, with action items and decisions circulated to all participants within 24 hours to ensure a common understanding moving forward.

Activity 1.2: Requirements gathering

This step involves refining the requirements specified in the terms of reference and gathering additional insights from end users. Our requirements gathering process will be comprehensive, addressing both functional and non-functional aspects of the website enhancement.

We will conduct structured interviews with key stakeholders, including the Director of Communications and the Head of Data and Digital Solutions, to understand their specific needs and expectations. These interviews will be conducted using a predefined questionnaire designed to elicit detailed information about current pain points, desired improvements, and success criteria.

Our requirements gathering activities will specifically focus on detailing the functionalities identified in the terms of reference:

- **Modern, responsive design:** We will explore NetHope's brand guidelines, preferred aesthetic direction, and responsive design requirements across different devices and screen sizes.
- **Enhanced navigation and user experience:** Through user journey mapping and stakeholder input, we will identify specific navigation improvements needed to enhance user experience.
- **Advanced online banking & branches geo-location capabilities:** We will gather detailed requirements for implementing geo-location features, including data sources, display preferences, and integration requirements.
- **Improved security measures:** We will conduct a security assessment of the current website to identify vulnerabilities and gather requirements for enhanced security protocols.
- **Faster load times and optimized performance:** Using tools like Google PageSpeed Insights and WebPageTest, we will analyze the current website's performance and establish baseline metrics for improvement.
- **Integration of innovative features:** We will explore opportunities for innovative features that align with NetHope's mission and user needs.
- **Enhanced communication tools:** We will gather specific requirements for communication tools, including integration with Campaign Monitor for sign-up forms and other potential communication channels.
- **Multi-channel communication:** We will explore requirements for ensuring consistent user experience across different communication channels and platforms.

Beyond stakeholder interviews, we will conduct a thorough review of the current website, analyzing its structure, content, functionality, and technical implementation. This analysis will help us understand the starting point and identify specific areas for improvement.

Activity 1.3: Technology requirements analysis

A technical discussion will be held with NetHope's IT team to align on technical choices, including programming languages, database management systems, and other critical technology components.

MK BA brings proven expertise in numerous web development environments and database management systems, including:

- **PHP environments:** Laravel and Symfony frameworks, integrated with frontend technologies like AngularJS, ReactJS, jQuery, NodeJS, along with HTML5 and CSS3 (Bootstrap)
- **Java environment:** JEE, Spring, Tomcat, and Glassfish
- **Python environment:** Django framework
- **Microsoft environment:** C#, .NET
- **Database systems:** MySQL, PostgreSQL, Microsoft SQL Server, Oracle Database, and MongoDB
- **Server operating systems:** Ubuntu Server and Windows Server

During this technical analysis, we will specifically assess the current WordPress implementation, focusing on the Oxygen theme that is expiring. We will evaluate different migration options, considering factors like:

- Compatibility with existing content and functionality
- Performance impact of different theme options
- Long-term sustainability and support availability
- Alignment with NetHope's visual identity and communication needs

We will also analyze the current plugin ecosystem, identifying essential plugins that need to be maintained, outdated plugins that should be replaced, and potential new plugins that could enhance functionality while maintaining optimal performance.

For third-party integrations, particularly Campaign Monitor, we will examine the current implementation and identify opportunities for improved integration that enhances both functionality and data analysis capabilities.

Activity 1.4: Review of NetHope's existing website

MK BA's team has already conducted a preliminary review of NetHope's website and intends to deepen this analysis when the contract is awarded. This comprehensive review will help clarify key improvement points that have led to the redesign request.

We will identify both strengths and weaknesses of the current website, collaborating with the NetHope team to preserve and enhance the strengths while addressing the weaknesses. This analysis will cover multiple dimensions:

- **User experience assessment:** We will evaluate the visual design, branding consistency, information architecture, and ease of access to key information. This assessment will include heatmap analysis (if analytics are available) to understand how users currently interact with the site.
- **Content completeness and quality:** We will review the current content structure, identifying gaps, redundancies, and opportunities for improved organization and presentation.
- **Administrative experience:** We will assess the ease of content management and website administration, identifying pain points in the current workflow that could be addressed in the redesigned site.
- **Technical implementation:** We will conduct a technical audit of the current implementation, focusing on code quality, performance optimization opportunities, and potential security vulnerabilities.

The findings from this comprehensive review will be documented and prioritized based on impact and implementation complexity, creating a clear roadmap for improvement.

Activity 1.5: Inception report development

Following the completion of the initial discovery activities, we will develop a comprehensive Inception Report that synthesizes all findings, decisions, and plans. This report will serve as the foundational document for the remainder of the project and will include:

1. **Agreed methodology and project schedule:** A detailed project plan with clear milestones, deliverables, and timelines based on the discoveries and agreements made during the kickoff and subsequent analysis.

2. **Roles and responsibilities:** A clear delineation of responsibilities for both MK BA and NetHope team members, ensuring accountability throughout the project.
3. **Detailed requirements:** Comprehensive documentation of both functional and non-functional requirements, organized by priority and implementation phase.
4. **Stakeholder analysis:** Identification of key stakeholders, their interests, influence, and engagement strategies throughout the project.
5. **Market research findings:** Analysis of industry best practices, competitor websites, and emerging trends relevant to NetHope's online presence.
6. **Technologies to be used:** Detailed recommendations for the technology stack, including WordPress theme selection, plugins, and integration approaches.

The draft Inception Report will be submitted to NetHope for review and feedback. We will incorporate any comments and revisions until reaching a final version that has full stakeholder approval. This collaborative approach ensures that all parties have a shared understanding of the project before proceeding to the Design Phase.

Estimated workload and duration

WORKLOAD		DURATION
15 person-days		10 working days

Role	Days	Activities
Project Manager	5	Kickoff meeting, stakeholder coordination, inception report development, project planning
UX Designer	3	Website UI/UX audit, usability assessment, requirements gathering
Web Developer	4	Technical audit, WordPress assessment, technology stack evaluation
Test Engineer	3	Performance testing, security assessment, quality assurance planning
Total	15 person-days	Duration: 10 working days

Deliverables

- **Inception Report** containing:
 - Agreed methodology and project schedule
 - Roles and responsibilities matrix
 - Detailed requirements specification
 - Stakeholder analysis
 - Market research findings
 - Technology recommendations
 - Risk assessment and mitigation strategies

Upon validation of the inception report by NetHope, we will transition seamlessly to the Design Phase, carrying forward the insights and agreements established during this critical foundation-setting phase.

IV.2 Phase 2: Design

Objectives

The Design Phase has two primary objectives:

- **Create a compelling and functional user interface and user experience** that aligns with NetHope's communication goals
- **Establish the technical architecture and database design** that will support the enhanced website

Description

The Design Phase builds upon the discoveries and decisions from Phase 1, translating requirements into concrete design concepts and technical specifications. This phase is structured into four distinct steps.

Activity 2.1 : User interface and experience design

Upon project commencement, we will develop a comprehensive design concept for the entire website, expanding beyond the initial samples¹.

Our UX/UI Designer will lead this process, working closely with NetHope's communications team to ensure the design aligns with organizational branding and communication objectives. We will utilize industry-standard design tools including Figma and Adobe XD to create high-fidelity mockups for all key website pages.

The design process will be iterative, beginning with wireframes that establish information architecture and content hierarchy. These wireframes will be presented to NetHope stakeholders for initial feedback before proceeding to full visual designs. We recognize that visual design is subjective, so we will present multiple design concepts for NetHope to consider, each aligned with the organization's visual identity but offering different interpretations.

Once basic layouts are approved, we will create detailed mockups showing:

- Typography choices and hierarchies
- Color schemes and application
- Navigation structures
- Content presentation formats
- Interactive element designs
- Mobile and tablet responsive variations

To provide NetHope stakeholders with a clear understanding of the proposed user experience, we will create a clickable prototype that simulates website navigation and interaction. This prototype will be accompanied by a video walkthrough that demonstrates the envisioned user journey through key sections of the site.

NetHope's feedback will be incorporated through multiple refinement cycles until reaching final design approval. This collaborative approach ensures the design not only meets aesthetic preferences but also satisfies functional requirements and communication objectives.

Activity 2.2 : Database design

While WordPress provides a standardized database structure, customizations are often needed to support specific functionality. Our database design work will focus on:

- > First, we will conduct a thorough assessment of the current WordPress database implementation, identifying custom tables, metadata structures, and potential optimization opportunities. This analysis

¹ A preliminary mockup for certain pages of the NetHope website is provided in the Annexe 1 of our offer.

will help us understand what needs to be preserved during the theme migration and what can be improved.

- > Second, we will design a logical data model for any custom functionality that requires database extensions beyond the standard WordPress schema. For instance, if NetHope requires specialized content relationships or custom post types, we will design these using the MERISE method to ensure data integrity and performance.

This data modeling will include defining:


- Custom post types and taxonomies
- Extended metadata fields and relationships
- Integration points with third-party systems
- Optimization strategies for frequently accessed data

All database extensions will be designed with performance and security as primary considerations, ensuring they follow WordPress best practices and maintain compatibility with the core system. We will normalize the logical data model to the Boyce-Codd normal form, creating an efficient and maintainable database structure.

The resulting database design will be documented with entity-relationship diagrams and data dictionaries that NetHope's technical team can reference for future maintenance and integration projects.

Activity 2.3 : Technical architecture

The technical architecture for NetHope's website will follow a standard 3-tier model optimized for WordPress environments. This architecture ensures clean separation between presentation, business logic, and data layers while maintaining the flexibility and extensibility that are hallmarks of the WordPress platform.

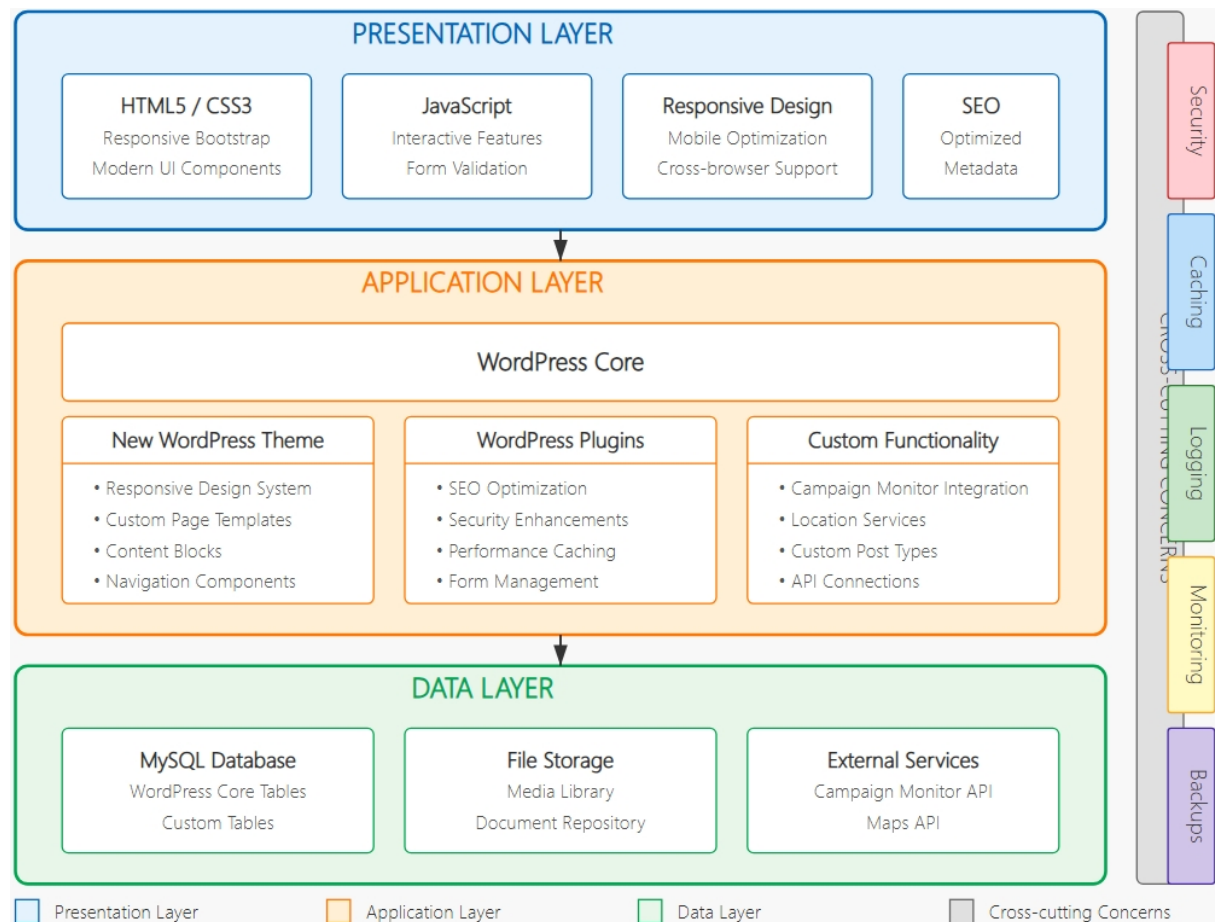

> **Tier 1: Presentation layer.** The presentation layer will consist of the web-based graphical user interface accessible through HTTPS. This includes all the forms, views, and interactive elements presented to users. Our implementation will emphasize:

- Responsive design ensuring optimal display across devices (laptops, desktops, tablets, smartphones)
- Progressive enhancement techniques that maintain functionality across various browser capabilities
- Accessibility compliance with WCAG 2.1 AA standards
- Performance optimization for fast loading times across global regions

The presentation layer will be built using modern HTML5, CSS3 (with Bootstrap for responsive components), and JavaScript frameworks that complement WordPress's architecture.

> **Tier 2: Application layer.** The application layer handles all data processing and business logic. For WordPress, this includes:

- WordPress core functionality
- Theme components that replace the current Oxygen theme
- Essential plugins selected during the technical evaluation
- Custom functionality developed specifically for NetHope's requirements

Our architecture will emphasize modular design with clear separation of concerns. Custom functionality will be implemented through properly structured WordPress hooks and filters rather than direct core modifications, ensuring maintainability through WordPress updates.

> **Tier 3: Data layer.** The data layer manages persistent storage of content, settings, and user data. Our architecture will:

- Leverage WordPress's native database structure
- Implement any required custom tables following WordPress conventions
- Optimize database queries for performance
- Establish proper indexing strategies for frequently accessed data
- Implement caching mechanisms to reduce database load

The technical architecture will also address cross-cutting concerns:

- **Security:** Implementation of proper authentication, authorization, input validation, and output encoding to protect against common web vulnerabilities
- **Caching:** Strategic implementation of page, object, and database query caching to optimize performance
- **Logging:** Comprehensive logging of system events, errors, and user actions for troubleshooting and auditing
- **Monitoring:** Integration with monitoring tools to track performance and availability

This architecture will be documented with detailed diagrams and specifications that will guide development activities in the subsequent phase.

Activity 2.4 : Design approval workshop

Following the completion of all design artifacts, we will organize a dedicated workshop with key NetHope stakeholders to present, discuss, and finalize the design. This workshop will be structured to:

1. Present the finalized UI/UX designs with explanations of design decisions and their alignment with requirements
2. Demonstrate the clickable prototype to illustrate user journeys and interactions
3. Review the database design and technical architecture at a level appropriate for the audience

4. Address questions and gather final feedback
5. Document approval or any required modifications

This collaborative workshop approach ensures all stakeholders have an opportunity to provide input before development begins, reducing the risk of misalignment during implementation. Any modifications agreed during the workshop will be incorporated into the final design documents before proceeding to the Development Phase.

We recognize that approval processes often involve multiple stakeholders with varying concerns. Our workshop format accommodates this by organizing discussions around both aesthetic considerations and technical validations, allowing different stakeholder groups to focus on their areas of expertise.

Upon final approval of all design elements, we will prepare a comprehensive Design Documentation Package that includes all approved designs, technical specifications, and notes from the approval process. This package will serve as the definitive reference for development activities.

Estimated workloads and duration

WORKLOAD		DURATION
20 person-days		10 working days

Role	Days	Activities
Project Manager	3	Stakeholder coordination, design review, approval facilitation
UX Designer	10	Wireframes, visual designs, prototyping, design revisions
Web Developer	5	Technical architecture, database design, migration planning
Test Engineer	2	Design review, testability assessment, test planning
Total	20 person-days	Duration: 10 working days

Deliverables

- **Approved UI/UX Design Package** including:
 - Wireframes for all key page templates
 - Full visual designs for all page templates
 - Responsive variations for mobile and tablet
 - Interactive prototype demonstrating user flows
 - Style guide documenting typography, colors, and UI components
- **Technical Architecture Document** including:
 - System architecture diagrams
 - Component specifications
 - Integration points and APIs
 - Security considerations
 - Performance optimization strategies
- **Database Design Document** including:
 - Entity-relationship diagrams
 - Custom post types and taxonomies specifications
 - Data dictionary
 - Migration considerations

The approval of these design deliverables will mark the successful completion of Phase 2, providing a solid foundation for development activities in Phase 3.

IV.3 Phase 3: Development

Objectives

The Development Phase focuses on translating the approved designs into a fully functional website that meets all technical and user experience requirements. The objectives of this phase are to:

- **Develop and implement** the new WordPress theme replacing the Oxygen framework
- **Build all required technical components** following the approved architecture
- **Integrate third-party services** including Campaign Monitor for sign-up forms
- **Optimize website performance** for speed, security, and user experience
- **Conduct thorough testing** at each development iteration

Description

The Development Phase represents the core implementation work of the project, where approved designs and technical specifications are transformed into a functional website. This phase is structured into six interconnected steps.

Activity 3.1 : Development environment setup

Before beginning active development, we will establish a robust development environment that ensures code quality, version control, and collaboration efficiency.

First, we will configure a staging environment that mirrors the production environment but remains isolated for development purposes. This environment will include a complete installation of WordPress with relevant plugins, allowing us to develop and test without affecting the live website. We use industry-standard tools to ensure consistency between development and production environments, minimizing the risk of deployment issues.

Second, we will implement a version control system using Git to manage code changes throughout the development process. Our repository structure will follow WordPress best practices, separating theme files, custom plugins, and configuration elements. This structured approach enables multiple developers to work simultaneously while maintaining code integrity and providing a complete history of changes.

Third, we will establish automated deployment workflows to streamline the process of moving code between development, staging, and production environments. These workflows will include automated testing to catch issues early in the development cycle, ensuring that only quality code reaches the staging environment for review.

Finally, we will configure development tools and standards, including code linting, formatting standards, and documentation requirements. These standards ensure consistency across the codebase and facilitate future maintenance by NetHope's technical team.

Activity 3.2: Core WordPress theme development

The migration from the expiring Oxygen theme to a new theme framework represents a critical component of this project. Our approach to theme development follows WordPress best practices while ensuring a seamless transition.

We will begin by developing the theme's foundational elements, including the header, footer, and basic layout structures. These elements will be implemented according to the approved designs from Phase 2, with careful attention to both aesthetic requirements and technical performance considerations. Our development approach

emphasizes clean, semantic HTML, modular CSS using SASS preprocessors, and efficient JavaScript that enhances the user experience without compromising performance.

Next, we will implement the responsive design frameworks that ensure optimal display across devices. Rather than creating separate mobile designs as an afterthought, our mobile-first approach builds responsiveness into every component from the beginning. This ensures consistent user experience regardless of device, with special attention to navigation elements, typography scaling, and touch-friendly interactive components.

The theme will include custom page templates for key content types, including the homepage, program pages, member pages, and resource libraries. Each template will be structured to highlight the most important content while maintaining visual consistency across the site. Template development will follow the WordPress template hierarchy, allowing for specific customization while maintaining a consistent codebase.

Throughout theme development, we maintain strict adherence to WordPress coding standards and accessibility guidelines (WCAG 2.1 AA compliance). This commitment ensures that the website is not only visually appealing but also accessible to users with disabilities and optimized for long-term maintenance.

Activity 3.3: Custom functionality implementation

Beyond the core theme, NetHope's website requires several custom functionalities to meet its operational requirements. These functionalities will be implemented as modular components that integrate seamlessly with the WordPress framework.

One key component is the Campaign Monitor integration for sign-up forms. We will develop a custom integration that allows NetHope staff to create and manage forms directly within the WordPress admin interface, with automatic synchronization to Campaign Monitor lists. This integration will include custom form builders, validation logic, and reporting capabilities that track form submissions and conversion rates.

Another important functionality is the location services implementation for branch and office geo-location. This feature will use mapping APIs to display NetHope's global presence, with filtering capabilities that allow users to find relevant locations based on region, program focus, or other criteria. The implementation will include both interactive map displays and traditional directory listings for accessibility.

We will also develop custom content types and taxonomies for programs, members, resources, and other specialized content. These custom types will extend WordPress's native content management capabilities, providing structured data models that ensure consistency and enable advanced filtering and search capabilities. Each content type will include custom meta fields, relationship mappings, and specialized display templates.

Additionally, we will implement enhanced search functionality that allows users to quickly find relevant content across the website. Our search implementation will include faceted filtering, relevance ranking, and content previews to help users efficiently navigate NetHope's information resources.

Activity 3.4: Performance optimization

Website performance directly impacts user engagement and search engine rankings. Throughout the development process, we will implement various optimization techniques to ensure the website loads quickly and operates efficiently.

Image optimization will be a key focus, as images often represent the largest portion of a page's file size. We will implement responsive image handling that serves appropriately sized images based on device characteristics, modern image formats like WebP with appropriate fallbacks, and lazy loading techniques that defer non-essential image loading until they are needed.

Code optimization will include minification and bundling of CSS and JavaScript files to reduce file sizes and HTTP requests. We will implement critical path CSS rendering for above-the-fold content, ensuring that the most visible portions of each page render quickly while less critical styles load in the background.

Database query optimization will ensure efficient data retrieval, with careful attention to query complexity, proper indexing, and caching of frequent queries. We will implement a tiered caching strategy that includes object caching for database queries, page caching for frequently accessed content, and browser caching for static assets.

Server-side optimizations will include proper configuration of HTTP/2, compression algorithms, and cache headers to minimize network latency and bandwidth usage. We will also implement Content Delivery Network (CDN) integration for static assets, ensuring fast delivery regardless of user location.

These optimization efforts will be guided by regular performance testing using tools like Google PageSpeed Insights, WebPageTest, and GTmetrix, with performance metrics tracked throughout development to ensure continuous improvement.

Activity 3.5: Security implementation

Security is a critical consideration for any website, particularly for an organization like NetHope that works with numerous international partners. Our security implementation follows a defense-in-depth approach, securing the website at multiple levels.

At the infrastructure level, we will ensure proper server hardening, including secure configuration of web servers, database servers, and network components. This includes implementing proper firewall rules, disabling unnecessary services, and configuring secure access protocols.

For the WordPress application, we will implement security best practices including limited login attempts, strong password enforcement, two-factor authentication for administrative accounts, and role-based access controls that limit privileges to the minimum required for each user type. We will also ensure that all WordPress core files, themes, and plugins are kept updated with security patches.

Code-level security measures will include input validation for all user-submitted data, output encoding to prevent XSS attacks, prepared statements for database queries to prevent SQL injection, and CSRF protection for form submissions. We will also implement proper file permissions and secure handling of file uploads to prevent unauthorized access.

Additional security measures will include implementation of HTTPS throughout the site with proper SSL/TLS configuration, security headers to prevent common web vulnerabilities, and regular security scanning to identify and address potential issues before they can be exploited.

Activity 3.6: Testing and Quality Assurance

Throughout the development phase, rigorous testing and quality assurance processes will ensure that the website meets all functional, performance, and security requirements.

Unit testing will be conducted for individual components and functions, verifying that each piece of code performs as expected in isolation. Integration testing will assess how components work together, ensuring that interactions between different parts of the system function correctly.

Functional testing will verify that all features meet the specified requirements, with test cases covering both common usage patterns and edge cases. This testing will be conducted across multiple browsers (Chrome, Firefox, Safari, Edge) and devices (desktop, tablet, mobile) to ensure consistent functionality.

Performance testing will measure load times, resource usage, and responsiveness under various conditions, including simulated high traffic scenarios. Security testing will include vulnerability scanning, penetration testing, and code reviews focused on identifying security weaknesses.

Accessibility testing will verify compliance with WCAG 2.1 AA standards, ensuring that the website is usable by people with a wide range of abilities. This testing will include both automated checks and manual testing with screen readers and other assistive technologies.

User acceptance testing will involve NetHope stakeholders reviewing the implementation against their requirements and providing feedback on usability and functionality. This collaborative testing approach ensures that the website not only meets technical specifications but also addresses the practical needs of NetHope and its users.

Any issues identified during testing will be documented, prioritized, and addressed according to their severity and impact on core functionality. Our iterative development approach allows for continuous improvement throughout the development phase, with regular deployments to the staging environment for review and feedback.

Estimated workload and duration

WORKLOAD		DURATION
70 person-days		35 working days

Role	Days	Activities
Project Manager	10	Sprint planning, stakeholder coordination, progress monitoring, risk management
UX Designer	5	Design refinement, asset preparation, UI implementation support
Lead Web Developer	25	Theme development, custom functionality implementation, integration work
Support Developer	20	Component development, testing support, bug fixes
Test Engineer	10	Test planning, execution, quality assurance, documentation
Total	70 person-days	Duration: 35 working days

Deliverables

- **Functional Development Environment** including:
 - Configured staging server
 - Version control repository
 - Automated deployment workflows
 - Development standards documentation
- **Implemented WordPress Theme** including:
 - Responsive layout system
 - Header and footer components
 - Page templates for all content types

- Navigation systems
- **Custom Functionality Modules** including:
 - Campaign Monitor integration
 - Geo-location features
 - Custom post types and taxonomies
 - Enhanced search functionality
- **Performance Optimization Report** including:
 - Benchmark results
 - Optimization measures implemented
 - Recommendations for ongoing performance monitoring
- **Security Implementation Documentation** including:
 - Security measures implemented
 - Administration guidelines
 - Vulnerability assessment results
- **Testing Documentation** including:
 - Test plans and cases
 - Test results and issue logs
 - Resolution documentation

Upon completion of the Development Phase, the website will be functionally complete and ready for final deployment to the production environment in Phase 4.

IV.4 Phase 4: Deployment and Launch

Objectives

The Deployment and Launch Phase aims to successfully transition the enhanced website from development to production while ensuring:

- **Seamless migration** of content from the current website to the new platform
- **Minimal disruption** to NetHope's online presence during transition
- **Comprehensive knowledge transfer** to NetHope's team
- **Thorough documentation** of the system for future maintenance
- **Post-launch verification** of all functionality in the production environment

Description

The Deployment and Launch Phase represents the culmination of the project, where all development work is finalized, thoroughly tested, and moved to the production environment. This phase consists of five carefully orchestrated steps designed to ensure a smooth transition.

Activity 4.1: Pre-deployment testing and quality assurance

Before deploying to the production environment, we conduct a final, comprehensive round of testing on the staging environment to ensure that all functionality works as expected and that the website is ready for public access.

This testing includes a full regression test of all website features to verify that recent changes haven't affected previously working functionality. We perform compatibility testing across all target browsers (Chrome, Firefox, Safari, Edge) and devices (desktop, tablet, and various mobile devices) to confirm consistent user experience.

Performance testing is conducted under conditions that simulate production traffic, ensuring the website maintains responsiveness under expected load. Security testing includes a final vulnerability scan and penetration testing to identify and remediate any security issues before deployment.

We also conduct a content readiness assessment, reviewing all pages to ensure proper formatting, accurate links, and correct display of images and media. SEO verification confirms that all pages include proper metadata, structured data, and canonical tags to maintain search engine visibility during the transition.

Finally, we perform an acceptance review with NetHope stakeholders, allowing them to sign off on the final implementation before deployment. Any issues identified during pre-deployment testing are prioritized and addressed before proceeding.

Activity 4.2: Content migration and final preparation

With testing complete, we proceed to the migration of content from the current website to the new platform. Our content migration approach balances automation with manual verification to ensure accuracy and completeness.

For structured content like posts, pages, and media files, we use WordPress's native export/import functionality combined with custom migration scripts to transfer content while preserving relationships, metadata, and taxonomies. Custom post types require specialized migration procedures to ensure proper mapping to the new data structures.

SEO considerations are paramount during migration, with careful attention to URL structures to prevent broken links. We implement appropriate redirects for any URLs that need to change, ensuring that search engine rankings and bookmarks continue to function. We also preserve and transfer SEO metadata including titles, descriptions, and custom fields.

Media assets require special handling during migration. We process images to optimize them for the new responsive design, implementing modern formats and size variations as needed. Documents and downloadable resources are cataloged and transferred with appropriate permissions and metadata.

After automated migration, we conduct a thorough manual review of migrated content, verifying formatting, links, and visual presentation. This hybrid approach ensures both efficiency and quality in the migration process.

Activity 4.3 : Production deployment

The actual deployment to the production environment follows a carefully planned procedure designed to minimize downtime and risk.

We begin by implementing a maintenance mode for the current website, displaying a user-friendly message indicating that updates are in progress. This maintenance window is scheduled for a time of minimal traffic based on NetHope's analytics data, typically late evening or early morning hours.

Database migration comes first, with the new database structure deployed to the production environment and populated with the migrated content. File system deployment follows, with theme files, plugins, and media assets transferred to the production server according to our deployment plan.

Configuration updates include setting environment-specific variables, security parameters, and integration credentials for the production environment. We implement proper caching configurations, CDN settings, and server optimizations to ensure optimal performance from the first moment of launch.

Before deactivating maintenance mode, we perform rapid verification checks on key pages and functionalities to confirm that the deployment was successful. Once verified, we deactivate maintenance mode, making the new website publicly accessible.

Immediately following deployment, we conduct post-deployment verification, checking critical paths and functionality in the production environment to catch any issues that might only appear in production. We maintain a rapid response team on standby during the first 24 hours after deployment to address any unexpected issues that might arise.

Activity 4.4: Staff training and knowledge transfer

With the new website successfully deployed, we conduct comprehensive training for NetHope staff to ensure they can effectively manage and maintain the platform.

Administrator training focuses on the technical aspects of website management, including security procedures, plugin updates, backup processes, and performance monitoring. This training is tailored to NetHope's IT staff and includes hands-on exercises in a safe training environment.

Content manager training covers the day-to-day operations of updating website content, creating new pages, managing media, and utilizing the custom functionality developed for the project. This training is designed for communications staff and emphasizes practical workflows for common tasks.

We deliver both formal training sessions via video conferencing and supplementary training materials including step-by-step guides, video tutorials, and reference documentation. Training is conducted in small groups to ensure personalized attention and ample opportunity for questions and practice.

Beyond formal training, we provide hands-on assistance during the initial period after launch, helping staff with their first real-world tasks on the new system. This supported transition period bridges the gap between training and independent operation.

Activity 4.5: Documentation and handover

The final step in the Deployment and Launch Phase is the creation and delivery of comprehensive documentation and formal handover of the project.

Technical documentation includes system architecture diagrams, database schemas, code documentation, and integration specifications. This documentation is designed for technical staff who may need to maintain or extend the system in the future.

User documentation provides detailed guides for content management, explaining how to perform common tasks with step-by-step instructions and screenshots. This documentation serves as both a training resource and an ongoing reference for NetHope staff.

Maintenance documentation outlines recommended procedures for routine maintenance, including backup schedules, update procedures, and security monitoring. It also includes troubleshooting guides for common issues and emergency procedures for critical situations.

The formal handover includes a comprehensive project closure meeting where we review all deliverables, ensure all requirements have been met, and address any outstanding questions or concerns. We also establish a

transition plan for post-launch support, defining how issues will be reported and addressed during the warranty period.

As part of our commitment to NetHope's long-term success, we provide recommendations for future enhancements and outline a roadmap for ongoing website evolution. This forward-looking guidance helps NetHope plan for sustained digital excellence beyond the initial project.

Estimated workload and duration

WORKLOAD		DURATION
25 person-days		10 working days

Role	Days	Activities
Project Manager	5	Deployment coordination, stakeholder management, handover facilitation
UX Designer	2	Visual verification, content migration support, training materials preparation
Lead Web Developer	8	Migration scripting, deployment execution, technical documentation
Support Developer	5	Content migration, post-deployment fixes, quality assurance
Test Engineer	5	Pre-deployment testing, post-deployment verification, documentation review
Total	25 person-days	Duration: 10 working days

Deliverables

- **Migration Report** documenting:
 - Content migration statistics
 - Resolved migration issues
 - URL mapping and redirect implementation
 - SEO preservation measures
- **Deployment Documentation** including:
 - Deployment procedure and checklist
 - Configuration settings
 - Server environment specifications
 - Post-deployment verification results
- **Training Materials** including:
 - Administrator guides
 - Content management tutorials
 - Video training sessions
 - Quick reference guides
- **System Documentation** including:
 - Technical architecture documentation
 - Code documentation
 - Database schema
 - Third-party integration specifications
 - Security implementation details
- **Maintenance Guide** outlining:
 - Routine maintenance procedures
 - Backup and recovery processes

- Update protocols
- Performance monitoring guidelines
- Security monitoring recommendations

The successful completion of the Deployment and Launch Phase marks the transition of the enhanced website into operational use, with NetHope staff equipped with the knowledge and resources to maintain and extend the platform.

IV.5 Phase 5: Closure

Objective

The Closure Phase serves as the formal conclusion of the project, ensuring that:

- **All project deliverables** are properly finalized and accepted
- **Knowledge transfer** is complete and verified
- **Project documentation** is comprehensive and archived
- **Performance evaluation** is conducted to measure project success
- **Transition to ongoing support** is smoothly executed

Description

The Closure Phase represents the formal conclusion of the project, where we ensure that all deliverables meet NetHope's expectations and that the transition to operational status is complete. This phase consists of three structured steps designed to bring the project to a successful close while establishing the foundation for future support and enhancement.

Activity 5.1: Final deliverable review and acceptance

The first step in closing the project is a comprehensive review of all deliverables to ensure they meet the agreed requirements and quality standards.

We begin with a systematic audit of all project deliverables, comparing them against the original requirements and success criteria established at the project's outset. This audit covers the implemented website functionality, documentation, training materials, and any other deliverables specified in the project scope. For each deliverable, we verify completeness, quality, and alignment with NetHope's expectations.

Next, we conduct a final quality assurance review, which includes both technical and functional aspects of the website. The technical review examines code quality, performance metrics, security implementations, and compliance with web standards. The functional review confirms that all features work as expected across different devices and browsers, with special attention to any issues that might have emerged since the production deployment.

We also perform a post-launch analytics review, examining user behavior data from the first days or weeks after launch. This analysis helps identify any usability issues or unexpected patterns that might require attention before project closure. We prepare a summary of these findings with recommendations for any necessary adjustments.

Finally, we facilitate a formal acceptance process with NetHope stakeholders. This process includes a comprehensive walkthrough of all deliverables, addressing any questions or concerns, and documenting formal acceptance. Any outstanding minor issues are cataloged with an agreed plan for resolution, either as part of the project closure or through subsequent support arrangements.

Activity 5.2: Data migration execution

With deliverables accepted, we conduct a thorough evaluation of the project's performance against its objectives, timelines, and quality targets.

We begin with a comprehensive review of the project schedule, comparing planned versus actual timelines for each phase and analyzing the causes of any variances. This analysis helps identify successful planning approaches as well as areas for improvement in future projects. We document these findings in a schedule performance report that includes recommendations for future estimation and planning practices.

Next, we evaluate the quality of the delivered solution against the defined quality criteria. This evaluation considers technical quality (code structure, performance, security), user experience quality (usability, accessibility, visual design), and content quality (organization, clarity, completeness). We compile quality metrics from throughout the project lifecycle to demonstrate trends and improvements.

We also conduct a scope management review, examining how well the project adhered to its defined scope and how effectively change requests were handled. This review documents approved changes, their impact on the project, and the effectiveness of the change management process.

Finally, we facilitate a lessons learned session with both the MK BA team and NetHope stakeholders. This collaborative session identifies successful practices that should be continued, challenges that were encountered, and opportunities for improvement in future projects. The insights from this session are documented in a lessons learned report that provides valuable guidance for both organizations.

Activity 5.3: Transition to support and project closure

The final step ensures a smooth transition from project mode to ongoing operational support and maintenance.

First, we establish a formal transition plan that outlines how support and maintenance responsibilities will be handled after project closure. This plan defines support levels, response times, issue reporting procedures, and escalation paths. It also clarifies the boundaries between warranty support (covering issues with the implemented solution) and enhancement requests (new features or significant changes).

Next, we conduct a final knowledge transfer session with NetHope's technical and content teams. This session ensures that all necessary information has been transferred and that NetHope staff are comfortable with their responsibilities for ongoing maintenance and support. We address any remaining questions and provide guidance on best practices for system administration and content management.

We then prepare and deliver the final project report, which provides a comprehensive summary of the project, including objectives, approach, achievements, challenges, and recommendations for future enhancements. This report serves as both a historical record of the project and a foundation for planning future initiatives.

Finally, we conduct a formal project closure meeting with key stakeholders from both MK BA and NetHope. This meeting includes a review of the final project report, acknowledgment of project achievements, recognition of team contributions, and official declaration of project closure. We also use this meeting to establish channels for ongoing communication during the warranty period and to discuss potential future collaboration opportunities.

Estimated workloads and deadlines

WORKLOAD	DURATION
7 person-days	5 working days

Role	Days	Activities
Project Manager	4	Deliverable review coordination, performance evaluation, closure meeting facilitation
UX Designer	1	Visual quality verification, UX evaluation, design documentation finalization
Lead Web Developer	1	Technical review, code documentation finalization, support transition
Test Engineer	1	Final quality verification, testing documentation finalization
Total	7 man-days	Duration: 5 working days

Deliverables

- **Final Acceptance Document** confirming:
 - All deliverables have been completed to satisfaction
 - Outstanding items and resolution plan (if any)
 - Formal client acceptance signatures
- **Project Performance Report** including:
 - Schedule performance analysis
 - Quality metrics and evaluation
 - Scope management assessment
 - Budget performance summary
- **Lessons Learned Report** documenting:
 - Successful practices to continue
 - Challenges encountered and solutions implemented
 - Recommendations for future projects
 - Stakeholder feedback summary
- **Support Transition Plan** outlining:
 - Support responsibilities and procedures
 - Warranty terms and conditions
 - Issue reporting and escalation processes
 - Scheduled maintenance activities
- **Final Project Report** summarizing:
 - Project objectives and scope
 - Approach and methodology
 - Key achievements and deliverables
 - Challenges and how they were addressed
 - Recommendations for future enhancements

The Closure Phase ensures that the project is formally completed with all deliverables accepted, knowledge successfully transferred, and a clear path established for ongoing support and future enhancements. This structured closure process provides both MK BA and NetHope with the documentation and insights needed to build on the project's success.

V. PROJECT TEAM AND SCHEDULE

V.1 Project Team

MK BA has assembled an experienced team of professionals with specialized expertise in WordPress development, UI/UX design, and digital communications. Our team members have extensive experience working with international organizations and nonprofit clients, ensuring a deep understanding of NetHope's specific needs and context.

Role	Expert	Experience	Key responsibilities	Relevant expertise
Project Manager	Joel KUATE MABOU	12 years	- Overall project oversight and coordination - Client communication and stakeholder management - Sprint planning and resource allocation - Quality assurance and timeline adherence	- PMP Certified - Led UNDP Madagascar website project - Managed 12 projects of website - ISO 27001 certified (security expertise)
UX Engineer	Marlyse TEUNOU	10 years	- User interface design and wireframing - Brand alignment and visual consistency - Responsive design implementation - User testing and UX optimization	- Designed UNDP Guinea web platform - UX lead for Bange Bank website - Healthcare UI design for UNICEF projects - Expert in Figma and Adobe XD
Business Analyst	Claude Cyriac KOUM	14 years	- Requirements gathering and analysis - System architecture design - Technical specification development - Performance optimization strategy	- CISA certified (audit expertise) - Led UNICEF m-Health platform design - WebSec and InfoSec specialist


Role	Expert	Experience	Key responsibilities	Relevant expertise
				• ITIL v3 certified (IT service management)
Full Stack Developer	Marius KEMAYOU	10 years	• WordPress theme development • Custom plugin development • API integration (Campaign Monitor) • Database optimization	• WordPress specialist (8+ years) • Developed UNDP Madagascar platform • Expert in Laravel, React, and PHP • Implemented geo-location features
Full Stack Developer	Louis YOUNBI	11 years	• Front-end development • Performance optimization • Security implementation • Cross-browser compatibility	• Developed UNDP Guinea platform • Implemented DigiBanking solutions • Expert in JavaScript/TypeScript • Specialized in website optimization
Test Engineer	Francis KAMGA	7 years	• Quality assurance testing • Regression and UAT testing • Performance testing • Security vulnerability assessment	• Testing lead for UNICEF projects • PageSpeed optimization specialist • Automated testing implementation

Role	Expert	Experience	Key responsibilities	Relevant expertise
				• Cross-platform compatibility testing
Backstopper	Franck FOWA	8 years	• Administrative coordination • Contract management • Resource planning • Quality control	• M&E specialist • Nonprofit project management • Remote team coordination • Documentation specialist


Our team's expertise extends beyond technical skills to include substantial experience working with international organizations and nonprofits. This ensures we not only deliver technical excellence but also understand the communication and operational needs specific to NetHope's environment.

V.2 Project Organization Chart

Our project organization structure is designed to ensure clear accountability, effective communication, and comprehensive coverage of all project aspects. The structure facilitates efficient decision-making while maintaining strong coordination between technical implementation and stakeholder needs.

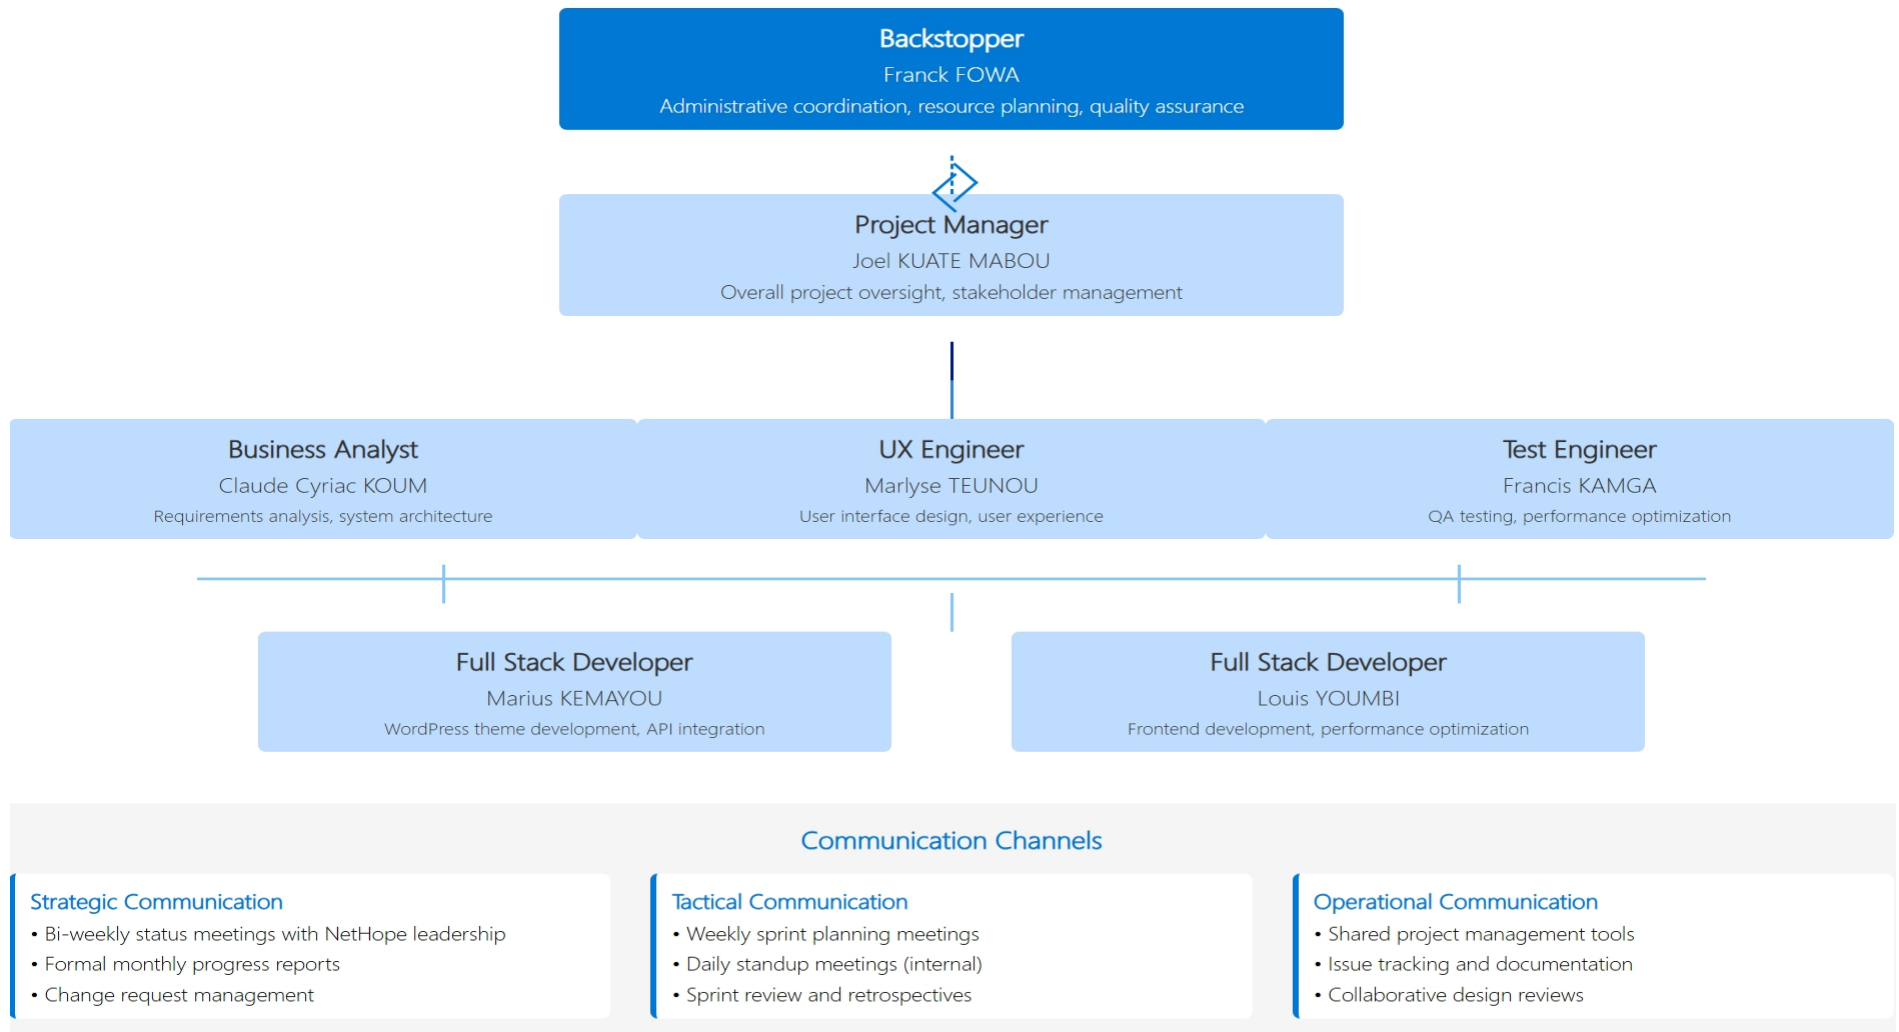

V.3 Project Schedule

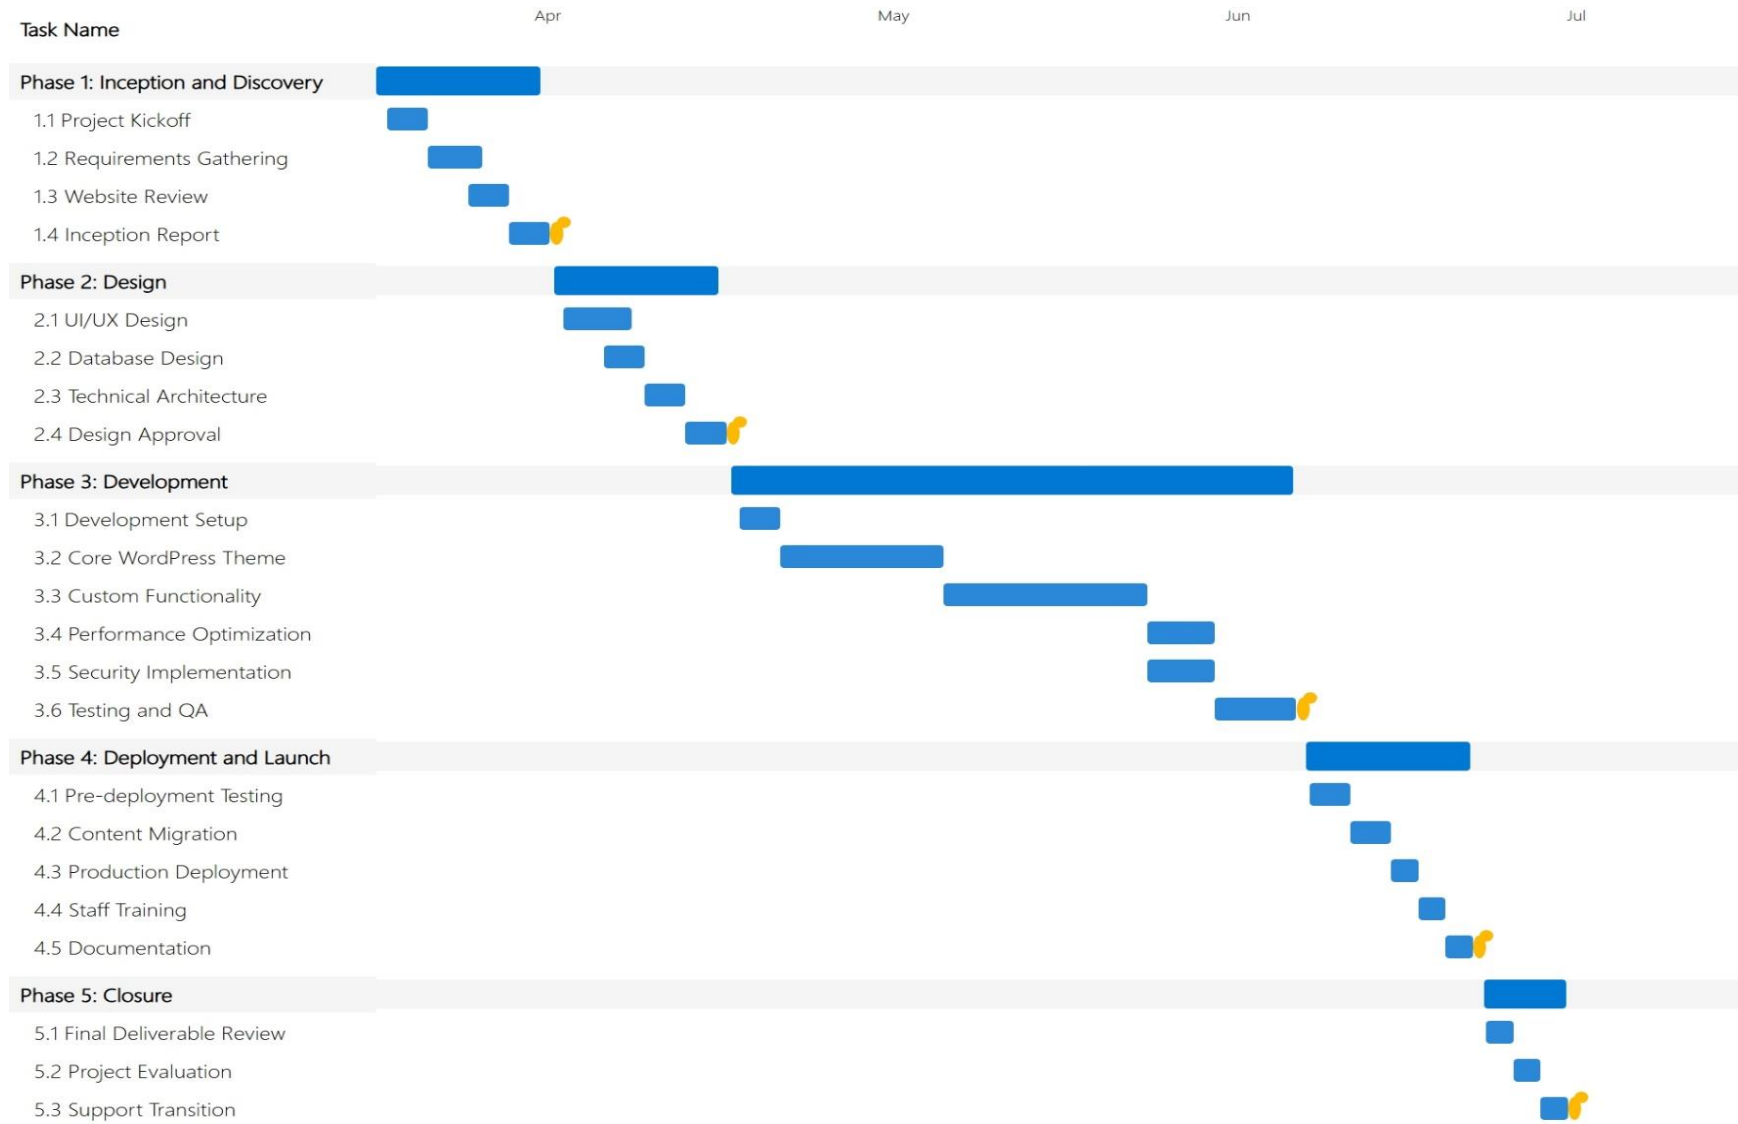

V.3.1 Resource allocation matrix

Team Member	Phase 1 (10 days)	Phase 2 (10 days)	Phase 3 (35 days)	Phase 4 (10 days)	Phase 5 (5 days)	Total Days
Project Manager	5	3	10	5	4	27
UX Engineer	3	10	5	2	1	21
Business Analyst	4	4	5	2	0	15
Full Stack Developer 1	0	1	25	8	1	35
Full Stack Developer 2	0	0	20	5	0	25
Test Engineer	3	2	10	5	1	21
Program Coordinator	0	0	10	3	0	13

V.3.1 Key milestones

#	Milestone	Temporary date	Deliverables
M1	Project Inception Complete	April 18, 2025	• Approved Inception Report • Agreed requirements and scope • Technology recommendations
M2	Design Approval	May 2, 2025	• Approved UI/UX designs • Technical architecture document • Database design document
M3	Development Complete	June 20, 2025	• Fully functional staging environment • Completed theme implementation • All custom functionalities implemented • QA testing complete
M4	Website Launch	July 4, 2025	• Live website deployment • Migration complete • Staff training delivered • System documentation delivered
M5	Project Closure	July 11, 2025	• Final project report • Client acceptance sign-off • Support transition complete • Warranty period begins

VI. EXPERTS CVs

VI.1 CV of the Project Manager

1. **Proposed role in the project:** Project Manager
2. **Names :** KUATE MABOU Joel
3. **Occupation :** Software Engineer
4. **Total experience:** 12 years
5. **Nationality:** Cameroonian
6. **Education:**

Institution	Period	Degree(s) or Diploma(s) obtained:
National Advanced School of Engineering of Yaoundé, Cameroon	2013	Computer Engineering Design Engineer
ESSEC Douala, Cameroon	2017	Master of Business Administration

7. Certification

- ISO 27001 (Information Security Management System)
- Project Management Professional (PMP)

8. Language skills: Indicate competence on a scale of 1 to 5 (1 - excellent; 5 - basic)

Language	Reading	Speaking	Writing
English	1	1	1
French	1	1	1

9. Skills: (e.g., Computer literacy, etc.)

Domain	Tools/skills
Project management	PMBOK approach, Agile with SCRUM, PMBOK Guide, MS Project, Jira, Trello
Databases	MySQL, PostgreSQL, MS SQL Server, Oracle
Web development	HTLM, CSS + Bootstrap, Javascript + ReactJs + AngularJs, NodeJs, Electron Js, Java, Spring, Python + Django, PHP+ Symfony, C#, ASP.Net, React Native
Statistics, data analysis, business intelligence	R, Microsoft Power BI, Microsoft SQL Server Integration Services, Analysis Services, Reporting Services, Talend Open Studio For Data Integration,
Data visualization	React Google Charts, D3.js, Microsoft Power BI, Tableau
Geographical Information Systems	ArcGIS, PostGIS, Google Maps, Bing Maps, Leaflet Map
Collaboration	Git, MS Teams, Skype for Business, Zoom, Cisco Jabber
Networking	Routing et Switching
Information security	Pen Testing, Gouvernance sécurité IT
Office works	Suite Microsoft Office, Google Docs
Other	IT support, Information systems audits

10. Relevant Work Experience

Date	Country	Company	Position	Description
January – May 2024	Madagascar	UNDP Madagascar Fanomezantsoa ANDRIANAIVOARIVON fanomezantsoa.andrianaivoarivon@undp.org	Project Manager	Development of an Environment Management Information System
September 2023 – March 2024	Guinea	UNDP Guinea Mouna El JAOUHARI eljaouhari@un.org	Project Manager	Web platform for the coordination of development partners of the Republic of Guinea
July 2023 – January 2024	Cameroon	UNICEF Cameroon	Technical Lead	Development of an “m-Hhealth” initiative aiming to strengthen compliance and retention in care of pregnant/breast-feeding women and adolescents living with HIV (ongoing project)
December 2023 – March 2024	Cameroon	Bange Bank Cameroon Hugues Arnaud TENKEU +237 657 10 87 10	Technical Lead	Design, Development and Deployment of the corporate website of Bange Bank Cameroon
Since January 2023	Cameroon	MK WBC	Project Manager	LegalApp – web application for managing criminal records, nationality certificates and judicial files
July 2022 – March 2023	Cameroon	UNICEF Cameroun Jean Jacques NDONGBANG jndongbang@unicef.org	Lead Developer	Design and implementation of the pilot Management Information System (MIS) for the Unified Social Register in Cameroon
January 2020 – December 2023	Cameroon	MK WBC Lionnel KAMGA Lionnel.kamga@mk-wbc.com	Project Manager	MKonnected – Networking, consulting and employment support platform

Date	Country	Company	Position	Description
November 2020 – January 2022	Cameroon	Oversee Advising Group Hubal PFUMTCHUM hp@myoag.org	IT Consultant	Online dashboard including an interactive map, for the visualization of reinforced monitoring-evaluation indicators and conflict-sensitive analysis for AFD in Cameroon Funded by Agence Française de Développement
October 2020 – March 2021	Cameroon/Central African Republic	Oversee Advising Group Hubal PFUMTCHUM hp@myoag.org	IT Consultant	“Third Party Monitoring” for 52 projects funded by UNICEF in Central African Republic Funded by UNICEF
September 2018 – September 2024	Cameroon	Nokia Cameroun Romulus DEFO, +237 696 52 32 43	Project Manager – Networks and Telecoms	Construction of transmission links to increase capacity necessary for the deployment of 3G and 4G
June 2018 – June 2022	Cameroon	Multiples clients : Guigui SARL, K2R Solutions, 3SMI, The Best Group (TBG), Smart Consulting Group (SCG) Rodrigue KOM (K2R Solutions), +237 675 95 65 83	IT Consultant	Multiple web development projects: – Implementation of online learning platform – Implementation of electronic archiving systems – Implementation of budget management application
October 2015 – August 2018	Cameroon	Nokia Cameroun Romulus DEFO, +237 696 52 32 43	Deputy Project Manager – Networks and Telecoms	Construction of transmission links to increase capacity necessary for the deployment of 3G and 4G
June 2015 – August 2018	Cameroon	MK WBC Lionnel KAMGA Lionnel.kamga@mk-wbc.com	IT Manager	– Managed multiple IT projects – Contributed to the development of the IT strategy of the company
August 2014 – July 2015	Cameroon	Alcatel-Lucent Cameroun	Quality Auditor and Data Manager	– Audit of telecom sites in the Orange Cameroon network to verify that the equipment is properly installed and configured – Analysis of deployment data to improve site quality

Date	Country	Company	Position	Description
		Paul YOUNBI +237 696 31 07 72		
July 2013 – July 2014	Cameroon	Interface SA Dimitri HAPPI +237 675 98 74 70	Business Intelligence (BI) Engineer	Sesame BI project - Design and implementation of the Business Intelligence layer (Business intelligence, data analysis) of an ERP software
March 2013 – June 2013	Cameroon	GRID Engineering Jean Paul EBODE +237 650 20 49 35	Software Developer	Multiple projects

11. Evidences


Engineering diploma



MBA diploma



ISO 27001 (Information Security Management System) Certificate

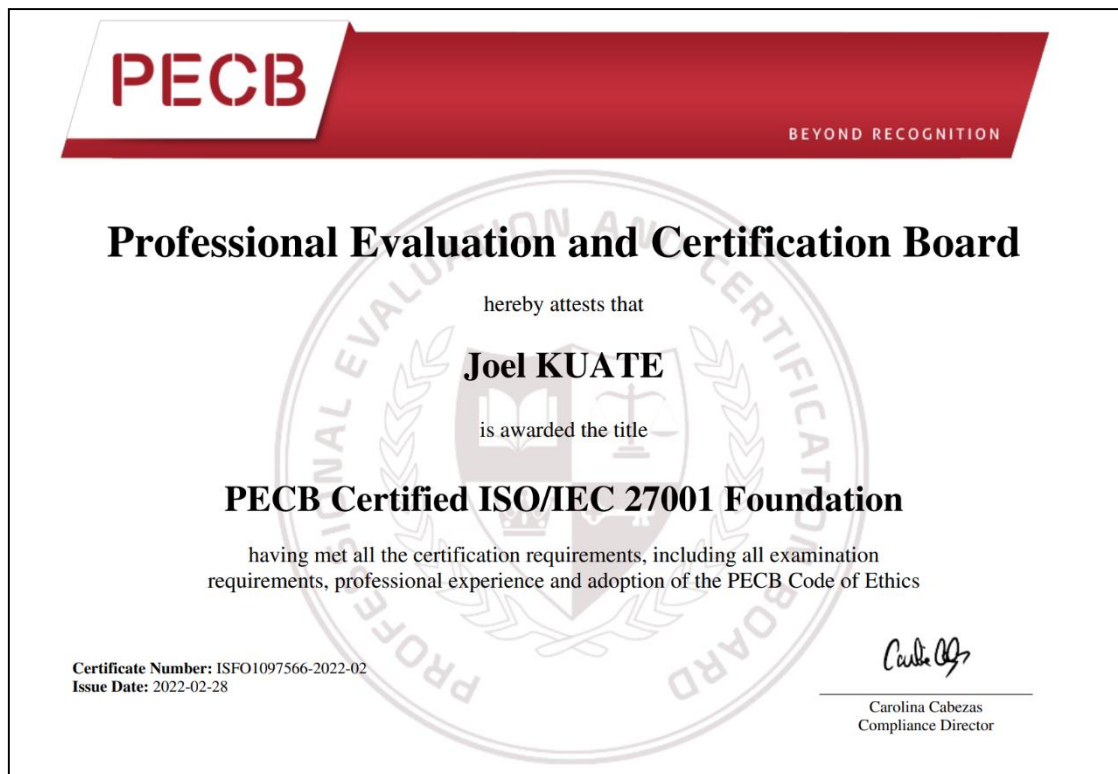

PMP (Project Management) Certificate



Certificates of good completion



ATTESTATION DE BONNE EXECUTION

Je soussigné, Monsieur **ANDRIANAIVOARIVONY Fanomezantsoa**, Coordonnateur du projet CCCD-Rio au PNUD Madagascar atteste par la présente que Monsieur **KUATE MABOU Joel**, consultant international, a conduit en qualité de **Chef de mission** du cabinet MK BA le projet de **Développement d'un Système d'Information de Gestion de l'Environnement (SIGE)** pour Madagascar, entre janvier et mai 2024.

La mission a été menée à bien avec sérieux et professionnalisme, dans le respect des délais, avec notre pleine satisfaction et appréciation.

La présente attestation est délivrée pour servir et valoir ce que de droit.

Fait à Antananarivo le 31 mai 2024

Fanomezantsoa Andrianaivoarivony

ANDRIANAIVOARIVONY Fanomezantsoa
Coordonnateur Projet CCCD-Rio / PNUD



ATTESTATION DE BONNE EXECUTION

Je soussignée, Madame **Mouna El JAOUHARI**, Cheffe de Bureau de la Coordination Résidente du Système des Nations Unies en Guinée atteste par la présente que Monsieur **KUATE MABOU Joel**, consultant international, a conduit en qualité de **Chef de mission** du cabinet MK BA le projet de **CREATION DU SITE WEB POUR LA PLATEFORME DE CONCERTATION ET DE COORDINATION DES PTF EN GUINEE**, entre septembre 2023 et avril 2024.

La mission a été menée à bien avec sérieux et professionnalisme, dans le respect des délais, avec notre pleine satisfaction et appréciation.

La présente attestation est délivrée pour servir et valoir ce que de droit.

Fait à Conakry le 31 mai 2024



Mouna El JAOUHARI



**BANGE BANK
CAMEROUN**
La Banque de tous

ATTESTATION DE BONNE EXECUTION

Nous soussignés,

BANGE BANK CAMEROUN, Société Anonyme avec Conseil d'Administration au capital de FCFA dix milliards (10.000.000.000) dont le siège social est situé au Centre Commercial du Hilton, boulevard du 20 mai, Yaoundé, BP 34692, attestons par la présente que **M. KUATE MABOU Joel, Consultant en informatique** pour la firme The Best Group (TBG), a fourni de l'expertise en développement et déploiement web dans le cadre du projet de " **CONCEPTION, DESIGN, DEVELOPPEMENT ET MISE EN PRODUCTION DU SITE WEB INSTITUTIONNEL DE BANGE BANK CAMEROUN**", accessible via l'adresse <https://www.bangecmr.com>.

La mission a été menée à bien avec sérieux et professionnalisme, dans le respect des délais, avec notre pleine satisfaction et appréciation.

La présente attestation est délivrée pour servir et valoir ce que de droit.



Nom, signature, cachet

**BANGE BANK
CAMEROUN**

Siège social: Centre commercial du Hilton,
Boulevard du 20 mai,
B.P. 34692 Yaoundé-Cameroun
RCCM : YAO/2020/BI/1150
NIU : M082015240414Y
info@bangecmr.com
www.bangecmr.com

Capital social 10.000.000.000 FCFA

Paul YOUNBI
Field Service Manager, Nokia Cameroun
Douala, Cameroun
Tel : +237 696 310 772

Objet : Recommandation pour M. KUATE MABOU Joël

J'ai collaboré avec Monsieur KUATE MABOU Joël chez Nokia Cameroun à Douala, qui y travaille depuis plus de 6 ans et que j'ai supervisé pendant 1 an à son poste de Chef de Projet Transmission. Son rôle consistait en l'initiation, la planification, le monitoring et la clôture des projets de transmission exécutés pour le client Orange Cameroun.


Monsieur KUATE est un collaborateur appliqué qui suit ses projets de façon correcte et atteint les objectifs opérationnels et financiers à lui confiés. Il sait gérer la pression et utiliser les outils informatiques pour une meilleure communication, un meilleur suivi des activités des projets et pour accroître son efficacité dans son travail. Par ailleurs, il sait très bien interfacer avec les parties prenantes aux différents projets (client, équipe projet, utilisateurs finaux B2B), tant dans des réunions qu'à travers des rapports d'avancement.

Je le recommanderais pour des fonctions similaires dans des entreprises et organisations privées et publiques, nationales et internationales.

Paul YOUNBI



05/03/2021



3 S.M.I

Société de Maintenance des Salles
Spécialisées et Industrielles

DIRECTION GENERALE

B.P. 696 Bafoussam

Tél. : 683 02 64 98

Tél. : 671 08 90 43

E-mail : ndjomirichard3smi@yahoo.fr

ELECTRICITE – ELECTRONIQUE – GENIE CIVIL – TELECOMMUNICATIONS – TRANSPORT

ATTESTATION DE BONNE EXECUTION

Nous soussignés, la Société de Maintenance des Salles Spécialisées et Industrielles (3SMI), société de services basée à Bafoussam au Cameroun et offrant des prestations dans les domaines de l'électricité, de l'électronique, des télécommunications, du génie civil et du transport, attestons par la présente que Monsieur Joel KUATE a collaboré avec nous en tant que Consultant IT dans le cadre de la mise d'un système de suivi des opérations et d'aide à la décision.

Le consultant a fourni les livrables conformément à nos prescriptions techniques, dans les délais contractuels et nous a donné entière satisfaction.

Nous le félicitons pour son professionnalisme, pour son engagement et pour les efforts fournis.

Cette attestation a été délivrée pour servir et valoir ce que de droit.

Fait à Bafoussam, le 26 mai 2020.



NDJOMI NANA Blondel, Directeur Général

Capital social : 10 000 000 F CFA
Contribuable : M011512332079D

N° STATISTIQUE : 5921301G RC 24/99-2000
Régime Réel CB : 03011000062-60UBA Bafoussam

VI.2 CV of the UX Engineer

1. **Proposed role in the project:** UX Engineer
2. **Names:** TEUNOU Marlyse
3. **Nationality:** Cameroonian
4. **Occupation:** Web/UX Designer
5. **Total experience :** 11 years
6. **Education:**

Institution	Period [Date from – Date to]	Degree(s) or Diploma(s) obtained:
Higher Institute of Technology and Management (a school of University of Yaoundé II Soa)	2016 - 2017	Bachelor Degree in Computer Science

7. **Language skills:** Indicate competence on a scale of 1 to 5 (1 - excellent; 5 - basic)

Language	Reading	Speaking	Writing
English	1	1	1
French	1	1	1

8. **Skills:** (e.g., Computer literacy, etc.)
 - UX/UI Design
 - Motion Design
 - Frontend design and development
 - Digital Marketing
 - Communication tools
 - Digital identity

9. Relevant Work Experience:

Date from – Date to	Location	Organization	Position	Description
January – May 2024	Madagascar	UNDP Madagascar	UX/UI Designer (for the firm MK BA)	Development of an Environment Management Information System
September 2023 – March 2024	Guinea	UNDP Guinea	UX/UI Designer (for the firm MK BA)	Web platform for the coordination of development partners of the Republic of Guinea
July 2023 – January 2024	Cameroon	UNICEF Cameroon	UX/UI Designer (for the firm MK BA)	Development of an “m-Hhealth” initiative aiming to strengthen compliance and retention in care of pregnant/breast-feeding women and adolescents living with HIV (ongoing project)
December 2023 – March 2024	Cameroon	Bange Bank Cameroon	UX/UI Designer (for the firm TBG)	Design, Development and Deployment of the corporate website of Bange Bank Cameroon
July 2022 – March 2023	Cameroon	UNICEF Cameroun	UX/UI Designer (for the firm MK BA)	Design and implementation of the pilot Management Information System (MIS) for the Unified Social Register in Cameroon
July 2020-March 2021	Cameroon	MK BA	Motion & Graphics Designer	Design of communication tools of the company Realization of solutions presentation videos
April 2018 – June 2020	Cameroon	MK BA	Graphics Designer / UX Developer	Development of MK Monitoring and Evaluation, a web and mobile platform to perform Monitoring and Evaluation of projects funded by international donors
May 2014 – July 2024	Cameroun	Novazen	Frontend Developer Web Integrator Web Project Manager	Developing websites for multiple clients • Frontend development • Web integration • Project management

VI.3 CV of the Analyst

1. **Proposed role in the project:** Analyst
2. **Names :** KOUM Claude Cyriac
3. **Nationality:** Cameroonian
4. **Occupation :** Software Engineer and Project Manager
5. **Total experience :** 17 years
6. **Education:**

Institution	Period [Date from – Date to]	Degree(s) or Diploma(s) obtained:
National Advanced School of Engineering of Yaoundé, Cameroon	2010	Computer Engineering Design Engineer
National Advanced School of Engineering of Yaoundé, Cameroon	2007	General University Studies Diploma (DEUG)

7. **Certification**

- Project Management Professional (PMP)
- Professional Scrum Master
- Certified Information Systems Auditor (CISA)
- Cisco Certified Network Analyst (CCNA) Security
- ITIL v3

8. **Language skills:** Indicate competence on a scale of 1 to 5 (1 - excellent; 5 - basic)

Language	Reading	Speaking	Writing
English	1	1	1
French	1	1	1

9. **Skills:** (e.g., Computer literacy, etc.)

- Design, implementation and operation of information systems
- Software testing and quality assurance
- Web design and development
- IT Project Management
- Information systems audit
- Computer security
- Computer network
- IT Support

10. **Specific experience in the region:**

Country	Date from – Date to
Cameroon	Country of residence and work
Burundi	2023
France	2022

11. Relevant Work Experience:

Date	Country	Company	Position	Description
January – May 2024	Madagascar	UNDP Madagascar	Lead Developer (Consultant for MK BA)	– Development of an Environment Management Information System – Technology stack: PHP+Laravel, AngularJs, Ionic
September 2023 – March 2024	Guinea	UNDP Guinea	Lead Developer (Consultant for MK BA)	– Web platform for the coordination of development partners of the Republic of Guinea – Technology stack: PHP + Symfony, Javascript (React Js, React Native, TypeScript), CSS3 (Bootstrap 4), HTML5
Since July 2023	Douala-Cameroon	UNICEF Cameroon	Project Manager (Consultant for MK WBC)	Development of a "Mhealth" initiative aimed at strengthening the observance and retention in care of pregnant/breastfeeding women and adolescents living with HIV in four (4) health districts in Cameroon (for UNICEF Cameroon). Activities carried out: Design of the web and mobile versions of the platform The firm's technical interface with the client Technical support for developers to resolve bottlenecks and enable them to monitor their developments Coordination of the technical team (developers, statisticians, graphic designers) Coordination of platform analysis and design activities Leading meetings with the customer's project team and the internal project team Tools: ArcGIS, Leaflet Map, Java, Talend Open Studio for Data Integration, PHP+Symfony, KoboToolbox, Python, OpenIMIS, MS Office


Date	Country	Company	Position	Description
Jan 2023 – Feb 2023	Cameroon	MK WBC	Project Manager	Deployment of the Bitrix24 for the customer Smart Consulting Group ▪ Telephony ▪ Analytics
July 2022 – March 2023	Douala-Cameroon	MK WBC	Project Manager	Design and implementation of the pilot management information system for the Unified Social Register of Cameroon (for UNICEF Cameroon) Activities carried out: Coordination of platform analysis and design activities Coordination of the technical team (developers, statisticians, graphic designers) The firm's technical interface with the client Technical support for developers to resolve bottlenecks and enable them to monitor their developments Coordination of the technical team (developers, statisticians, graphic designers) Coordination of platform analysis and design activities Leading meetings with the customer's project team and the internal project team Tools: ArcGIS, Leaflet Map, Java, Talend Open Studio for Data Integration, PHP+Symfony, Kobo Toolbox, Python, OpenIMIS, MS Office
Nov 2020 -Jan 2022	Douala - Cameroon	Agence Française de Développement	IT Project Manager, Team Leader (Consultant for OAG)	Design of a map showing the development of projects financed by AFD, the technical and financial partner of the National Participatory Development Program (PNDP), for the benefit of communes in the Far North of Cameroon. Activities carried out: Coordinating the development team

Date	Country	Company	Position	Description
				Participation in the development of complex modules; Participating in the design of the indicator monitoring dashboard Interfacing with the monitoring-evaluation experts to align the application's functionalities with the needs of the assignment Tools: ArcGIS, Leaflet Map, Java, Talend Open Studio for Data Integration, PHP+Symfony, Kobo Toolbox, Python, OpenIMIS, MS Office
October 2020 – March 2021	Douala Cameroon	UNICEF Central African Republic	IT Project Manager in the mission, (Consultant for OAG)	Activities carried out: Coordinating the development team Participation in the development of complex modules; Participating in the design of the indicator monitoring dashboard Interfacing with the monitoring-evaluation experts to align the application's functionalities with the needs of the assignment User training Tools: ArcGIS, Leaflet Map, Java, Talend Open Studio for Data Integration, PHP+Symfony, KoboToolbox, Python, OpenIMIS, MS Office
2020		West African Economic and Monetary Union (WAEMU) / Union of African Shippers' Councils (UCCA)	IT Consultant	Participation as analyst in the study on the impact of the Electronic Cargo Note on the economies of Central and West Africa
2019 - 2021	Douala Cameroon	Japan International Cooperation Agency (JICA)	Consultant Computer Engineer	Activities carried out: Study on the state of digitization of public services in Cameroon
Since 2016	Douala Cameroon	Cameroon National Shippers Council	Director of Information Systems	Oversaw technical projects in alignment with organizational goals that drove over 2 billion FCFA in annual revenue Improved business applications and corporate technology processes through rigorous data collection and analysis

Date	Country	Company	Position	Description
				Managed a staff of 10 people in charge of IT production, support and engineering Fostered a culture of robust documentation of business applications and APIs to reduce company wide on-boarding time for new tools by 40% Represented the CNCC in high-level strategic meetings on behalf of Cameroon with the following organizations: UNCTAD, WTO, AACE, AIS Hub Executed over 400 Million FCFA annual budget. Reduced costs while improving the level of service. Rigorously maintained and forecasted financial budgets to ensure all technical projects were delivered on-time and on-budget Led the development of the first trade information portal of Cameroon, a project involving more than 30 administrations, 300 stakeholders, and which is ranked by International Organizations such as UNCTAD, World BANK, TRALAC as one of the best in Africa.
2014-2015	Douala Cameroon	Cameroon National Shippers Council	Manager of the Network and Infrastructure department	Maintenance and development of an extensive network across 7 sites (including one in Paris). Responsible for providing IT services, for over 10,000 users worldwide, in a 7/24/365 environment. Preparation of calls for tenders and negotiation of maintenance contracts. Implementation of Office 365 services. – Evaluating and improving existing backup and disaster recovery strategies.

Date	Country	Company	Position	Description
2011-2013	Douala Cameroon	Cameroon National Shippers Council	Network Engineer	Responsible for the design, implementation and maintenance of equipment: Cisco, Allied Telesyn, Fortigate. VPN management, endpoint security, state policy and application control, IP addresses, monitoring, antispam, etc. Monitoring all network operations and performing necessary corrective actions to restore network outages. Supervision of the infrastructure of more than 50 servers, running both Linux and Windows.
2010-2011	Douala Cameroon	Perenco	Systems Administrator	Maintenance of a fleet of more than 250 computers, 50 printers. Migration of more than 800 computers from the TOTAL CAMEROUN environment to that of PERENCO via the WSUS tool. User support. Implementation of the project to transition radio stations from analog to digital. – Windows system administration: Active Directory, design of group policies.
2010	Douala Cameroon	CITECH	Web Developer	– Development of a Project Management application based on the PMBOK Guide approach

12. Copies of diplomas

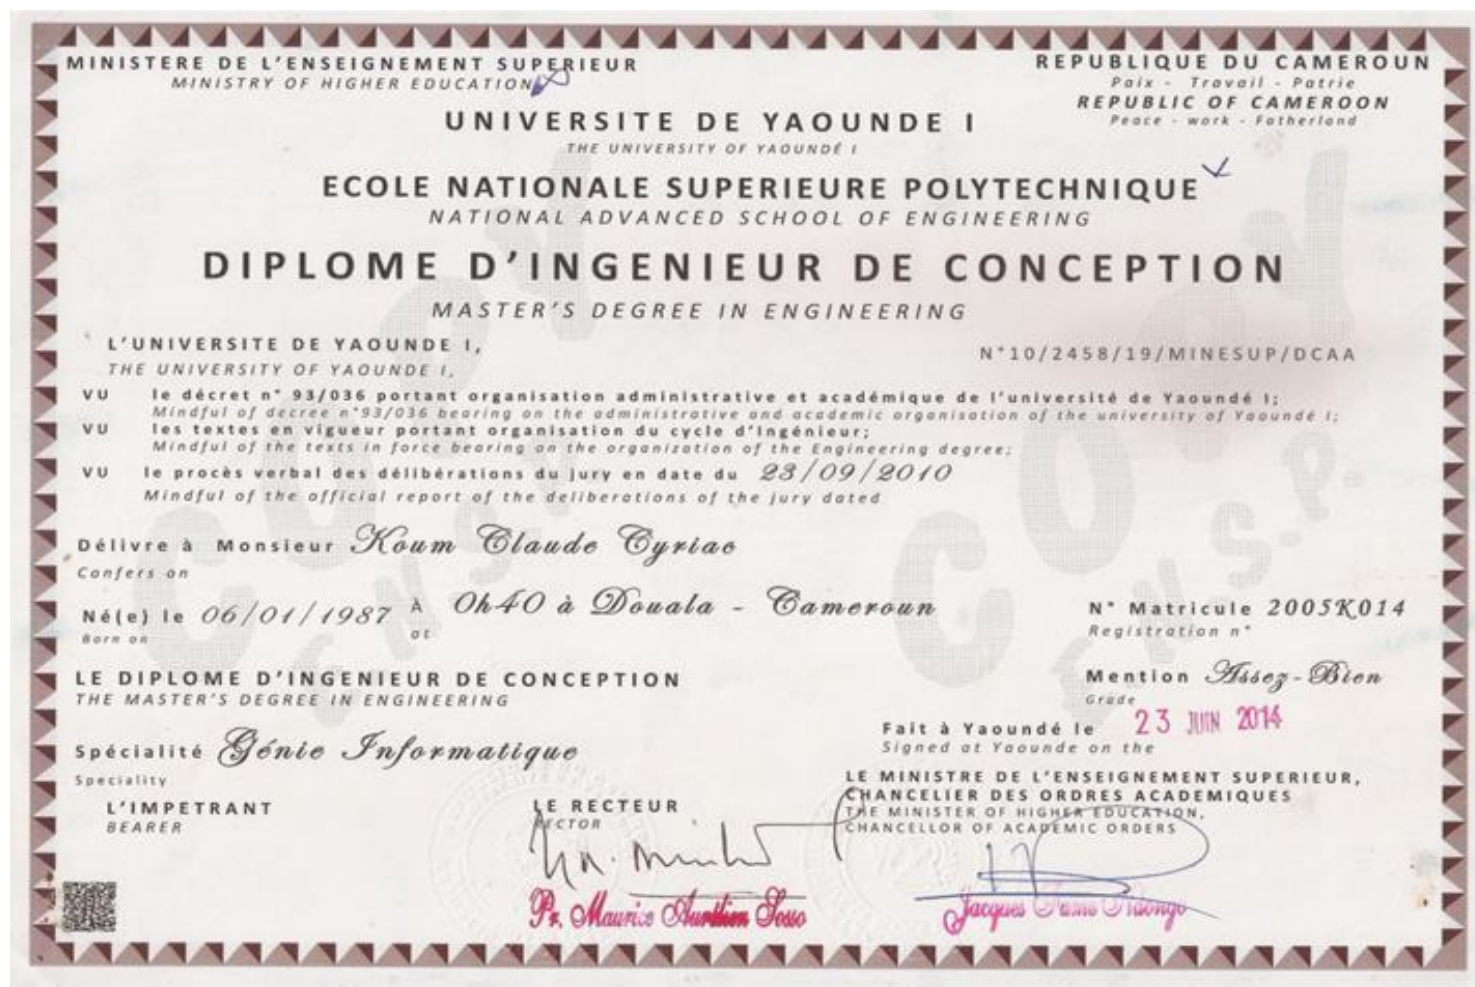

VI.4 CV of the Full Stack Developer N°1

1. **Proposed role in the project:** Full Stack Developer N°1
2. **Family name:** KEMAYOU DJEUMENI Marius Stanislas
3. **Nationality:** Cameroonian
4. **Occupation :** Software Developer
5. **Total experience:** 11 years
6. **Education:**

Institution	Period [Date from – Date to]	Degree(s) or Diploma(s) obtained:
ENSET Douala, Cameroon	2022	Master Degree in Information Systems Project Management
University Technology Institute of Bandjoun, Cameroon	2014	Bachelor of Technology, Computer Science

7. **Language skills:** Indicate competence on a scale of 1 to 5 (1 - excellent; 5 - basic)

Language	Reading	Speaking	Writing
English	1	1	1
French	1	1	1

8. **Other skills:** (e.g., Computer literacy, etc.)

Domain	Tools
Software development	- o Java EE Spring Boot, Hibernate, JSP, SOAP, REST, JSON, XML - o Bash/Shell - o Android, Flutter - o JQuery, Bootstrap, Angular, NodeJS, React, PHP - o Python/Django, C++ - o Docker
Databases	- o MySQL, SQL Server - o Oracle 11GR2, NoSQL, - o HFSQL, PostgreSQL
Methodologies	UML, MERISE, SCRUM
Collaboration/Project Management	Git, Trello
System and Network Administration	- o VSphere ESXI Hypervisor - o Windows server, linux - o AWS S3
Application servers	APACHE, TOMCAT, NGINX
Other tools	NetBeans, Eclipse, IntelliJ, PyCharm, Android Studio, SAP Business One, Sage Saari, MS Office, Navicat, Win'design, Argo UML, MySQL Workbench, SQL server Management Studio, WireShark, Packet tracert, TeamViewer, Google Sketchup, Blender.

9. Relevant Work Experience:

Date from – Date to	Location	Company	Position	Description
January – May 2024	Madagascar	UNDP Madagascar	Business Analyst	Development of an Environment Management Information System • Contribution to requirements gathering and analysis • Platform design • Ensuring customer requirements are met
September 2023 – March 2024	Guinea	UNDP Guinea	Business Analyst	Web platform for the coordination of development partners of the Republic of Guinea • Contribution to requirements gathering and analysis • Platform design • Ensuring customer requirements are met
July 2023 – January 2024	Cameroon	UNICEF Cameroon	Full Stack Developer	• Development of an “m-Hhealth” initiative aiming to strengthen compliance and retention in care of pregnant/breast-feeding women and adolescents living with HIV (ongoing project) • Technology stack: PHP + Symfony, Javascript (React Js, React Native, TypeScript), CSS3 (Bootstrap 4), HTML5
July 2022 – March 2023	Cameroon	UNICEF Cameroun	Full Stack Developer	• Design and implementation of the pilot Management Information System (MIS) for the Unified Social Register in Cameroon • Technology stack: PHP + Symfony, Javascript (React Js, React Native, TypeScript), CSS3 (Bootstrap 4), HTML5
January 2020 – December 2023	Cameroon	MK WBC Lionnel KAMGA Lionnel.kamga@mk-wbc.com	Business Analyst	MKonnected – Networking, consulting and employment support platform • Interfacing with end users to understand their needs so as to draft the most appropriate solution • Requirements gathering and analysis • Ensuring end users expectations are met

November 2020 – January 2022	Cameroon	Oversee Advising Group Hubal PFUMTCHUM hp@myoag.org	Full Stack Developer	Online dashboard including an interactive map, for the visualization of reinforced monitoring-evaluation indicators and conflict-sensitive analysis for AFD in Cameroon - Funded by Agence Française de Développement - Technology stack: PHP + Symfony, React Js, React Native, TypeScript, CSS3 (Bootstrap 4), HTML5
May – August 2021	Cameroon	The Best Group	Lead Developer	Development of the website of SW & Associates Web Site (Tools: WordPress)
Since March 2021	Canada	Novazen	Full Stack Developer	Development of multiple solutions
October 2020 – March 2021	Cameroon/Central African Republic	Oversee Advising Group Hubal PFUMTCHUM hp@myoag.org	Web Developer	“Third Party Monitoring” for 52 projects funded by UNICEF in Central African Republic - Funded by UNICEF - PHP + Symfony, Javascript (React Js, React Native, TypeScript), CSS3 (Bootstrap 4), HTML5
April – July 2019	Canada	AquaPiknik	Web Developer	Design and development of a ship booking platform named AquaPiknik
January 2017 – December 2019	Cameroon	MK WBC	Web Developer	- Development of multiple solutions - MK BID - MK Planning - MK Efficiency Generator - Gaaho Assurance
February – August 2015	Cameroon	FATSOG GROUP SARL	Web Developer	- Development of an inventory management platform - Technology stack: C# (Framework ASP.NET MVC5), CSS3 (Bootstrap 3), JavaScript (Framework Ext.Net MVC), HTML5
January – March 2015	Cameroon	FATSOG GROUP SARL	Web Developer	- Development of a land management platform - Technology stack: Java EE, Maven, CSS3, JSF, HTML5
February – August 2024	Cameroon	IUT of Bandjoun	Web Developer	- ArchiPrize :development of a house design solution - Technology stack: Java EE, CSS3 (Bootstrap 3), JavaScript (Jquery), HTML5

10. Copies of diplomas/transcripts



RÉPUBLIQUE DU CAMEROUN
Pais-Travail-Patrie
MINISTÈRE DE L'ENSEIGNEMENT SUPÉRIEUR
UNIVERSITÉ DE DSHANG

REPUBLIC OF CAMEROON
Peace-Work-Patrieland
MINISTRY OF HIGHER EDUCATION
UNIVERSITY OF DSHANG

INSTITUT UNIVERSITAIRE DE TECHNOLOGIE FOTSO VICTOR
FOTSO VICTOR INSTITUTE OF TECHNOLOGY

BP 134 Douala
Tél: (237) 81922935
Fax: (237) 3014801

CERTIFICAT DE REUSSITE
INDIVIDUAL RESULTS TESTIMONIAL

ID N° **3675_UQS/IUTV/D/DA/DSFPRMP/SFP/SSOP**

Je soussigné: Prof. Fogué Mieland
I, the undersigned:

Directeur de l'INSTITUT UNIVERSITAIRE DE TECHNOLOGIE FOTSO VICTOR, atteste que:
Director of the Fotso Victor Institute of Technology certifies that:

MONSIEUR KEMAYOU DJEUMENI MARIUS STANISLAS

Né(e) le: 06/01/1995
Born on: A: Certifié
At:

a été inscrit(e) dans mon établissement sous le matricule: C36/UDS-IUTV-D1/1
Has been registered under the matricule number:

A obtenu le diplôme: Diplôme Universitaire de Technologie
Has obtained the diploma: Grade: C+/Passable
Grade:

Montre total de crédits capitalisés: 120 CCT3
Number of credits earned:

Vu le Procès verbal du jury N° 0087, date: 27/09/2013
Based on a report of jury

Cursus: Licence
Level degree: Finalité / Voie: Technologique
Finality / Vocation:

Domaine: Sciences et Technologie
Domain of study: Mention: Génie Informatique
Field of study:

Spécialité: /
Specialization: Parcours: Génie Informatique
Course:

Année académique: 2012/2013
Academic year: Option: Informatique de Gestion
Learning option:

Séssion: Septembre 2013
Exam session:

En conséquence, le présent certificat est délivré pour servir et valoir ce que de droit.
The Certificate is issued to serve when and where necessary.

Le Chef de Département
The Head of Department

Le Directeur
The Director

Prof. Fogué Mieland

Il n'est délivré qu'un seul exemplaire de Certificat de réussite.
Only one copy of this testimonial shall be delivered.

Prof. Ouhalla Mieland
Ingénieur Polytechnicien
Maître de Conférences

6 JUIL 2014
10 JUIL 2014

VI.5 CV of the Full Stack Developer N°2

1. **Proposed role in the project:** Full Stack Developer N°2
2. **Family name:** YOUMBI Louis
3. **Nationality:** Cameroonian
4. **Occupation :** Software Developer
5. **Total experience:** 12 years
6. **Education:**

Institution	Period [Date from – Date to]	Degree(s) or Diploma(s) obtained:
University Technology Institute of Douala, Cameroon	2013	Bachelor of Technology, Software Engineering
University Technology Institute of Douala, Cameroon	2012	DUT in Software Engineering

7. **Language skills:** Indicate competence on a scale of 1 to 5 (1 - excellent; 5 - basic)

Language	Reading	Speaking	Writing
English	1	1	1
French	1	1	1

8. **Other skills:** (e.g., Computer literacy, etc.)

Domain	Tools
Web and mobile development	- o PHP(Laravel, Symfony) - o JAVA (EE, SE, ME et FX) - o Javascript (Angular, NodeJs, ReactJs, TypeScript) - o HTML, CSS, Firebase - o Ionic, Android - o Serverless - o Prisma
Databases	- o MySQL, SQL Server - o Oracle 11GR2, NoSQL, - o HFSQL, PostgreSQL
Methodologies	UML, MERISE, SCRUM
Collaboration/Project Management	Scrum, Agile methodologies, Git, Trello
System and Network Administration	- o VSphere ESXI Hypervisor - o Windows Server, Ubuntu Server, CentOS - o AWS S3
Other tools	- o Spring Boot, JPA (Eclipse link, Hibernate), jsp, Icefaces, jsf, Primefaces, Laravel, JasperReports - o Eclipse, Visual studio, Netbeans, Postman, Android studio, Git, Svn, PowerAMC, Dreamweaver, Photoshop, NotePad++ - o JUnit, Swagger, Docker, Maven

9. Relevant Work Experience:

Date from – Date to	Location	Company	Position	Description
January – May 2024	Madagascar	UNDP Madagascar	Business Analyst	Development of an Environment Management Information System • Contribution to requirements gathering and analysis • Platform design • Ensuring customer requirements are met
June 2022 – April 2023	Congo	DIGIPAY CONGO SA	Full Stack Developer	Projects : DigiTransfer (Fund transfer and currency exchange platform) and DigiShopping (Online sales platform for restaurants and supermarkets in Congo Brazzaville) • Requirements gathering and analysis • Writing technical specifications • Interfacing with marketing team to validate new designs • Defining software architectures • Design and development of the application using Java 8 • Upgrade of existing solutions • Deployment of solutions • Bug fixes • Training different user profiles (Operations Manager, Financial Manager, Sales Manager and Product Director) on the solution mastery • Tools : Java, Spring Boot, API REST, Spring security, Slack, Eclipse, Postgres, Agile (Scrum), AWS, Gitlab, Bitbucket, Wildfly, Notepad++, Git, visual studio code, Ionic.

December 2021 – May 2022	Cameroon	Engie Soft (Group of Cameroonian and Swiss experts providing support to businesses)	Full Stack Developer	Project: LE LYS BLEU EDITIONS, Book production and publication management software for our client in France • Market research • Project scheduling and tasks management with Trello • Writing technical specifications of the application • APIs Implementation • User Management (accounts, roles and permissions) • Business domain management: authors, manuscripts, publications and terminations • Tools : Laravel 8, PHP 7.4.9, MySQL, Rest API, Postman, git, VueJs
May 2021 – November 2021	Cameroon	Solutions Communication Sarl	Full Stack Developer	Consultancy services • Writing technical specs of applications • Database design • Websites development and maintenance • PHP, HTML, CSS, Bootstrap, Javascript, visual studio code
Mars 2021 – April 2021	Cameroon	Peers Exchange Cameroon Agency (a money transfer platform)	Backend Developer	Project: Prisma Rest API, Backend rest API for partner management • Apps database design • Writing technical specs • Development of APIs
January 2021 – March 2021	Cameroon	Peers Exchange Cameroon Agency (a money transfer platform)	Backend Developer	Project: Prisma Rest API, Backend rest API for chatbot management • Apps database design • Writing technical specs • Development of APIs • Backend deployment for chatbot management • Tools : Java, Spring Boot, NodeJs, Express, git, Serverless, MongoDB, Rest API, postman

August 2020 – December 2020	Cameroon	Peers Exchange Cameroon Agency (a money transfer platform)	Full Stack Developer	Project: Peex-advans, a transaction management system • Apps database design • Writing technical specs • APIs upgrade • Web interface upgrade • Tools: Java, AngularJs, Ruby on rails, PostgreSQL, Python, Django Tools: Java, AngularJs, Ruby on rails, postgresSQL, Python, Django
March 2020 – July 2020	Cameroon	Peers Exchange Cameroon Agency (a money transfer platform)	Full Stack Developer	Project: DIGIPAY, Transaction management platform for our partner in Congo • Apps database design • Writing technical specs • Development of web and mobile interfaces • Deployment of DIGIPAY web and mobile apps • Tools : Laravel, Ionic, html, Bootstrap, Git, MySQL, Rest API, postman.
October 2017 – March 2020	Cameroon	Gibraltech Sarl (a software development company)	Web and mobile Developer	Project: Kloonos, a social market platform • Apps database design • Writing technical specs • Review of web and mobile interfaces • Data consumption through API • Server administration • Deployment of mobile apps on Google Play • Angular, html, Javascript, CSS, Java, rest-API, NodeJs, Ionic, Symfony, Visual studio, PowerAMC, MySQL, Firebase, Rest API, postman

August 2016 – May 2017	Cameroon	NG CONSEIL (a software development company)	Web Developer	Project: KWANZA, electronic ticketing management platform for CAMRAIL • Apps database design • Writing technical specs • Development of web and mobile interfaces • Generation of travel tickets in A6 format with unique QR code • Data consumption via API (PHP) • Tools : Javascript, html, Php, android studio, Notepad++, PowerAMC, MySQL, Rest API.
December 2014 – July 2016	Cameroon	SIM-e	Web and mobile Developer	Design and development of enterprise software • Apps database design • Writing technical specs • Development of web interfaces • Development of mobile interfaces (Native: Android studio) • Tools: JavaEE, JSF, Primefaces, android studio, Visual studio, Eclipse, PowerAMC, MySQL, webServices • Key achievements : ◦ Design and development of a web and mobile application for online sales of haute couture clothing (West Africa: e-yamo) ◦ Design and development of a product distribution management application (e-distribution) ◦ Design and development of a production management application (e-agro) ◦ Creation of the Sim-e presentation website

Since September 2013	Cameroon	KOOLO Sarl	Software Developer & Community Manager (Freelance)	Activities • Participate in the design of the application database • Writing of technical specifications of applications • Development of company websites • Development of company mobile applications • Server administration (Local and online) • Management of the project team and task planning • Coordination of the creation of maps with the computer graphics software (Gimp 2.0) • Training of trainees Tools : Javascript, JQuery, PHP, html, css, Bootstrap, Visual studio, PowerAMC, MySQL, Rest API, Laravel Key achievements • Design and creation of a website and a mobile application for online sales (https://ekaoloshop.cm on Google Play Store: ekoolo) • Design and creation of an advertisement website (https://kaolo.cm)
August 2013 – December 2013	Cameroon	Information Systems Department, University of Douala	Analyst / Developer	SYSTHAG • Drafting of technical specification files for applications • Analysis and design of the system to be set up • Analysis, design and production of an application allowing jury members to more easily assign students newly pre-registered at the University of Douala to the chosen courses. • Production, development of APIs and backend using javaFX, website in JSF • Tools : JavaEE, JSF, Primefaces, JavaFX, Jasper Report, PostgreSQL

10. Copies of diplomas/transcripts

REPUBLICUE DU CAMEROUN
Paix - Travail - Patrie
MINISTRE DE L'ENSEIGNEMENT SUPERIEUR
UNIVERSITE DE DOUALA

REPUBLIC OF CAMEROON
Peace - Work - Fatherland
MINISTRY OF HIGHER EDUCATION
THE UNIVERSITY OF DOUALA

*Copie Certifiée Conforme à l'Original
présenté et Rendu par nos Soins*

Doouals Le

INSTITUT UNIVERSITAIRE DE TECHNOLOGIE
THE UNIVERSITY INSTITUTE OF TECHNOLOGY
BP.: 3698 Douala - Tel: 33407485 - Fax: 33402482 - URL: www.iut.u-douala.cm

ATTESTATION DE REUSSITE
ATTESTATION

N° 0694GL/IUT/DA/DEI/CD/SCO/SC-ILABD

Je soussigné, Directeur de l'Institut Universitaire de Technologie de l'Université de Douala, atteste que :
I, the undersigned, Director of the University Institute of Technology of the University of Douala, certify that:

M./Mlle : **YOUUMBI Louis** de Sexe : **M**
Mr./Mrs: Sex:

Né(e) le : **01/02/1987** A : **Mté de Penja** Inscrit(e) sous le matricule N° : **10A245**
Born on: At: Registered under registration n°:

A obtenu(e) le diplôme **LICENCE DE TECHNOLOGIE**
Has obtained the diploma:

Filière : **Génie Informatique**
Field of study:

Option : **Génie Logiciel**
Speciality:

Session de : **Décembre 2013** Mention : **Assez-Bien**
Session: Grade:

En foi de quoi la présente attestation lui est délivrée pour servir et valoir ce qu'il lui appartient.
In witness whereof, this attestation is issued to him/her for the purpose for which it is intended.

DOUALA

Le Titulaire
The Holder

Le Directeur
The Director

20 FEB 2016

*Il n'est délivré qu'une seule attestation, le titulaire peut en faire autant de copies certifiées conformes.
This attestation is issued only once, the holder may make as many certified true copies as necessary.*

VI.6 CV of the Test Engineer

Proposed role in the project: Test Engineer

1. **Names:** KAMGA NGANGUE Francis
2. **Nationality:** Cameroonian
3. **Occupation:** Software Engineer
4. **Education:**

Institution	Period [Date from – Date to]	Degree(s) or Diploma(s) obtained:
National Advanced School of Engineering of Douala, Cameroon	2020	Master of Engineering, Computer Engineering
University Technology Institute, Douala, Cameroon	2017	University Technology Diploma, Software Engineering

5. **Language skills:** Indicate competence on a scale of 1 to 5 (1 - excellent; 5 - basic)

Language	Reading	Speaking	Writing
English	1	1	1
French	1	1	1

6. **Skills:** (e.g., Computer literacy, etc.)
 - Frontend : VueJS, ReactJs, JavaScript, HTML/CSS, Bootstrap 3&4
 - Backend : Symfony, Laravel, PHP, Python, Flask, Java
 - Databases: MySQL, PostgreSQL, Firebase, NoSQL
 - CMS: Wordpress
 - Mobile: Kotlin, React Native
 - Other: API Development


7. Relevant Work Experience

Date from – Date to	Location	Company	Position	Description
Since July 2023	Cameroon	MK WBC Client : UNICEF	Full Stack Developer	Development of an "m-Hhealth" initiative aiming to strengthen compliance and retention in care of pregnant/breast-feeding women and adolescents living with HIV (ongoing project)
Since December 2023	France	Accor	Software Engineer (Consultant)	- Within the Digital & Business Factory, the Value & Delivery Excellence team is responsible for improving the Delivery of the Digital & Business Factory's Features Teams. - To meet the team's needs in terms of tools, I'm in charge of the design and development of mostly Cloud AWS & NodeJs Solution Tools.
March 2023 – November 2023	France	Docaposte	Senior Developer (Consultant)	As part of a team of developers and a scrum-master. Our objective was to design a multi-micro-service application to manage a loyalty program. This involved collecting, filtering and transforming data from multiple sources. Mission: Senior JavaScript / TypeScript Developer Collection, filtering and transformation of over 8 million pieces of data for a loyalty program application. My responsibilities for this project were as follows: - Design and implementation of data collection processes from various sources. - Implementation of filtering mechanisms to select relevant data according to specified criteria. - Transformation of raw data using appropriate techniques and tools to make it usable. - Manage and optimize performance when processing large quantities of data. - Collaborate with business teams to understand data transformation needs and requirements. - Creation of a micro-service to send transformed data to the loyalty program webservice. - Implementation of unit and validation tests to guarantee the quality of the transformed data. - Documentation of data collection and transformation processes. - Monitoring and maintenance of data flows to ensure continuous, reliable operation of the system.

September 2022 – March 2023	France	Engie	Full Stack Developer – (Consultant)	As part of a technical team within the ENGIE SA group, responsible for the design, development and production of internal administration tools, as well as data processing. The main aim of these tools is to bring together the management or management information of the entire Group and its entities. Mission : Full Stack NodeJs/ReactJs Developer - Design and development of software architectures - Development of a Web API backend using Node.js, AzureFunction and ArangoDB to provide real-time data flows to internal and external applications. - Configuration of development, pre-production and production environments with AWS Lambda/Serverless - Use DynamoDB/ArangoDB for data storage - Front-end development using Typescript, Angular ,React.js, Redux, Redux-Saga - Implement unit testing with Jest/Vitest - Use GIT (AzureDepot) to manage code versions - Use PowerShell to create administration scripts (accounts, distribution list, licenses, etc.) - Create CI/CD pipelines using AzurePipeline
February 2019 – June 2022	Cameroon	MK WBC	Full Stack Developer	- Development of a Web API backend using Node.js, Typescript, loopback.js and JWT for user authentication - Development of a Web API backend in PHP with Symfony - Use of MySQL for data storage and implementation of SQL search queries for all kinds of filters - Development of the front-end using Typescript, React.js and Redux, integrating microservices provided by a Node.js API layer based on Express. - Implementing automated testing with Jest, including unit testing and API testing to ensure code quality and reliability. - Use GIT for code version management, create CI/CD pipelines using GitLab Projects: – https://mkonnected.com – https://myoagexpert.com – https://gaahoimmo.com – Gaaho Assurance
September 2017 – January 2019	Cameroon	Planet-Trade	Web Developer	▪ Development of an Inventory Management application
July – August 2017	Cameroon	My Nearest Places / Heylo	Software Developer	▪ Development of a mobile application to locate nearest commodities

VII. ANNEXES

Annexe 1 : A preliminary mockup for certain pages of the NetHope website

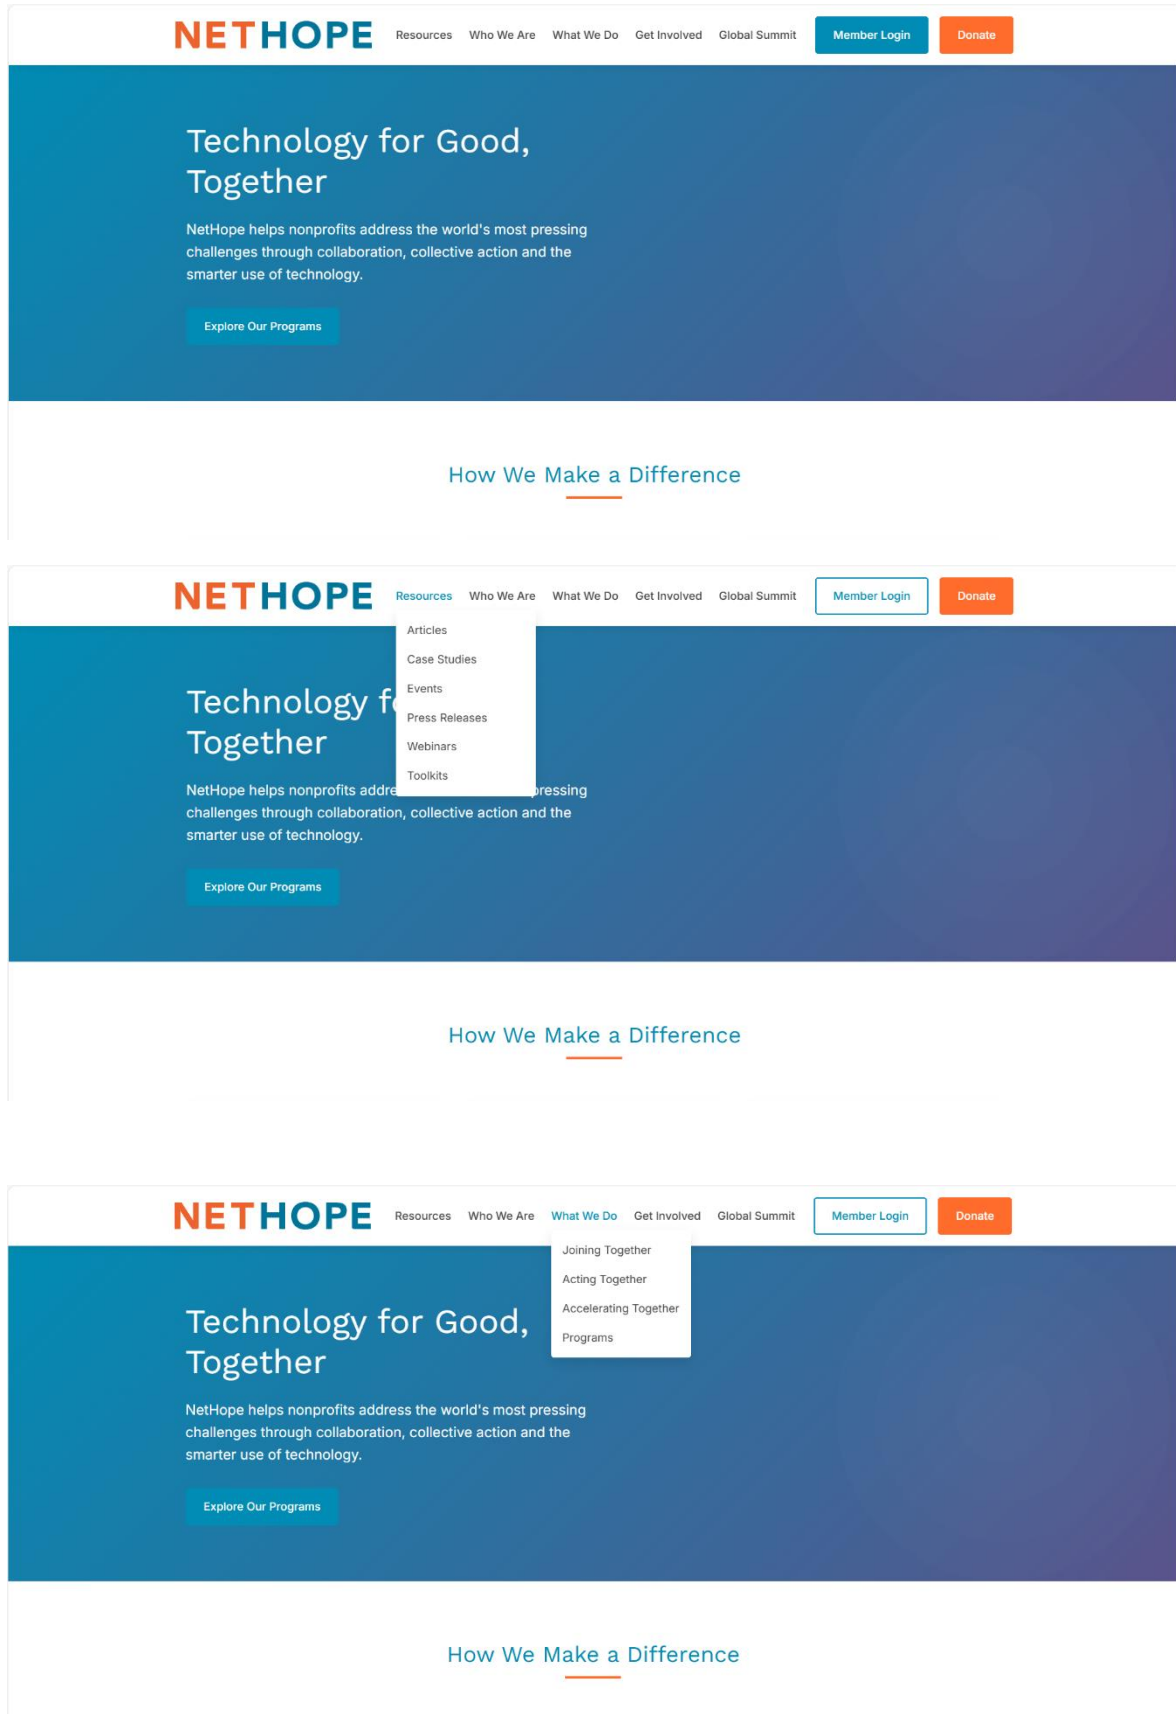


[Resources](#)
[Who We Are](#)
[What We Do](#)
[Get Involved](#)
[Global Summit](#)
[Member Login](#)
[Donate](#)

How We Make a Difference



Joining Together

Our community brings together nonprofits to collaborate, share experiences, and discover new solutions to common challenges.

[Learn More →](#)



Acting Together

We run programs with and for our Members, providing essential services, connectivity, and advancing technology usage in the nonprofit sector.

[Learn More →](#)



Accelerating Together

Our Center for the Digital Nonprofit accelerates digital transformation across the sector, helping organizations harness technology's potential.

[Learn More →](#)


[Resources](#)
[Who We Are](#)
[What We Do](#)
[Get Involved](#)
[Global Summit](#)
[Member Login](#)
[Donate](#)

Our Collective Impact

60+
Member Organizations

100+
Countries Reached


20+
Years of Impact

\$500M+
Technology Resources

Transforming Lives Through Technology

NetHope and its Members are at the forefront of applying innovative approaches to delivering aid and development assistance. By leveraging technology, we can amplify our impact and reach more communities in need.

From emergency response to long-term development programs, our collaborative approach ensures that technology solutions are effectively applied to address the world's most pressing challenges.


[View Case Studies](#)


[Resources](#)
[Who We Are](#)
[What We Do](#)
[Get Involved](#)
[Global Summit](#)
[Member Login](#)
[Donate](#)

Our Programs

[Connectivity & Infrastructure](#)
[Data & Information Management](#)
[Digital Protection & Cybersecurity](#)
[Digital Skills & Inclusion](#)
[Emerg](#)

Join Us in Making a Difference

Together, we can leverage technology to address the world's most pressing challenges and create lasting positive change.

[Become a Member](#)
[Partner With Us](#)

NETHOPE[Resources](#)[Who We Are](#)[What We Do](#)[Get Involved](#)[Global Summit](#)[Member Login](#)[Donate](#)

Latest Resources



Case Study

fAIR, Humanitarian
OpenStreetMap Team (HOT)

Exploring how AI-powered mapping is transforming humanitarian response in crisis situations.

🕒 March 15, 2025



Article

Bridging the New Digital Divides

Global leaders agree, digital is essential if we are to solve the world's most pressing challenges.

🕒 February 28, 2025



Webinar

2024-2030 NetHope Strategic Plan

Join us for a comprehensive overview of our six-year strategic plan and vision for the future.

🕒 January 20, 2025


[View All Resources](#)

NETHOPE[Resources](#)[Who We Are](#)[What We Do](#)[Get Involved](#)[Global Summit](#)[Member Login](#)[Donate](#)

Transforming Lives Through Technology

NetHope and its Members are at the forefront of applying innovative approaches to delivering aid and development assistance. By leveraging technology, we can amplify our impact and reach more communities in need.

From emergency response to long-term development programs, our collaborative approach ensures that technology solutions are effectively applied to address the world's most pressing challenges.



[View Case Studies](#)

NETHOPE[Resources](#)[Who We Are](#)[What We Do](#)[Get Involved](#)[Global Summit](#)[Member Login](#)[Donate](#)

Our Global Community

NetHope is a consortium of nearly 60 leading global nonprofit organizations working together to solve humanitarian, development, and conservation challenges.

Member 1

Member 2

Member 3

Member 4

Member 5

Member 6

Member 7

Member 8

[View All Members](#)


[Resources](#)
[Who We Are](#)
[What We Do](#)
[Get Involved](#)
[Global Summit](#)
[Member Login](#)
[Donate](#)

Stay Connected

Subscribe to our newsletter to stay updated on the latest news, events, and resources from NetHope and our community.

Name

Email

Organization (Optional)



NetHope enables our nonprofit Members to better serve their communities by leveraging technology through collaboration, innovation, and collective impact.

Resources

- Articles
- Case Studies
- Events
- Press Releases

About

- Who We Are
- Our Members
- Our Partners
- Careers

Get Involved

- Become a Member
- Partner With Us
- Donate
- Contact


[Resources](#)
[Who We Are](#)
[What We Do](#)
[Get Involved](#)
[Global Summit](#)
[Member Login](#)
[Donate](#)

Subscribe to our newsletter to stay updated on the latest news, events, and resources from NetHope and our community.

Organization (Optional)



NetHope enables our nonprofit Members to better serve their communities by leveraging technology through collaboration, innovation, and collective impact.







Resources

- Articles
- Case Studies
- Events
- Press Releases
- Webinars
- Toolkits

About

- Who We Are
- Our Members
- Our Partners
- Careers
- NetHope at 20

Get Involved

- Become a Member
- Partner With Us
- Donate
- Contact
- Member Login

© 2025 NetHope, Inc. All rights reserved.

[Privacy Policy](#)
[Terms of Use](#)
[Sitemap](#)
